





CLAIM SUMMARY

Contract No :

1. C&A. 1608.02/STP1 - 051

| Type of Work                 | Unit  | SPK Vol    | January 2011 Claim | February Claim | Total Claimed (Jan - Feb 2011) | %       |
|------------------------------|-------|------------|--------------------|----------------|--------------------------------|---------|
| <b>Excavator</b>             |       |            |                    |                |                                |         |
| Stacking Excavator           | Ha    | 90.00      | -                  | -              | -                              | 0.00%   |
| Main Drain 3,6x2,4x1,8       | Meter | 5,000.00   | 4,807.00           | 193.00         | 5,000.00                       | 100.00% |
| Main Drain 2,4x1,8x1,2       | Meter | 18,000.00  | 4,997.00           | -              | 4,997.00                       | 27.76%  |
| Collection Drain 1,8x1,2x0,9 | Meter | 113,000.00 | 67,949.00          | 9,333.00       | 77,282.00                      | 68.39%  |
| Infield Drain 1,2x0,9x0,6    | Meter | 396,342.00 | 26,988.00          | 37,997.00      | 64,985.00                      | 16.40%  |
| <b>Underbrushing (Imas)</b>  |       |            |                    |                |                                |         |
| Underbrushing (Imas)         | Ha    | 90.00      | -                  | -              | -                              | 0.00%   |

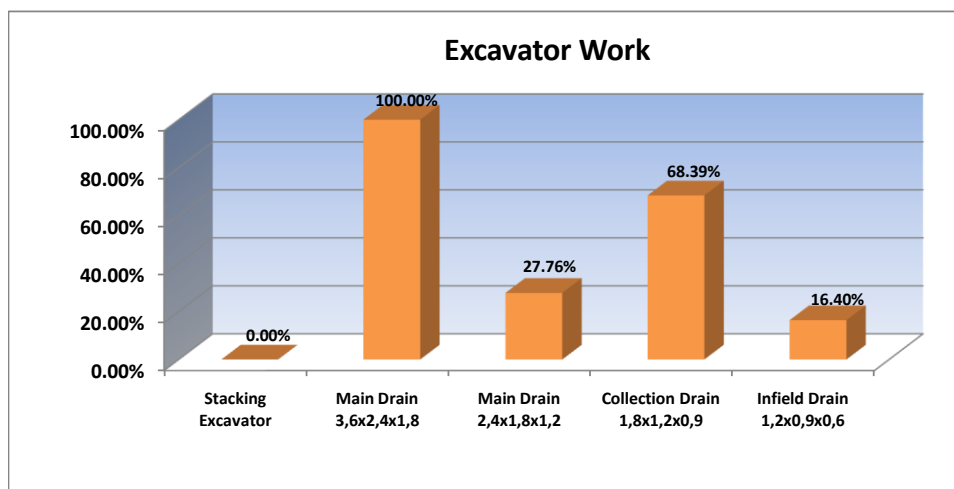




**CLAIM SUMMARY**


**Chart & Detail Per Month**

| Type of Work       | SPK Vol ( Ha ) | Progress | %     |
|--------------------|----------------|----------|-------|
| Stacking Excavator | 90.00          | -        | 0.00% |

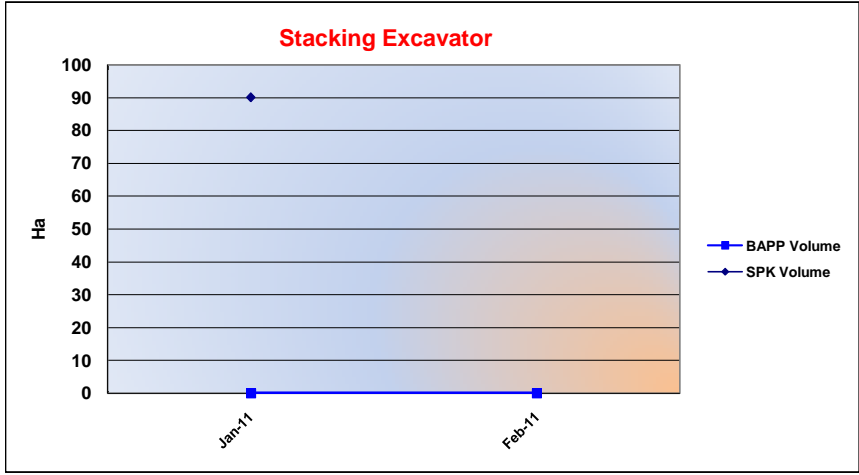


| Month        | Monthly Progress | Accumulated |
|--------------|------------------|-------------|
| Jan-11       | -                | -           |
| Feb-11       | -                | -           |
| <b>Total</b> | <b>-</b>         | <b>-</b>    |

| Type of Work           | SPK Vol (Meter) | Progress | %       |
|------------------------|-----------------|----------|---------|
| Main Drain 3,6x2,4x1,8 | 5,000.00        | 5,000.00 | 100.00% |

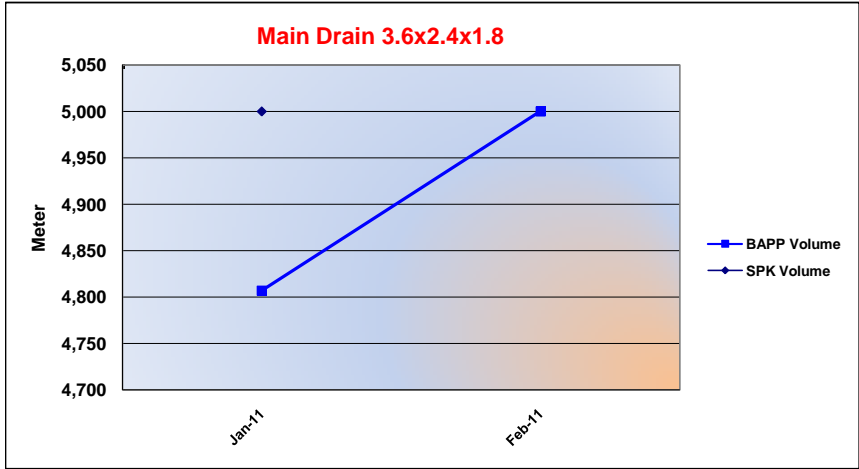

| Month        | Monthly Progress | Accumulated |
|--------------|------------------|-------------|
| Jan-11       | 4,807.00         | 4,807.00    |
| Feb-11       | 193.00           | 5,000.00    |
| <b>Total</b> | <b>5,000.00</b>  |             |

| Type of Work           | SPK Vol (Meter) | Progress | %      |
|------------------------|-----------------|----------|--------|
| Main Drain 2,4x1,8x1,2 | 18,000.00       | 4,997.00 | 27.76% |

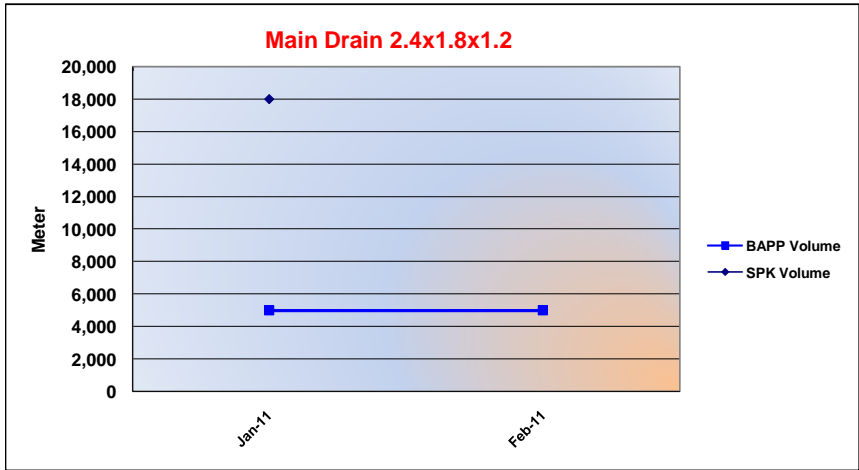


| Month        | Monthly Progress | Accumulated |
|--------------|------------------|-------------|
| Jan-11       | 4,997.00         | 4,997.00    |
| Feb-11       | -                | 4,997.00    |
| <b>Total</b> | <b>4,997.00</b>  |             |



# PT. SARANA TITIAN PERMATA


## CLAIM SUMMARY

| Type of Work                 | SPK Vol (Meter) | Progress  | %      |
|------------------------------|-----------------|-----------|--------|
| Collection Drain 1,8x1,2x0,9 | 113,000.00      | 77,282.00 | 68.39% |

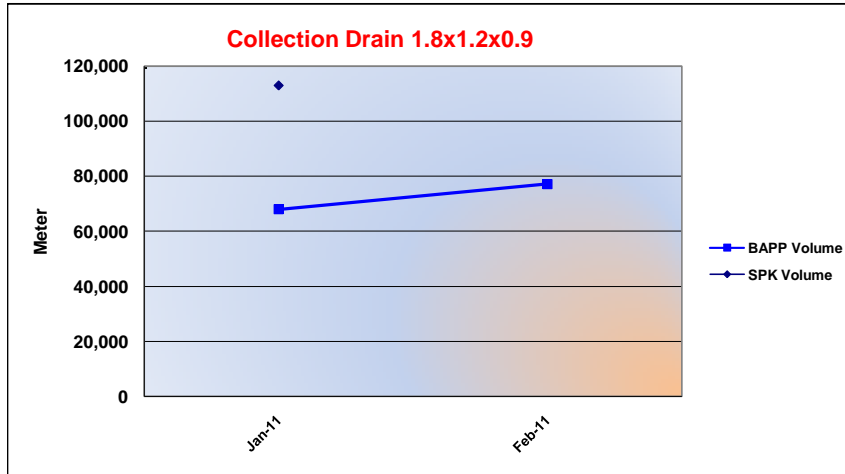


| Month        | Monthly Progress | Accumulated |
|--------------|------------------|-------------|
| Jan-11       | 67,949.00        | 67,949.00   |
| Feb-11       | 9,333.00         | 77,282.00   |
| <b>Total</b> | <b>77,282.00</b> |             |

| Type of Work              | SPK Vol (Meter) | Progress  | %      |
|---------------------------|-----------------|-----------|--------|
| Infield Drain 1,2x0,9x0,6 | 396,342.00      | 64,985.00 | 16.40% |

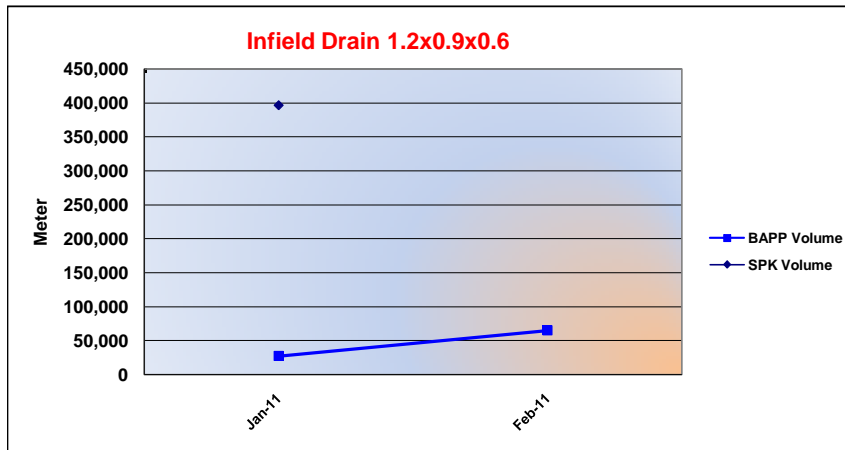

| Month        | Monthly Progress | Accumulated |
|--------------|------------------|-------------|
| Jan-11       | 26,988.00        | 26,988.00   |
| Feb-11       | 37,997.00        | 64,985.00   |
| <b>Total</b> | <b>64,985.00</b> |             |

| Type of Work         | SPK Vol ( Ha ) | Progress | %     |
|----------------------|----------------|----------|-------|
| Underbrushing (Imas) | 90.00          | -        | 0.00% |

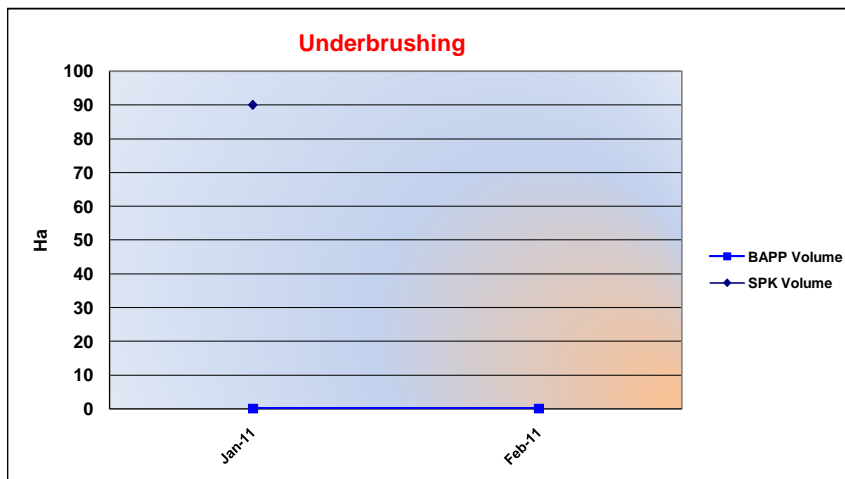

| Month        | Monthly Progress | Accumulated |
|--------------|------------------|-------------|
| Jan-11       | -                | -           |
| Feb-11       | -                | -           |
| <b>Total</b> | <b>-</b>         |             |
