



PT. SARANA TITIAN PERMATA

CLAIM SUMMARY

Contract No :

1. C&A. 1608.02/STP2 - 052

Type of Work	Unit	SPK Vol	Jan - Apr 2011 Claim	May Claim	Total Claimed (Jan - May 2011)	%
Excavator						
Main Drain 3,6x2,4x1,8	Meter	8,000.00	1,209.00	-	1,209.00	15.11%
Main Drain 2,4x1,8x1,2	Meter	-	-	-	-	-
Collection Drain 1,8x1,2x0,9	Meter	75,000.00	7,153.00	350.00	7,503.00	10.00%
Infield Drain 1,2x0,9x0,6	Meter	1,013,630.00	491,764.00	165,201.00	656,965.00	64.81%


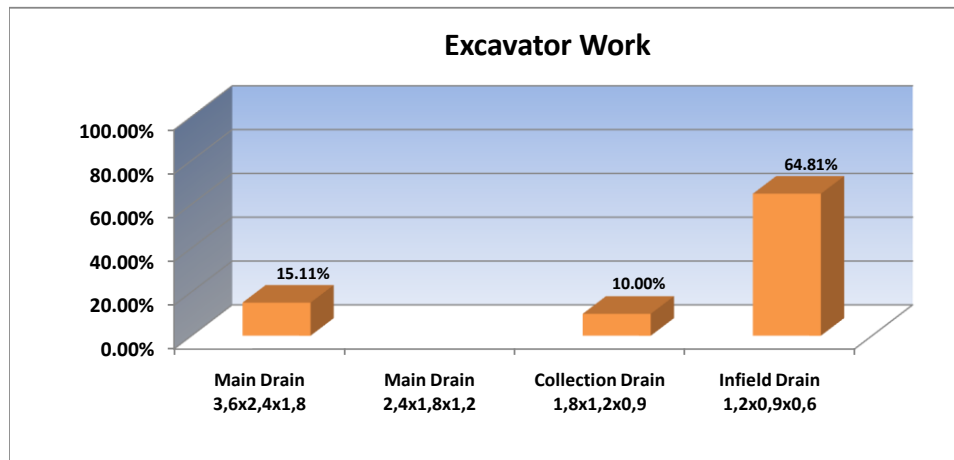


Chart & Detail Per Month

Type of Work	SPK Vol (Meter)	Progress	%
Main Drain 3,6x2,4x1,8	8,000.00	1,209.00	15.11%




Month	Monthly Progress	Accumulated
Jan-11	-	-
Feb-11	-	-
Mar-11	1,209.00	1,209.00
Apr-11	-	1,209.00
May-11	-	1,209.00
Total	1,209.00	

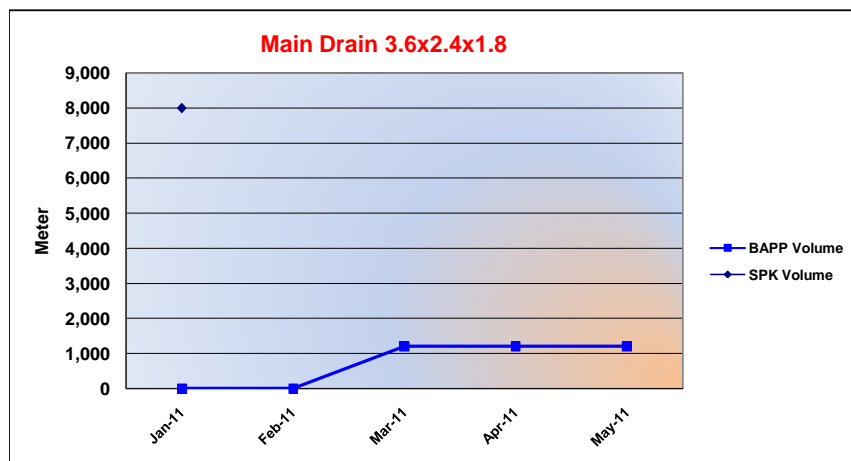


CLAIM SUMMARY

Type of Work	SPK Vol (Meter)	Progress	%
Main Drain 2,4x1,8x1,2	-	-	0.00%

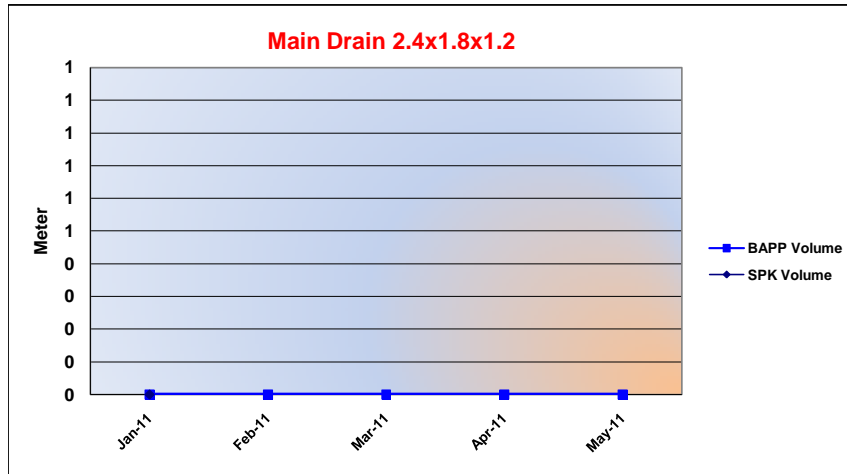


Month	Monthly Progress	Accumulated
Jan-11	-	-
Feb-11	-	-
Mar-11	-	-
Apr-11	-	-
May-11	-	-
Total	-	-

Type of Work	SPK Vol (Meter)	Progress	%
Collection Drain 1,8x1,2x0,9	75,000.00	7,503.00	10.00%

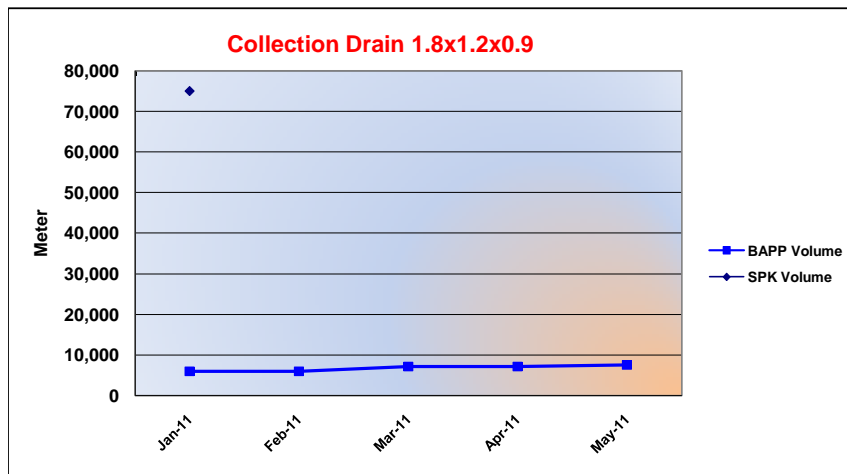

Month	Monthly Progress	Accumulated
Jan-11	5,947.00	5,947.00
Feb-11	-	5,947.00
Mar-11	1,206.00	7,153.00
Apr-11	-	7,153.00
May-11	350.00	7,503.00
Total	7,503.00	

Type of Work	SPK Vol (Meter)	Progress	%
Infield Drain 1,2x0,9x0,6	1,013,630.00	656,965.00	64.81%

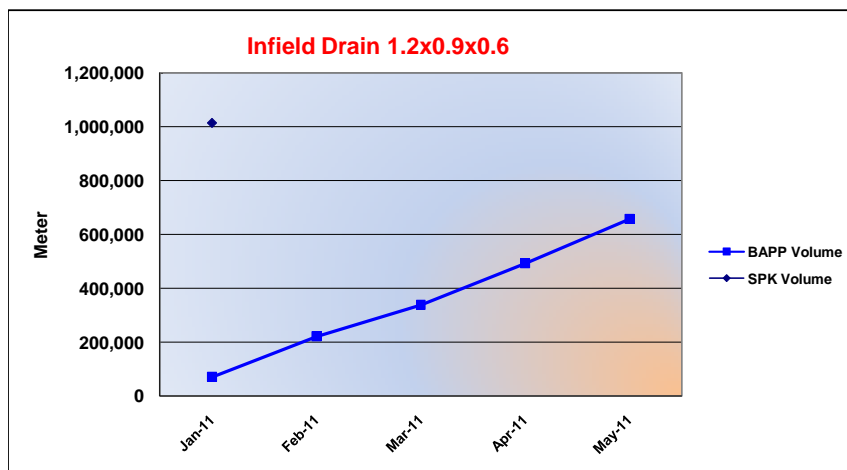

Month	Monthly Progress	Accumulated
Jan-11	70,669.00	70,669.00
Feb-11	149,954.00	220,623.00
Mar-11	117,166.00	337,789.00
Apr-11	153,975.00	491,764.00
May-11	165,201.00	656,965.00
Total	656,965.00	
