



CLAIM SUMMARY

Contract No :

1. C&A. 1608.02/STP3 - 053

Type of Work	Unit	SPK Vol	Jan - Aug 2011 Claim	September Claim	Total Claimed (Jan - Sep 2011)	%
Excavator						
Main Drain 3,6x2,4x1,8	Meter	-	-	-	-	-
Main Drain 2,4x1,8x1,2	Meter	-	-	-	-	-
Collection Drain 1,8x1,2x0,9	Meter	42,780.00	-	-	-	0.00%
Infield Drain 1,2x0,9x0,6	Meter	964,166.00	921,691.00	-	921,691.00	95.59%


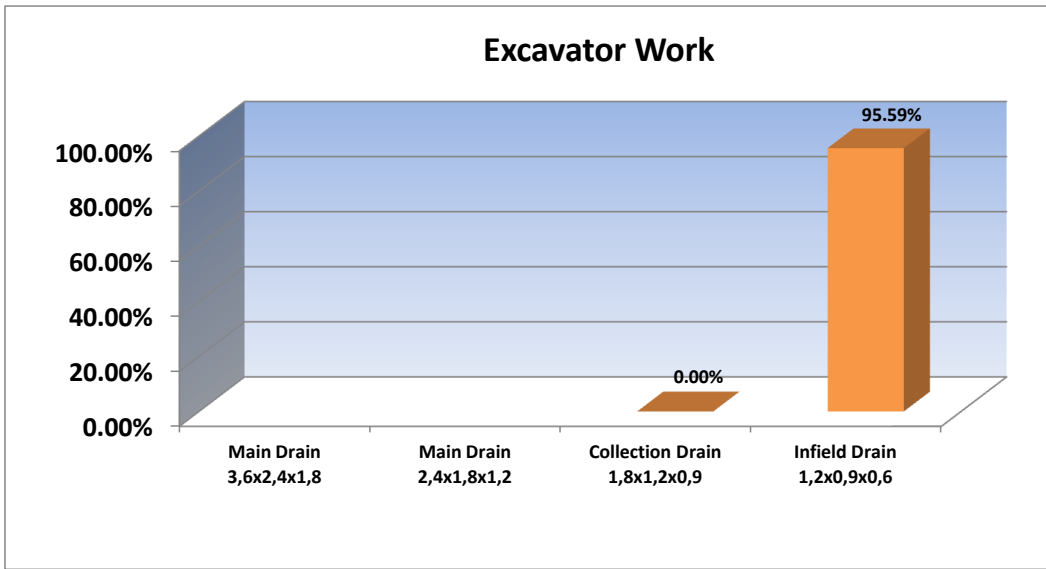


Chart & Detail Per Month

Type of Work	SPK Vol (Meter)	Progress	%
Main Drain 3,6x2,4x1,8	-	-	0.00%




Month	Monthly Progress	Accumulated
Jan-11	-	-
Feb-11	-	-
Mar-11	-	-
Apr-11	-	-
May-11	-	-
Jun-11	-	-
Jul-11	-	-
Aug-11	-	-
Sep-11	-	-
Total	-	-

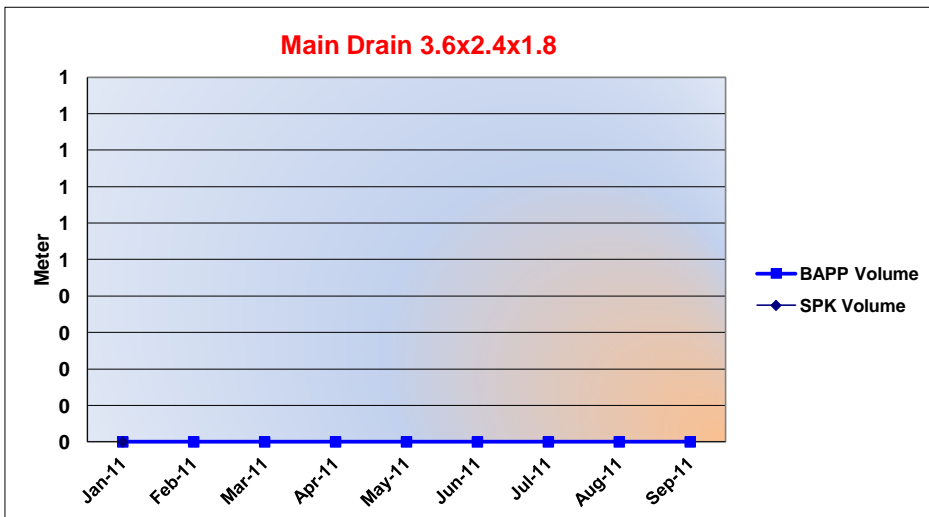


CLAIM SUMMARY

Type of Work	SPK Vol (Meter)	Progress	%
Main Drain 2,4x1,8x1,2	-	-	0.00%

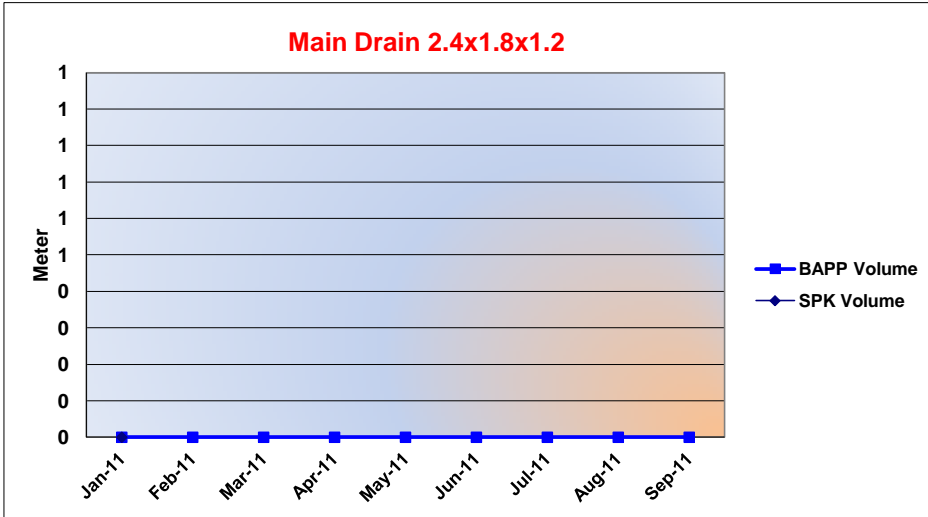


Month	Monthly Progress	Accumulated
Jan-11	-	-
Feb-11	-	-
Mar-11	-	-
Apr-11	-	-
May-11	-	-
Jun-11	-	-
Jul-11	-	-
Aug-11	-	-
Sep-11	-	-
Total	-	-

Type of Work	SPK Vol (Meter)	Progress	%
Collection Drain 1,8x1,2x0,9	42,780.00	-	0.00%

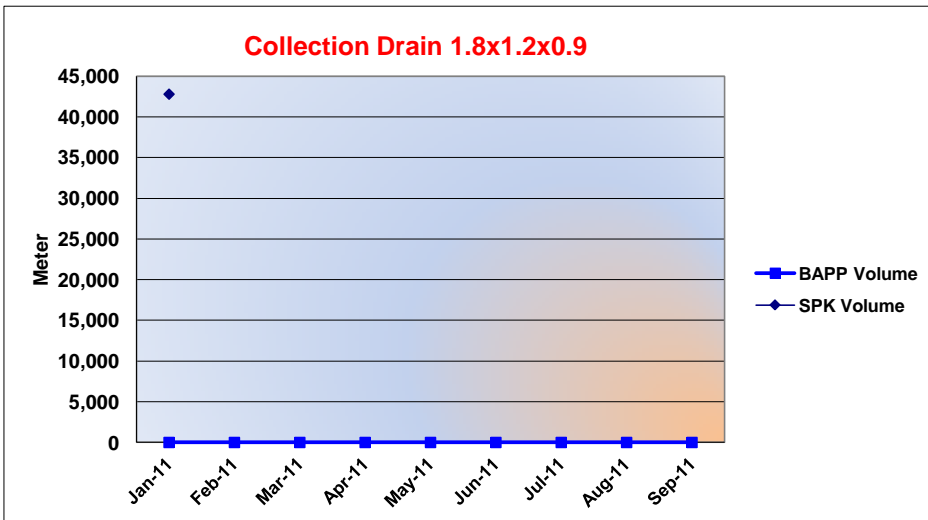

Month	Monthly Progress	Accumulated
Jan-11	-	-
Feb-11	-	-
Mar-11	-	-
Apr-11	-	-
May-11	-	-
Jun-11	-	-
Jul-11	-	-
Aug-11	-	-
Sep-11	-	-
Total	-	-

Type of Work	SPK Vol (Meter)	Progress	%
Infield Drain 1,2x0,9x0,6	964,166.00	921,691.00	95.59%

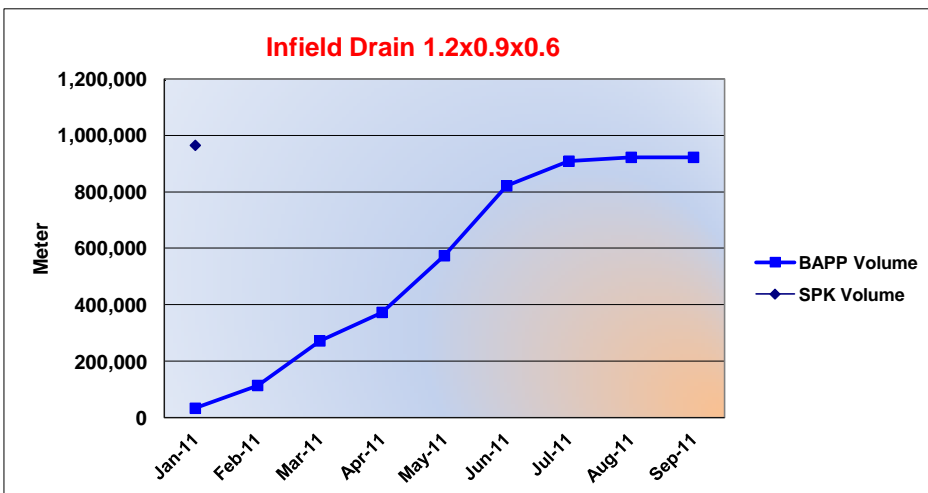

Month	Monthly Progress	Accumulated
Jan-11	33,849.00	33,849.00
Feb-11	80,743.00	114,592.00
Mar-11	157,726.00	272,318.00
Apr-11	100,747.00	373,065.00
May-11	200,571.00	573,636.00
Jun-11	247,403.00	821,039.00
Jul-11	86,973.00	908,012.00
Aug-11	13,679.00	921,691.00
Sep-11	-	921,691.00
Total	921,691.00	921,691.00
