





PT. KARUNIA KENCANA PERMAISEJATI

CLAIM SUMMARY KKP III

Contract No :
C&A. 1608.02/KKP3 - 070

| Type of Work | Unit | SPK Vol | Feb - May 2011 Claim | June Claim | Total Claimed (Feb - Jun 2011) | % |
|-------------------------------------|-------|-----------|----------------------|------------|--------------------------------|--------|
| Bulldozer | | | | | | |
| Stacking Bulldozer - Low Vegetation | Ha | 368.20 | - | - | - | 0.00% |
| Excavator | | | | | | |
| Stacking Excavator | Ha | 157.80 | 54.02 | 9.48 | 63.50 | 40.24% |
| Road Formation 8 M | Meter | 5,260.00 | 689.00 | 170.00 | 859.00 | 16.33% |
| Road Formation 6 M | Meter | 26,300.00 | 1,098.00 | 796.00 | 1,894.00 | 7.20% |
| Main Drain 2,4x1,8x1,2 | Meter | 2,630.00 | - | - | - | 0.00% |
| Collection Drain 1,8x1,2x0,9 | Meter | 13,150.00 | 3,617.00 | 2,191.00 | 5,808.00 | 44.17% |
| Infield Drain 1,2x0,9x0,6 | Meter | 81,512.00 | 4,298.00 | 15,666.00 | 19,964.00 | 24.49% |
| Underbrushing (Imas) | Ha | 526.00 | 54.02 | 9.48 | 63.50 | 12.07% |
| Felling (Tumbang) | Ha | 526.00 | 54.02 | 9.48 | 63.50 | 12.07% |

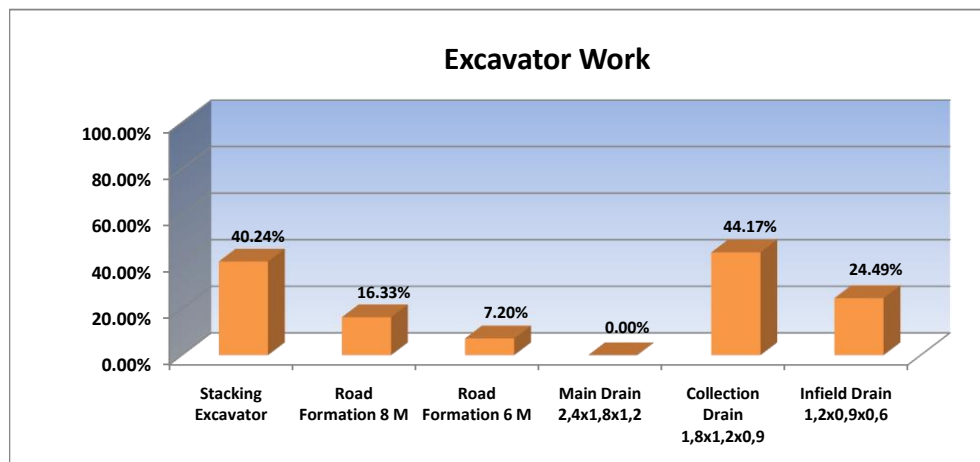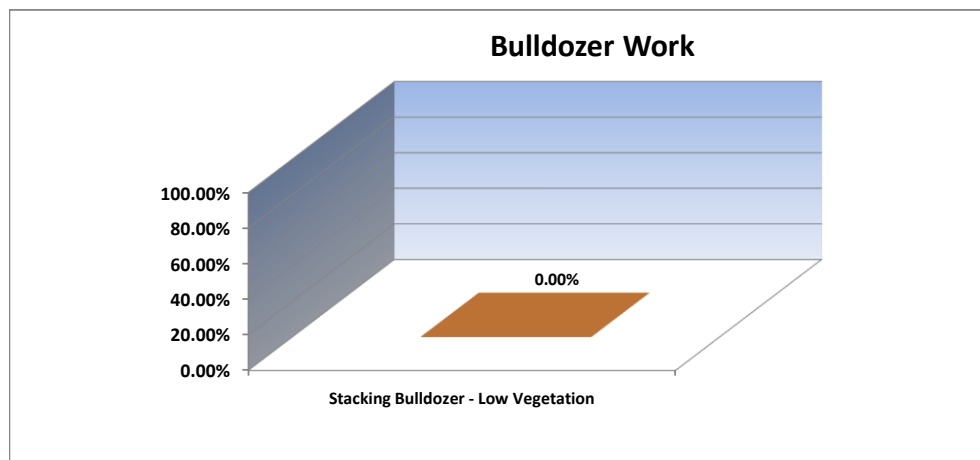



CLAIM SUMMARY KKP III


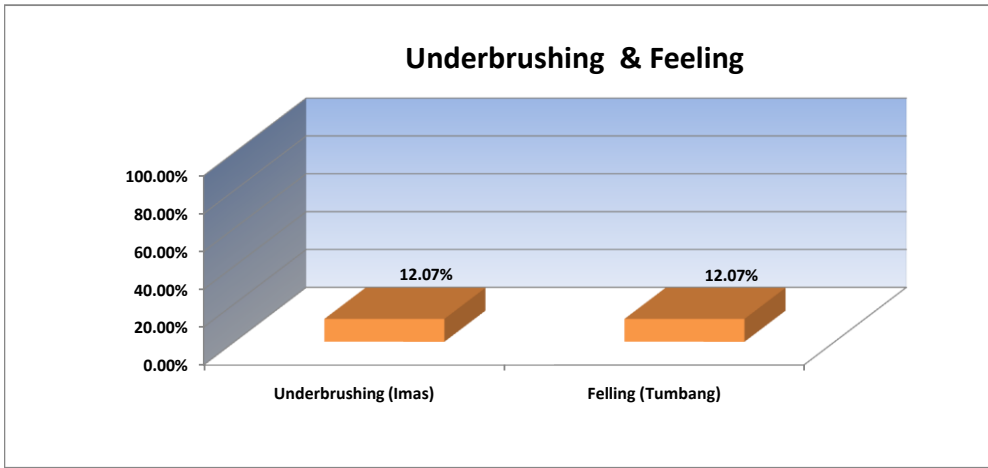



Chart & Detail Per Month

| Type of Work | SPK Vol (Ha) | Progress | % |
|-------------------------------------|----------------|----------|-------|
| Stacking Bulldozer - Low Vegetation | 368.20 | - | 0.00% |

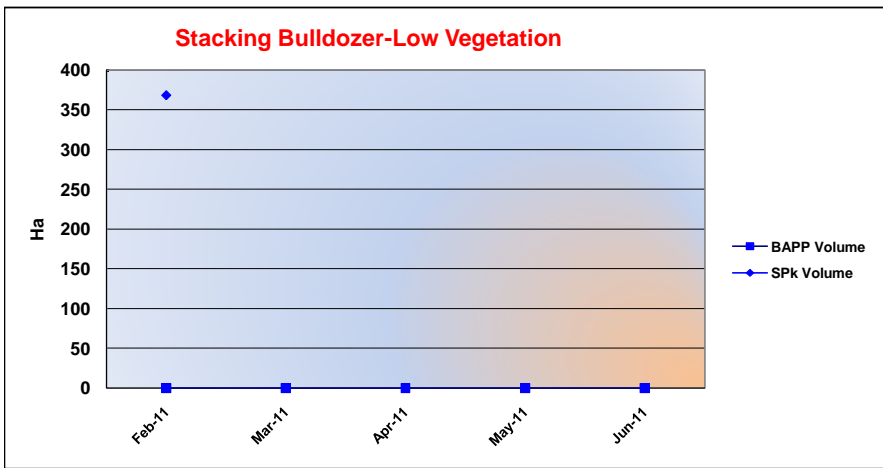

| Month | Monthly Progress | Accumulated |
|--------------|------------------|-------------|
| Feb-11 | - | - |
| Mar-11 | - | - |
| Apr-11 | - | - |
| May-11 | - | - |
| Jun-11 | - | - |
| Total | - | - |

| Type of Work | SPK Vol (Ha) | Progress | % |
|--------------------|----------------|----------|--------|
| Stacking Excavator | 157.80 | 63.50 | 40.24% |

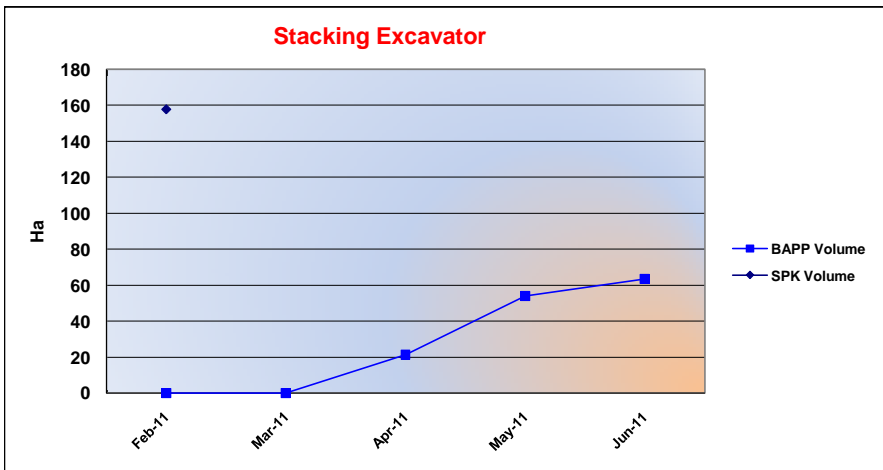


| Month | Monthly Progress | Accumulated |
|--------------|------------------|-------------|
| Feb-11 | - | - |
| Mar-11 | - | - |
| Apr-11 | 21.35 | 21.35 |
| May-11 | 32.67 | 54.02 |
| Jun-11 | 9.48 | 63.50 |
| Total | 63.50 | 63.50 |



PT. KARUNIA KENCANA PERMAISEJATI


CLAIM SUMMARY KKP III

| Type of Work | SPK Vol (Meter) | Progress | % |
|--------------------|-------------------|----------|--------|
| Road Formation 8 M | 5,260.00 | 859.00 | 16.33% |

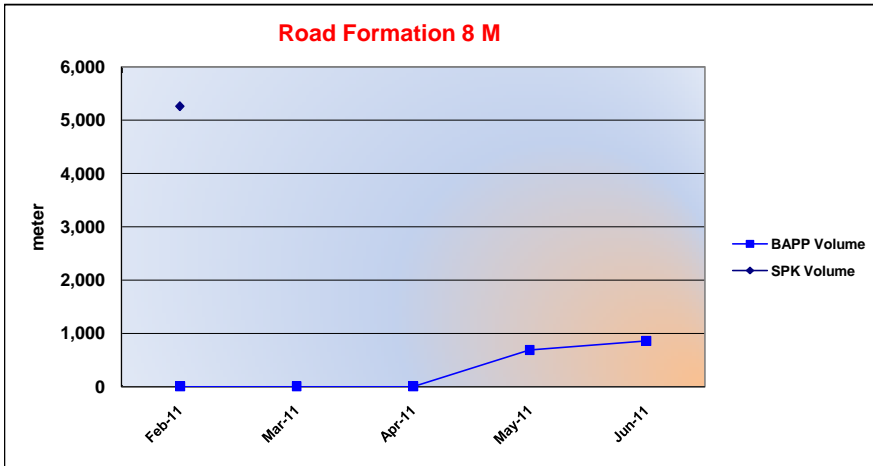


| Month | Monthly Progress | Accumulated |
|--------------|------------------|-------------|
| Feb-11 | - | - |
| Mar-11 | - | - |
| Apr-11 | - | - |
| May-11 | 689.00 | 689.00 |
| Jun-11 | 170.00 | 859.00 |
| Total | 859.00 | |

| Type of Work | SPK Vol (Meter) | Progress | % |
|--------------------|-------------------|----------|-------|
| Road Formation 6 M | 26,300.00 | 1,894.00 | 7.20% |

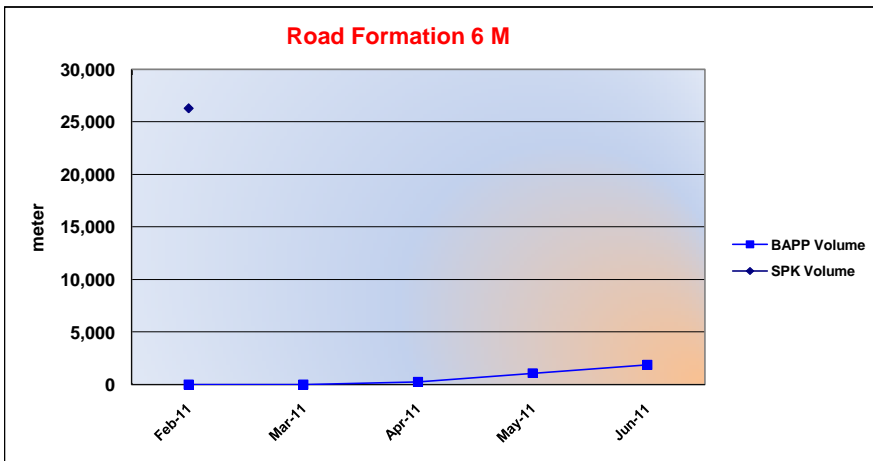

| Month | Monthly Progress | Accumulated |
|--------------|------------------|-------------|
| Feb-11 | - | - |
| Mar-11 | - | - |
| Apr-11 | 249.00 | 249.00 |
| May-11 | 849.00 | 1,098.00 |
| Jun-11 | 796.00 | 1,894.00 |
| Total | 1,894.00 | |

| Type of Work | SPK Vol (Meter) | Progress | % |
|------------------------|-------------------|----------|-------|
| Main Drain 2,4x1,8x1,2 | 2,630.00 | - | 0.00% |

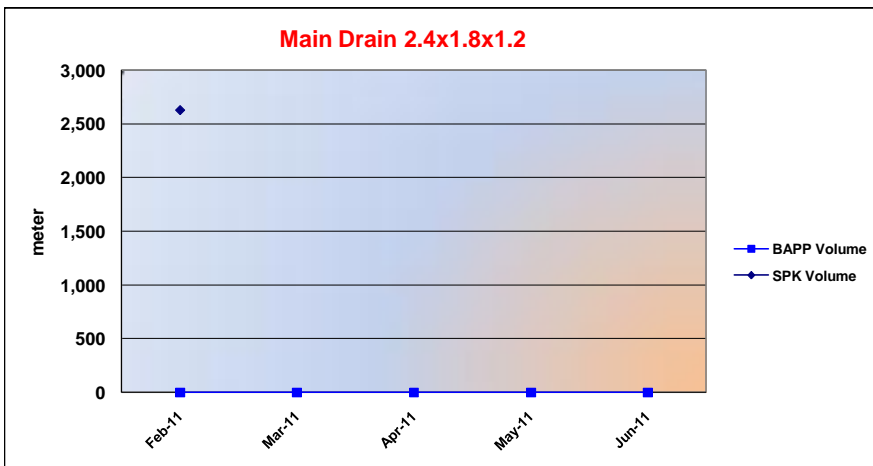


| Month | Monthly Progress | Accumulated |
|--------------|------------------|-------------|
| Feb-11 | - | - |
| Mar-11 | - | - |
| Apr-11 | - | - |
| May-11 | - | - |
| Jun-11 | - | - |
| Total | - | |



PT. KARUNIA KENCANA PERMAISEJATI


CLAIM SUMMARY KKP III

| Type of Work | SPK Vol (Meter) | Progress | % |
|------------------------------|-------------------|----------|--------|
| Collection Drain 1,8x1,2x0,9 | 13,150.00 | 5,808.00 | 44.17% |

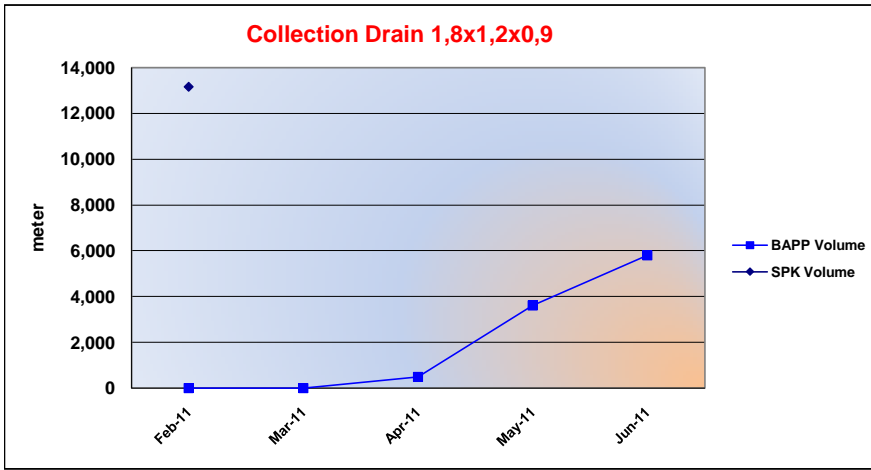


| Month | Monthly Progress | Accumulated |
|--------------|------------------|-------------|
| Feb-11 | - | - |
| Mar-11 | - | - |
| Apr-11 | 499.00 | 499.00 |
| May-11 | 3,118.00 | 3,617.00 |
| Jun-11 | 2,191.00 | 5,808.00 |
| Total | 5,808.00 | |

| Type of Work | SPK Vol (Meter) | Progress | % |
|---------------------------|-------------------|-----------|--------|
| Infield Drain 1,2x0,9x0,6 | 81,512.00 | 19,964.00 | 24.49% |

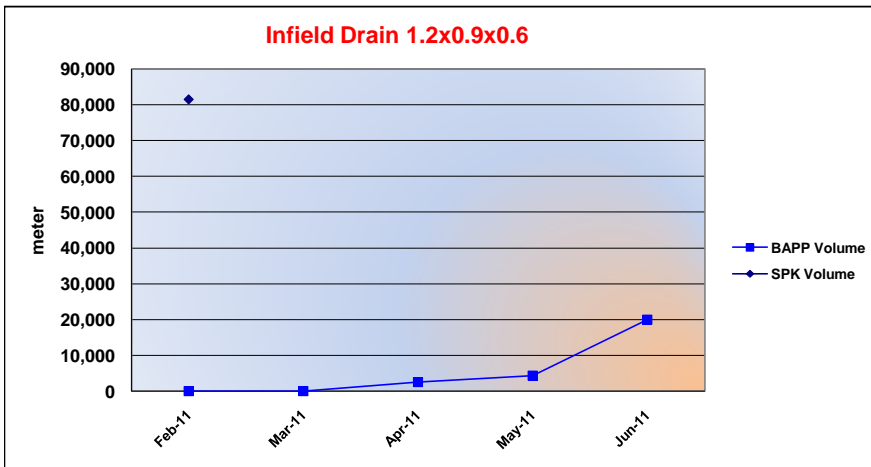

| Month | Monthly Progress | Accumulated |
|--------------|------------------|-------------|
| Feb-11 | - | - |
| Mar-11 | - | - |
| Apr-11 | 2,560.00 | 2,560.00 |
| May-11 | 1,738.00 | 4,298.00 |
| Jun-11 | 15,666.00 | 19,964.00 |
| Total | 19,964.00 | |

| Type of Work | SPK Vol (Ha) | Progress | % |
|----------------------|----------------|----------|--------|
| Underbrushing (Imas) | 526.00 | 63.50 | 12.07% |

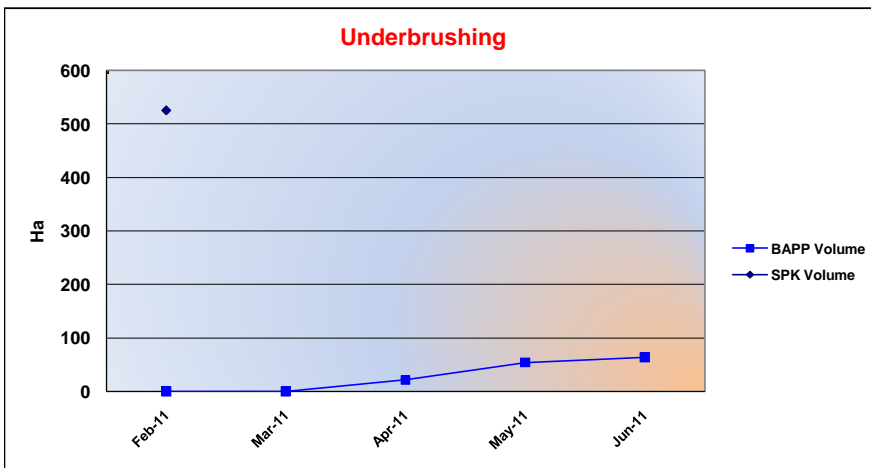


| Month | Monthly Progress | Accumulated |
|--------------|------------------|-------------|
| Feb-11 | - | - |
| Mar-11 | - | - |
| Apr-11 | 21.35 | 21.35 |
| May-11 | 32.67 | 54.02 |
| Jun-11 | 9.48 | 63.50 |
| Total | 63.50 | |



PT. KARUNIA KENCANA PERMAISEJATI

CLAIM SUMMARY KKP III

| Type of Work | SPK Vol (Ha) | Progress | % |
|-------------------|----------------|----------|--------|
| Felling (Tumbang) | 526.00 | 63.50 | 12.07% |

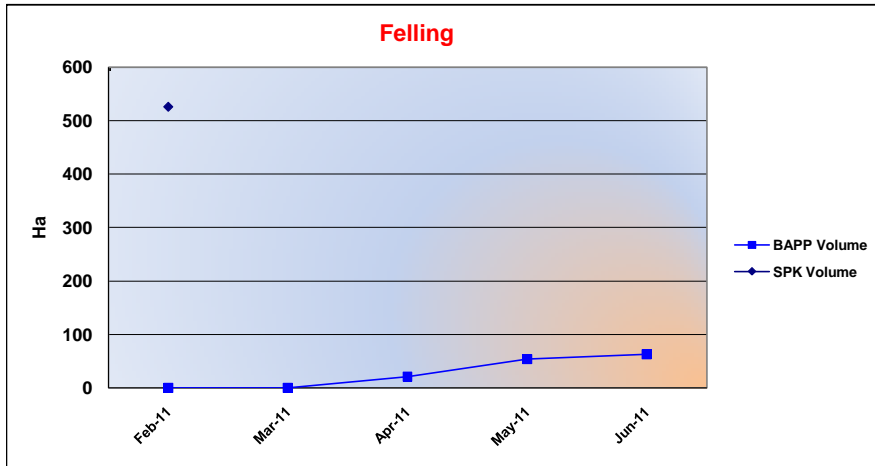

| Month | Monthly Progress | Accumulated |
|--------|------------------|-------------|
| Feb-11 | - | - |
| Mar-11 | - | - |
| Apr-11 | 21.35 | 21.35 |
| May-11 | 32.67 | 54.02 |
| Jun-11 | 9.48 | 63.50 |
| Total | 63.50 | |
