




CLAIM SUMMARY KKP III


Contract No :
C&A. 1608.02/KKP3 - 070

Type of Work	Unit	SPK Vol	Feb - Apr 2011 Claim	May Claim	Total Claimed (Feb - May 2011)	%
Bulldozer						
Stacking Bulldozer - Low Vegetation	Ha	368.20	-	-	-	0.00%
Excavator						
Stacking Excavator	Ha	157.80	21.35	32.67	54.02	34.23%
Road Formation 8 M	Meter	5,260.00	-	689.00	689.00	13.10%
Road Formation 6 M	Meter	26,300.00	249.00	849.00	1,098.00	4.17%
Main Drain 2,4x1,8x1,2	Meter	2,630.00	-	-	-	0.00%
Collection Drain 1,8x1,2x0,9	Meter	13,150.00	499.00	3,118.00	3,617.00	27.51%
Infield Drain 1,2x0,9x0,6	Meter	81,512.00	2,560.00	1,738.00	4,298.00	5.27%
Underbrushing (Imas)						
Underbrushing (Imas)	Ha	526.00	21.35	32.67	54.02	10.27%
Felling (Tumbang)						
Felling (Tumbang)	Ha	526.00	21.35	32.67	54.02	10.27%


Bulldozer Work



Excavator Work

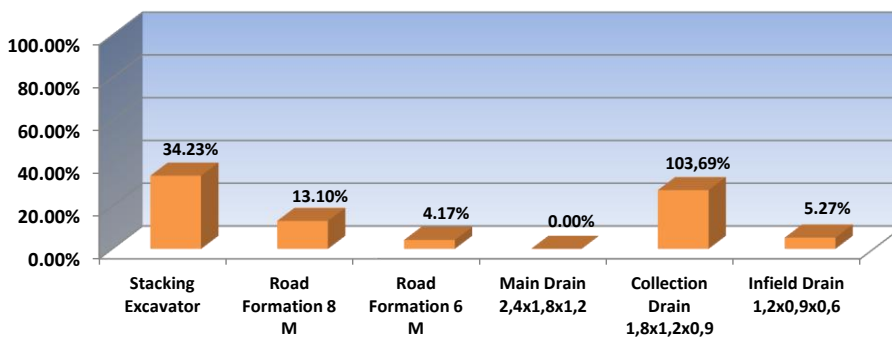

Underbrushing & Feeling

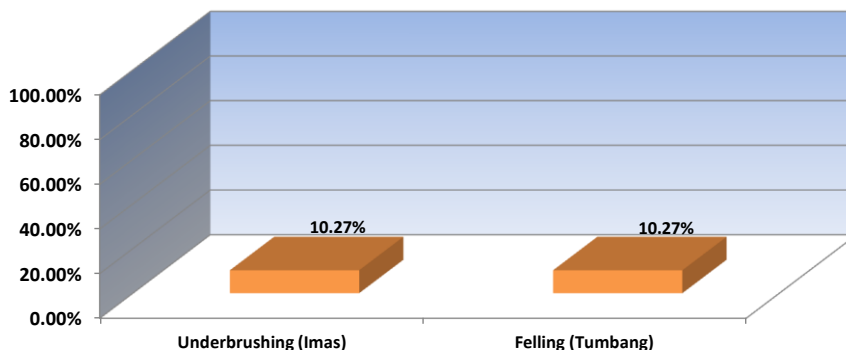




CLAIM SUMMARY KKP III


Chart & Detail Per Month

Type of Work	SPK Vol (Ha)	Progress	%
Stacking Bulldozer - Low Vegetation	368.20	-	0.00%

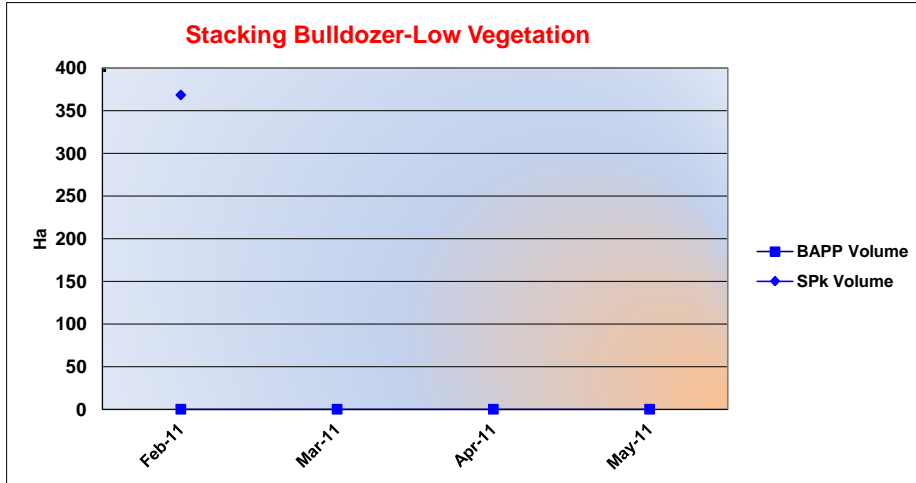


Month	Monthly Progress	Accumulated
Feb-11	-	-
Mar-11	-	-
Apr-11	-	-
May-11	-	-
Total	-	-

Type of Work	SPK Vol (Ha)	Progress	%
Stacking Excavator	157.80	54.02	34.23%

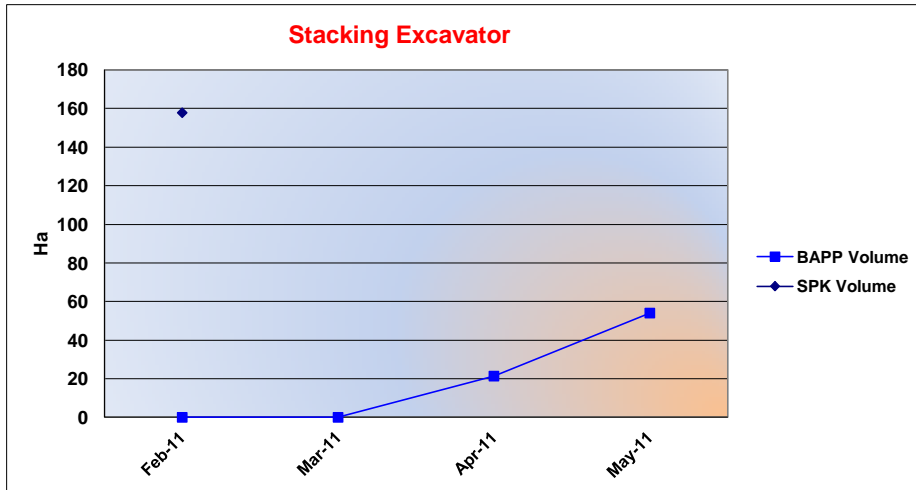

Month	Monthly Progress	Accumulated
Feb-11	-	-
Mar-11	-	-
Apr-11	21.35	21.35
May-11	32.67	54.02
Total	54.02	54.02

Type of Work	SPK Vol (Meter)	Progress	%
Road Formation 8 M	5,260.00	689.00	13.10%

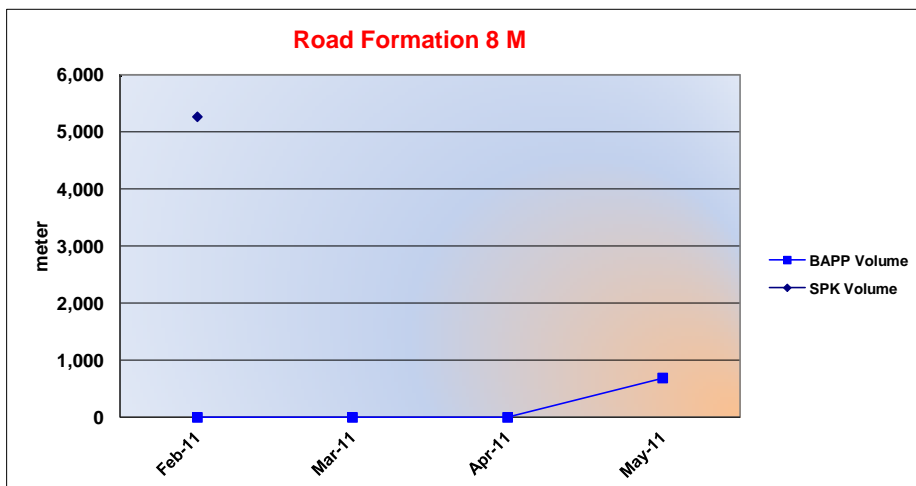


Month	Monthly Progress	Accumulated
Feb-11	-	-
Mar-11	-	-
Apr-11	-	-
May-11	689.00	689.00
Total	689.00	689.00




CLAIM SUMMARY KKP III

Type of Work	SPK Vol (Meter)	Progress	%
Road Formation 6 M	26,300.00	1,098.00	4.17%

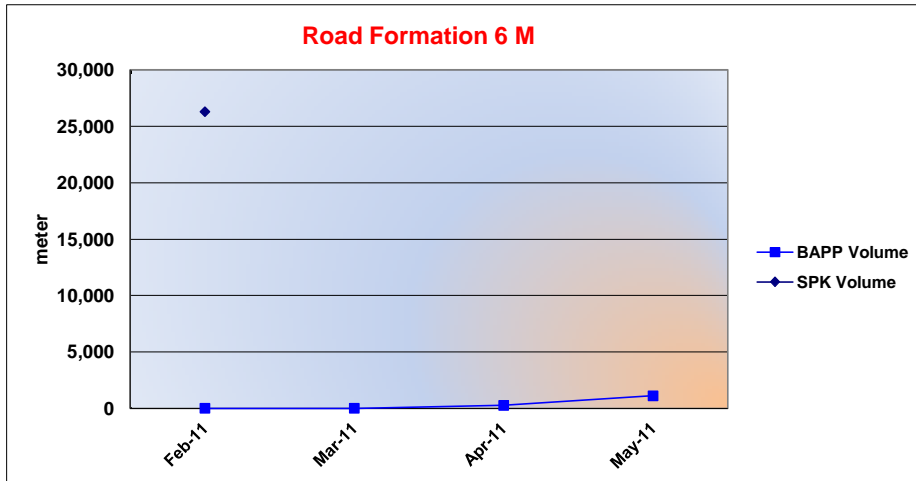


Month	Monthly Progress	Accumulated
Feb-11	-	-
Mar-11	-	-
Apr-11	249.00	249.00
May-11	849.00	1,098.00
Total	1,098.00	

Type of Work	SPK Vol (Meter)	Progress	%
Main Drain 2,4x1,8x1,2	2,630.00	-	0.00%

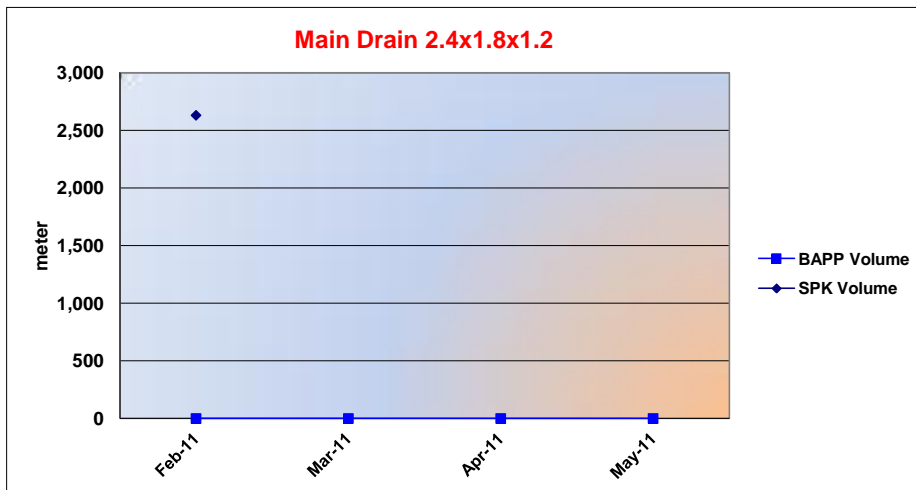

Month	Monthly Progress	Accumulated
Feb-11	-	-
Mar-11	-	-
Apr-11	-	-
May-11	-	-
Total	-	

Type of Work	SPK Vol (Meter)	Progress	%
Collection Drain 1,8x1,2x0,9	13,150.00	3,617.00	27.51%

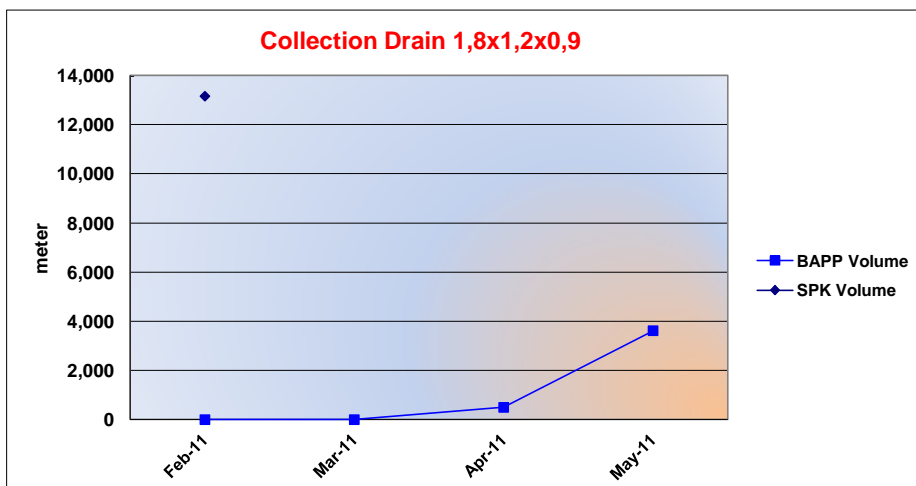


Month	Monthly Progress	Accumulated
Feb-11	-	-
Mar-11	-	-
Apr-11	499.00	499.00
May-11	3,118.00	3,617.00
Total	3,617.00	




CLAIM SUMMARY KKP III

Type of Work	SPK Vol (Meter)	Progress	%
Infield Drain 1,2x0,9x0,6	81,512.00	4,298.00	5.27%

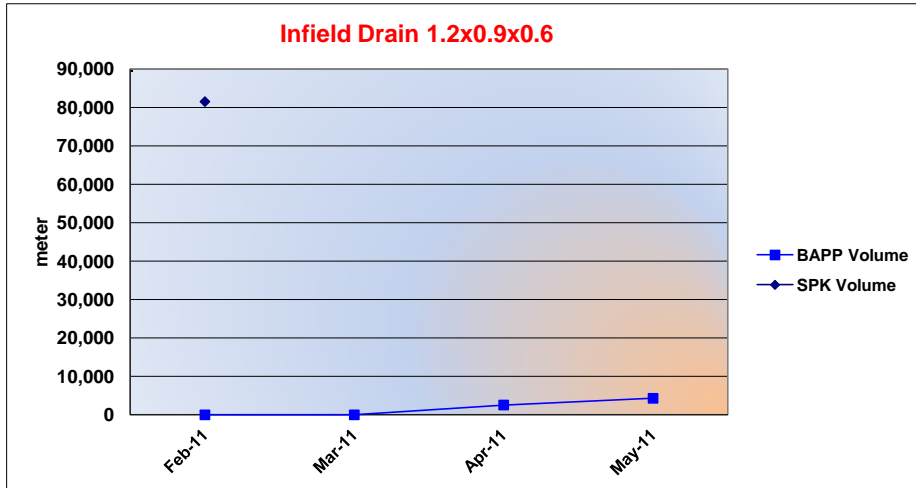


Month	Monthly Progress	Accumulated
Feb-11	-	-
Mar-11	-	-
Apr-11	2,560.00	2,560.00
May-11	1,738.00	4,298.00
Total	4,298.00	

Type of Work	SPK Vol (Ha)	Progress	%
Underbrushing (Imas)	526.00	54.02	10.27%

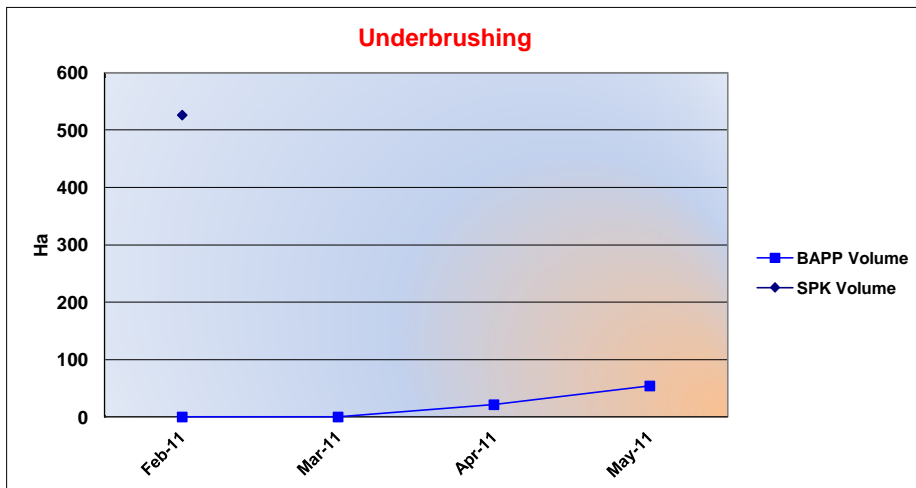

Month	Monthly Progress	Accumulated
Feb-11	-	-
Mar-11	-	-
Apr-11	21.35	21.35
May-11	32.67	54.02
Total	54.02	

Type of Work	SPK Vol (Ha)	Progress	%
Felling (Tumbang)	526.00	54.02	10.27%

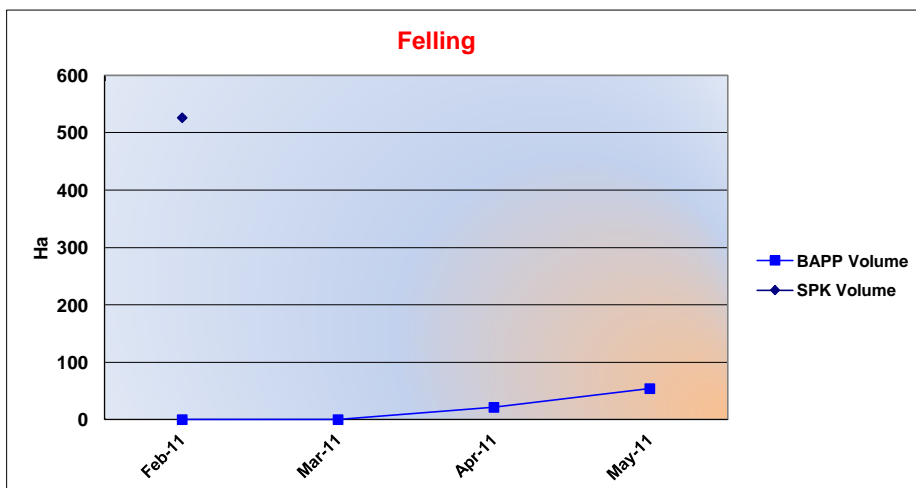

Month	Monthly Progress	Accumulated
Feb-11	-	-
Mar-11	-	-
Apr-11	21.35	21.35
May-11	32.67	54.02
Total	54.02	
