




CLAIM SUMMARY KKP III


Contract No :
C&A. 1608.02/KKP3 - 070

Type of Work	Unit	SPK Vol	Feb - May 2011 Claim	June Claim	Total Claimed (Feb - Jun 2011)	%
Bulldozer						
Stacking Bulldozer - Low Vegetation	Ha	368.20	-	-	-	0.00%
Excavator						
Stacking Excavator	Ha	157.80	54.02	9.48	63.50	40.24%
Road Formation 8 M	Meter	5,260.00	689.00	170.00	859.00	16.33%
Road Formation 6 M	Meter	26,300.00	1,098.00	796.00	1,894.00	7.20%
Main Drain 2,4x1,8x1,2	Meter	2,630.00	-	-	-	0.00%
Collection Drain 1,8x1,2x0,9	Meter	13,150.00	3,617.00	2,191.00	5,808.00	44.17%
Infield Drain 1,2x0,9x0,6	Meter	81,512.00	4,298.00	15,666.00	19,964.00	24.49%
Underbrushing (Imas)						
Underbrushing (Imas)	Ha	526.00	54.02	9.48	63.50	12.07%
Felling (Tumbang)						
Felling (Tumbang)	Ha	526.00	54.02	9.48	63.50	12.07%


Bulldozer Work



Excavator Work

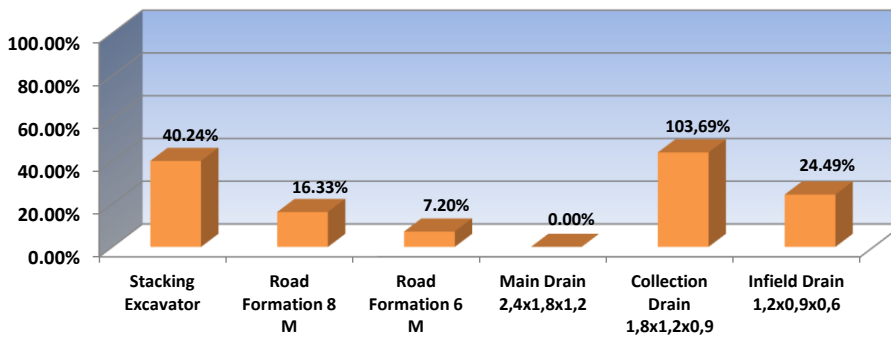

Underbrushing & Feeling

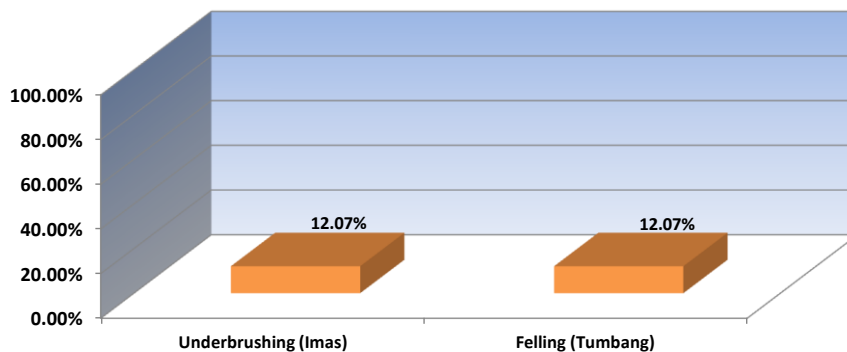




CLAIM SUMMARY KKP III


Chart & Detail Per Month

Type of Work	SPK Vol (Ha)	Progress	%
Stacking Bulldozer - Low Vegetation	368.20	-	0.00%

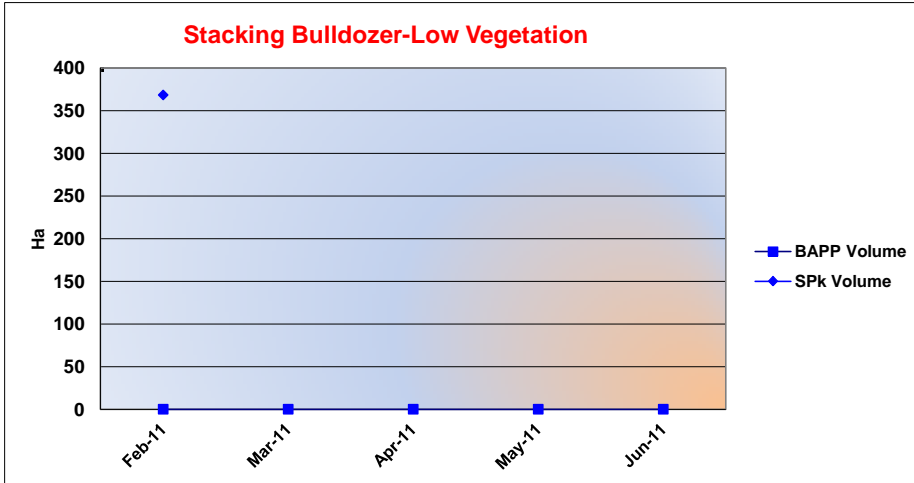


Month	Monthly Progress	Accumulated
Feb-11	-	-
Mar-11	-	-
Apr-11	-	-
May-11	-	-
Jun-11	-	-
Total	-	-

Type of Work	SPK Vol (Ha)	Progress	%
Stacking Excavator	157.80	63.50	40.24%

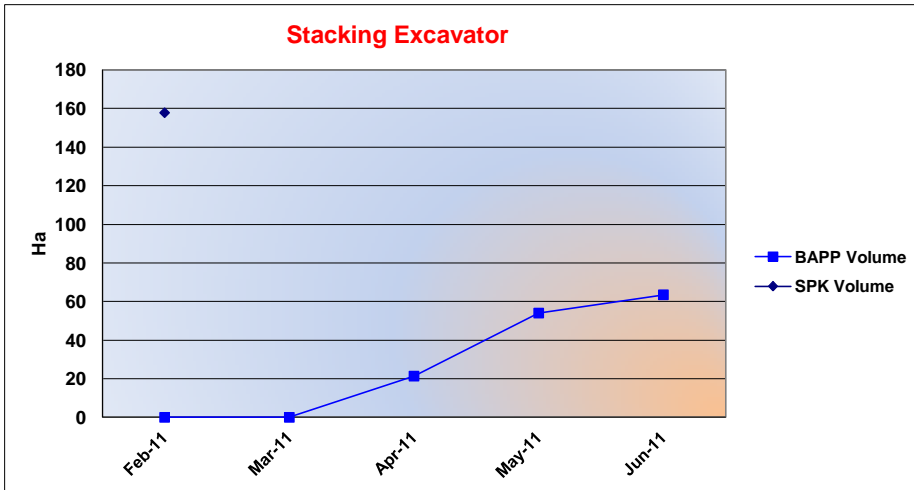

Month	Monthly Progress	Accumulated
Feb-11	-	-
Mar-11	-	-
Apr-11	21.35	21.35
May-11	32.67	54.02
Jun-11	9.48	63.50
Total	63.50	63.50

Type of Work	SPK Vol (Meter)	Progress	%
Road Formation 8 M	5,260.00	859.00	16.33%

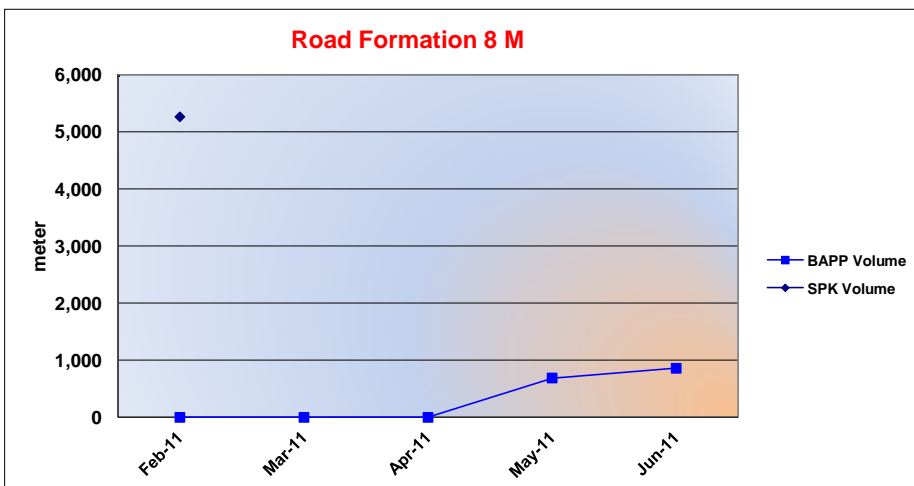


Month	Monthly Progress	Accumulated
Feb-11	-	-
Mar-11	-	-
Apr-11	-	-
May-11	689.00	689.00
Jun-11	170.00	859.00
Total	859.00	859.00



CLAIM SUMMARY KKP III


Type of Work	SPK Vol (Meter)	Progress	%
Road Formation 6 M	26,300.00	1,894.00	7.20%

Month	Monthly Progress	Accumulated
Feb-11	-	-
Mar-11	-	-
Apr-11	249.00	249.00
May-11	849.00	1,098.00
Jun-11	796.00	1,894.00
Total	1,894.00	

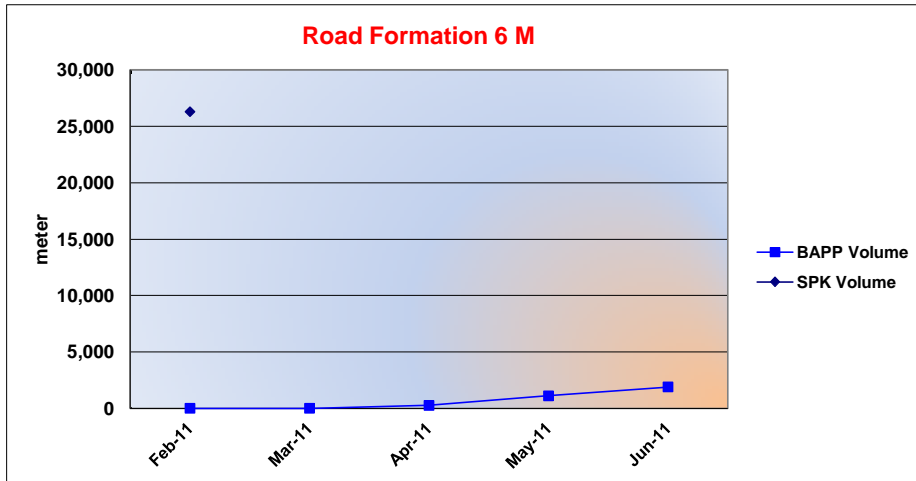


Type of Work	SPK Vol (Meter)	Progress	%
Main Drain 2,4x1,8x1,2	2,630.00	-	0.00%

Month	Monthly Progress	Accumulated
Feb-11	-	-
Mar-11	-	-
Apr-11	-	-
May-11	-	-
Jun-11	-	-
Total	-	

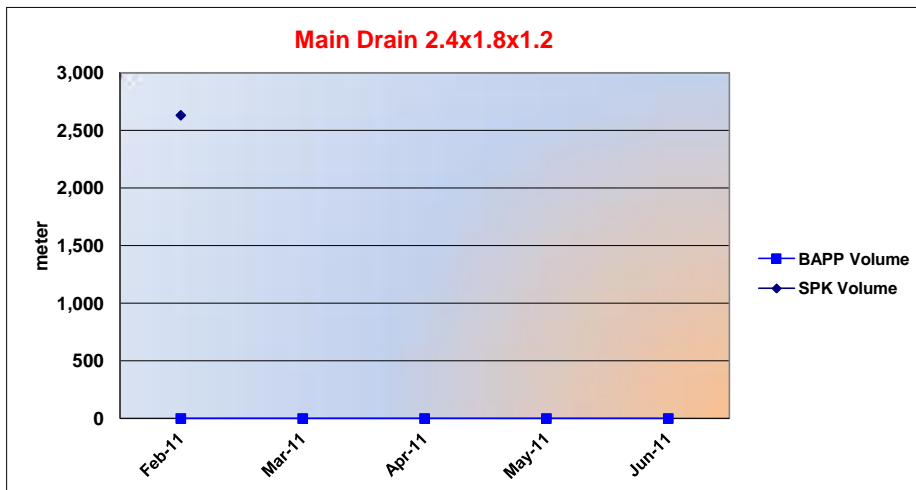

Type of Work	SPK Vol (Meter)	Progress	%
Collection Drain 1,8x1,2x0,9	13,150.00	5,808.00	44.17%


Month	Monthly Progress	Accumulated
Feb-11	-	-
Mar-11	-	-
Apr-11	499.00	499.00
May-11	3,118.00	3,617.00
Jun-11	2,191.00	5,808.00
Total	5,808.00	

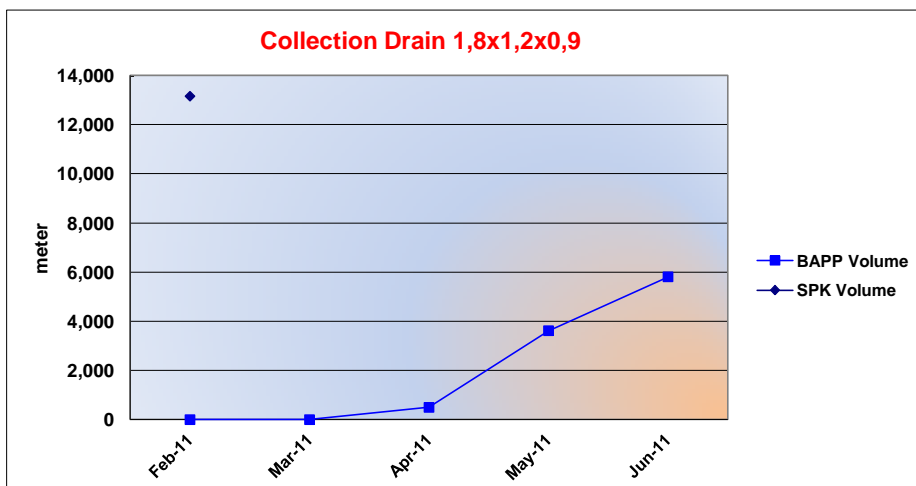




CLAIM SUMMARY KKP III

Type of Work	SPK Vol (Meter)	Progress	%
Infield Drain 1,2x0,9x0,6	81,512.00	19,964.00	24.49%

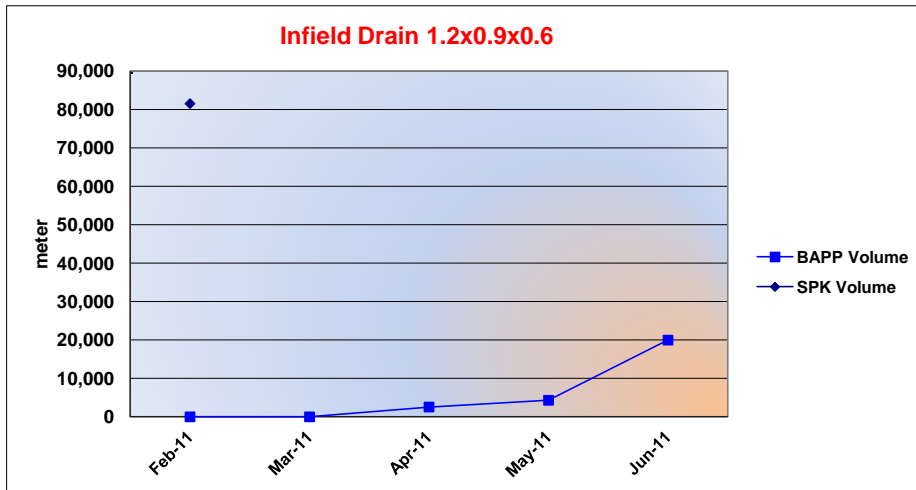


Month	Monthly Progress	Accumulated
Feb-11	-	-
Mar-11	-	-
Apr-11	2,560.00	2,560.00
May-11	1,738.00	4,298.00
Jun-11	15,666.00	19,964.00
Total	19,964.00	

Type of Work	SPK Vol (Ha)	Progress	%
Underbrushing (Imas)	526.00	63.50	12.07%

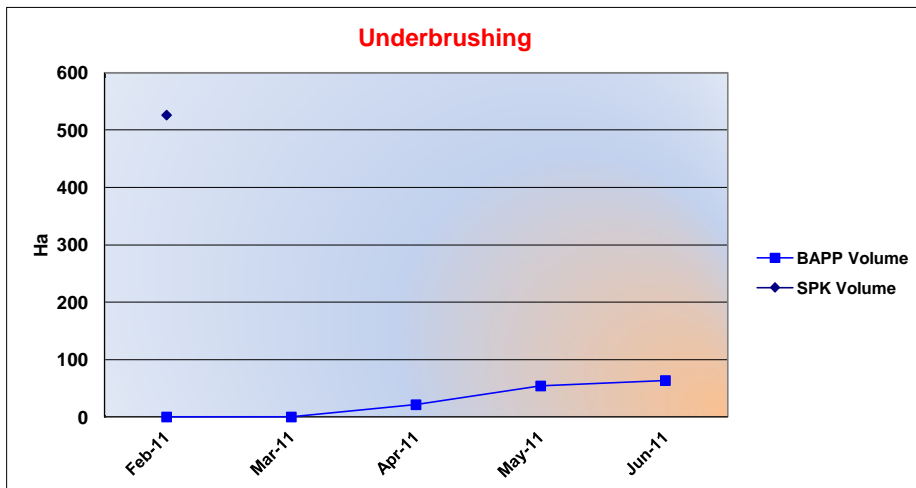

Month	Monthly Progress	Accumulated
Feb-11	-	-
Mar-11	-	-
Apr-11	21.35	21.35
May-11	32.67	54.02
Jun-11	9.48	63.50
Total	63.50	

Type of Work	SPK Vol (Ha)	Progress	%
Felling (Tumbang)	526.00	63.50	12.07%

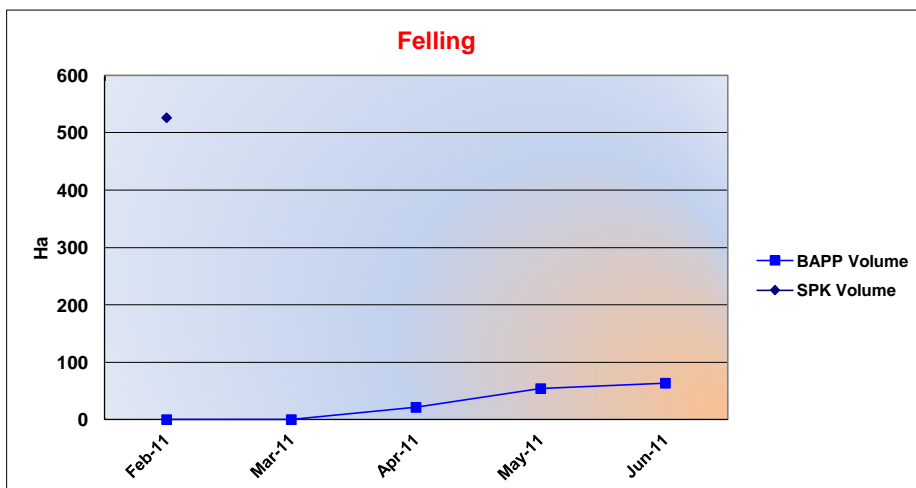

Month	Monthly Progress	Accumulated
Feb-11	-	-
Mar-11	-	-
Apr-11	21.35	21.35
May-11	32.67	54.02
Jun-11	9.48	63.50
Total	63.50	
