





PT. RIMBA HARAPAN SAKTI

CLAIM SUMMARY

Contract No :

1. C&A. 1608.02/RHS - 020

Type of Work	Unit	SPK Vol	January 2011 Claim	February Claim	Total Claimed (Jan - Feb 2011)	%
Bulldozer						
Stacking Bulldozer	Ha	200.00	-	-	-	0.00%
Excavator						
Stacking Excavator	Ha	500.00	-	49.90	49.90	9.98%
Road Formation 8 M	Meter	7,000.00	-	-	-	0.00%
Road Formation 6 M	Meter	35,000.00	-	474.00	474.00	1.35%
Main Drain 3,6x2,4x1,8	Meter	8,100.00	-	1,185.00	1,185.00	14.63%
Main Drain 2,4x1,8x1,2	Meter	27,000.00	-	8,847.00	8,847.00	32.77%
Collection Drain 1,8x1,2x0,9	Meter	130,000.00	-	26,298.00	26,298.00	20.23%
Infield Drain 1,2x0,9x0,6	Meter	1,782,000.00	-	671,001.00	671,001.00	37.65%
Underbrushing (Imas)	Ha	700.00	-	461.42	461.42	65.92%

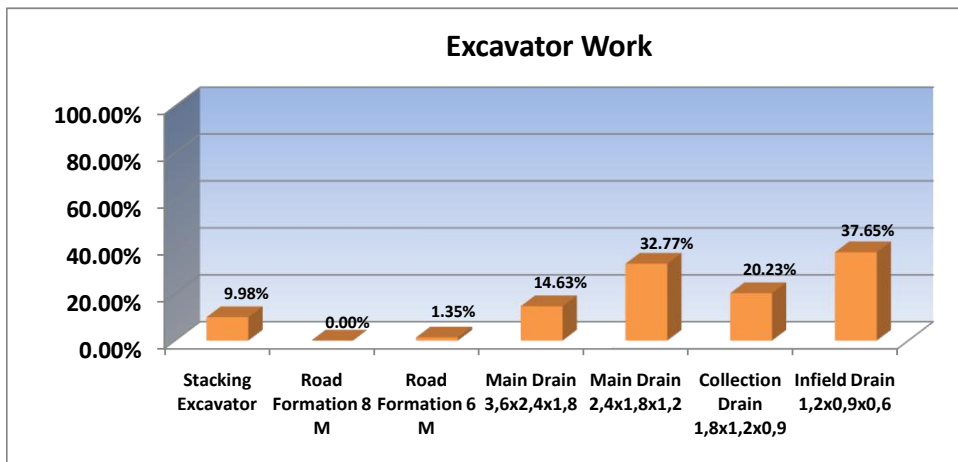



CLAIM SUMMARY


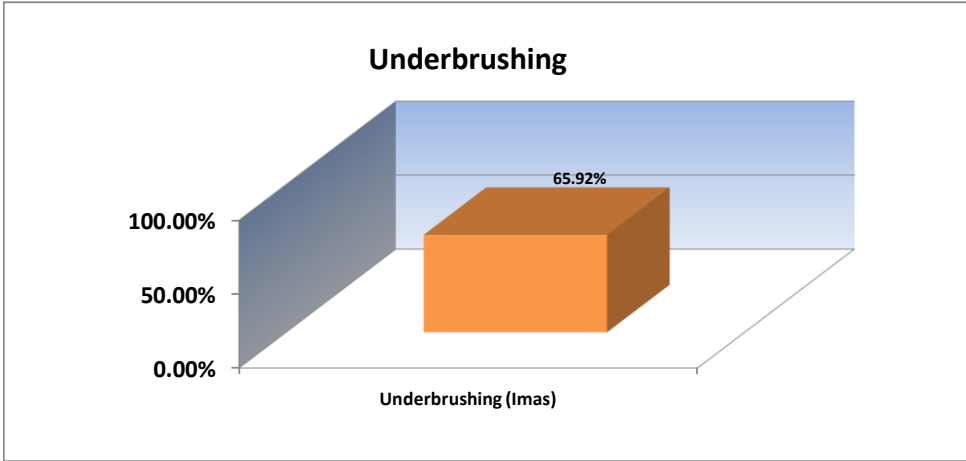



Chart & Detail Per Month

Type of Work	SPK Vol (Ha)	Progress	%
Stacking Bulldozer	200.00	-	0.00%

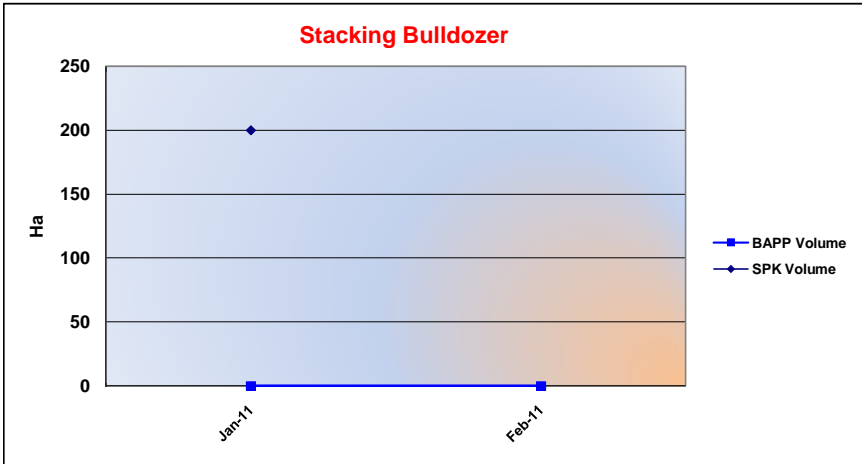

Month	Monthly Progress	Accumulated
Jan-11	-	-
Feb-11	-	-
Total	-	-

Type of Work	SPK Vol (Ha)	Progress	%
Stacking Excavator	500.00	49.90	9.98%

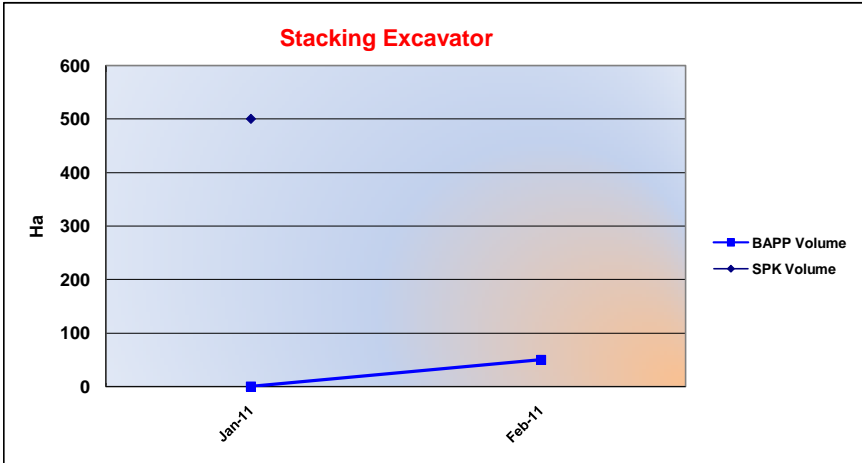


Month	Monthly Progress	Accumulated
Jan-11	-	-
Feb-11	49.90	49.90
Total	49.90	



PT. RIMBA HARAPAN SAKTI


CLAIM SUMMARY

Type of Work	SPK Vol (Meter)	Progress	%
Road Formation 8 M	7,000.00	-	0.00%

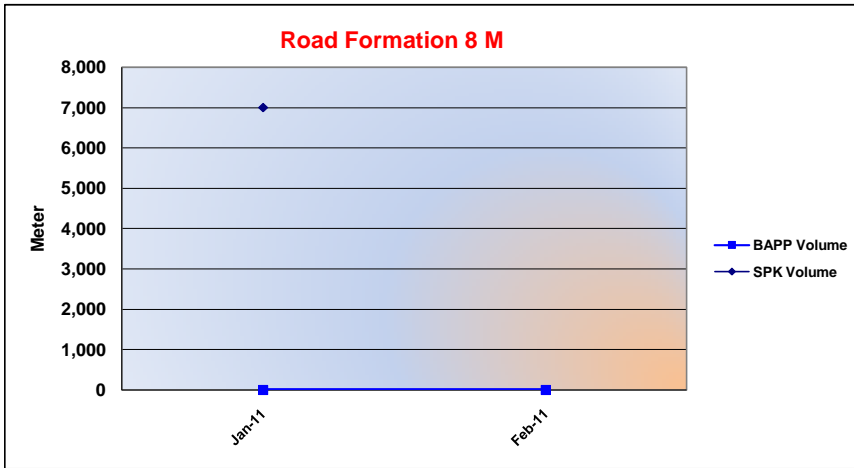


Month	Monthly Progress	Accumulated
Jan-11	-	-
Feb-11	-	-
Total	-	-

Type of Work	SPK Vol (Meter)	Progress	%
Road Formation 6 M	35,000.00	474.00	1.35%

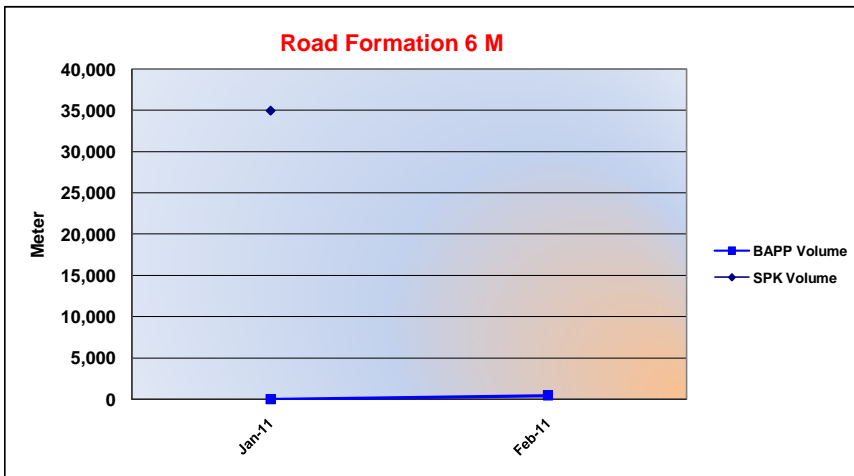

Month	Monthly Progress	Accumulated
Jan-11	-	-
Feb-11	474.00	474.00
Total	474.00	474.00

Type of Work	SPK Vol (Meter)	Progress	%
Main Drain 3,6x2,4x1,8	8,100.00	1,185.00	14.63%

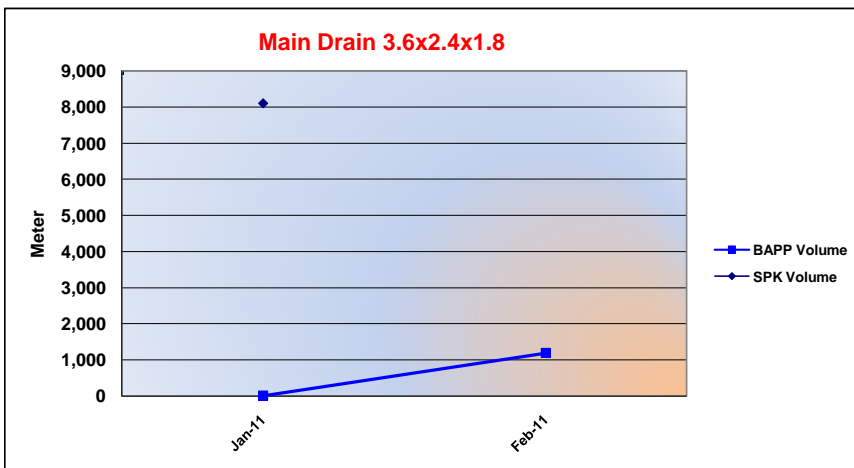


Month	Monthly Progress	Accumulated
Jan-11	-	-
Feb-11	1,185.00	1,185.00
Total	1,185.00	1,185.00



PT. RIMBA HARAPAN SAKTI


CLAIM SUMMARY

Type of Work	SPK Vol (Meter)	Progress	%
Main Drain 2,4x1,8x1,2	27,000.00	8,847.00	32.77%

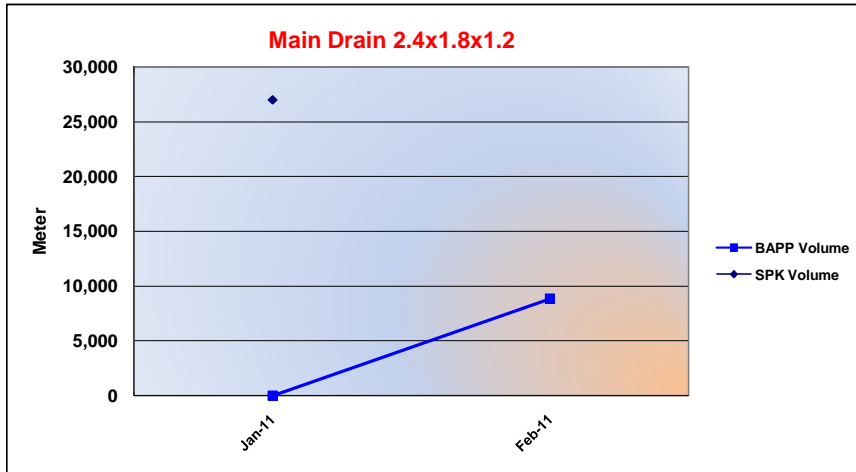


Month	Monthly Progress	Accumulated
Jan-11	-	-
Feb-11	8,847.00	8,847.00
Total	8,847.00	

Type of Work	SPK Vol (Meter)	Progress	%
Collection Drain 1,8x1,2x0,9	130,000.00	26,298.00	20.23%

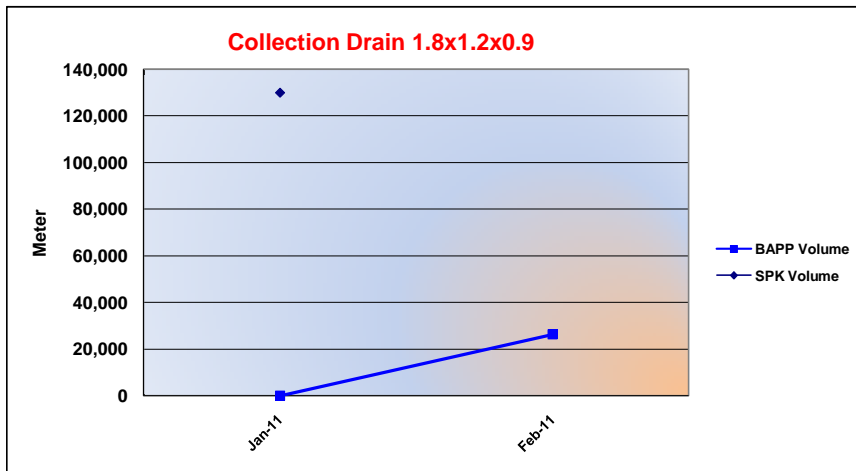

Month	Monthly Progress	Accumulated
Jan-11	-	-
Feb-11	26,298.00	26,298.00
Total	26,298.00	

Type of Work	SPK Vol (Meter)	Progress	%
Infield Drain 1,2x0,9x0,6	1,782,000.00	671,001.00	37.65%

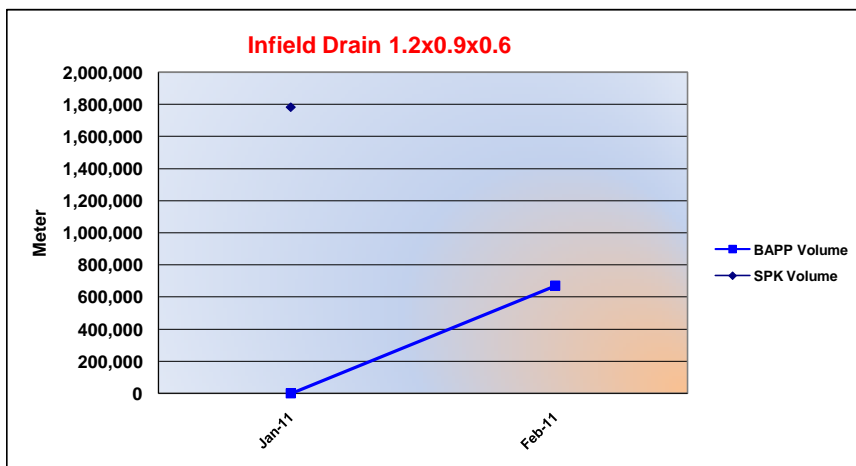


Month	Monthly Progress	Accumulated
Jan-11	-	-
Feb-11	671,001.00	671,001.00
Total	671,001.00	



PT. RIMBA HARAPAN SAKTI

CLAIM SUMMARY

Type of Work	SPK Vol (Ha)	Progress	%
Underbrushing (Imas)	700.00	461.42	65.92%

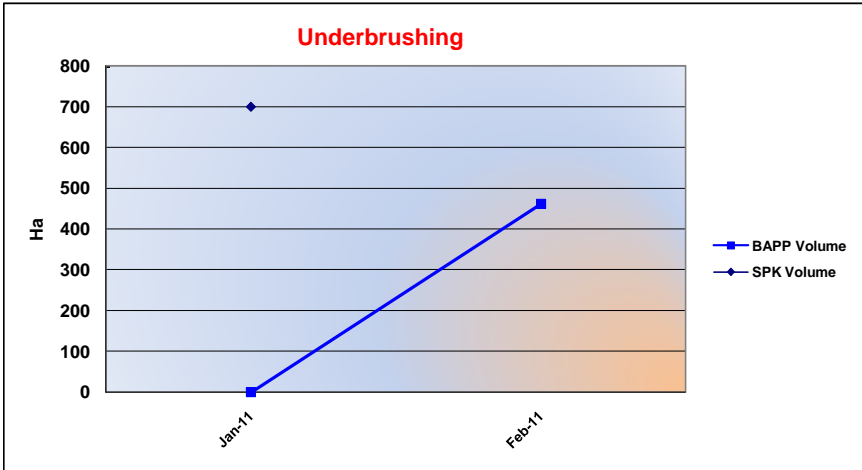

Month	Monthly Progress	Accumulated
Jan-11	-	-
Feb-11	461.42	461.42
Total	461.42	
