





# PT. RIMBA HARAPAN SAKTI

## CLAIM SUMMARY

Contract No :

1. C&A. 1608.02/RHS - 020


Type of Work	Unit	SPK Vol	Jan - May 2011 Claim	June Claim	Total Claimed (Jan - Jun 2011)	%
<b>Bulldozer</b>						
Stacking Bulldozer	Ha	200.00	-	-	-	0.00%
<b>Excavator</b>						
Stacking Excavator	Ha	500.00	175.99	17.50	193.49	38.70%
Road Formation 8 M	Meter	7,000.00	-	-	-	0.00%
Road Formation 6 M	Meter	35,000.00	6,510.00	-	6,510.00	18.60%
Main Drain 3,6x2,4x1,8	Meter	8,100.00	1,185.00	-	1,185.00	14.63%
Main Drain 2,4x1,8x1,2	Meter	27,000.00	11,173.00	-	11,173.00	41.38%
Collection Drain 1,8x1,2x0,9	Meter	130,000.00	30,446.00	4,451.00	34,897.00	26.84%
Infield Drain 1,2x0,9x0,6	Meter	1,782,000.00	1,116,914.00	260,381.00	1,377,295.00	77.29%
Underbrushing (Imas)	Ha	700.00	587.51	17.50	605.01	86.43%

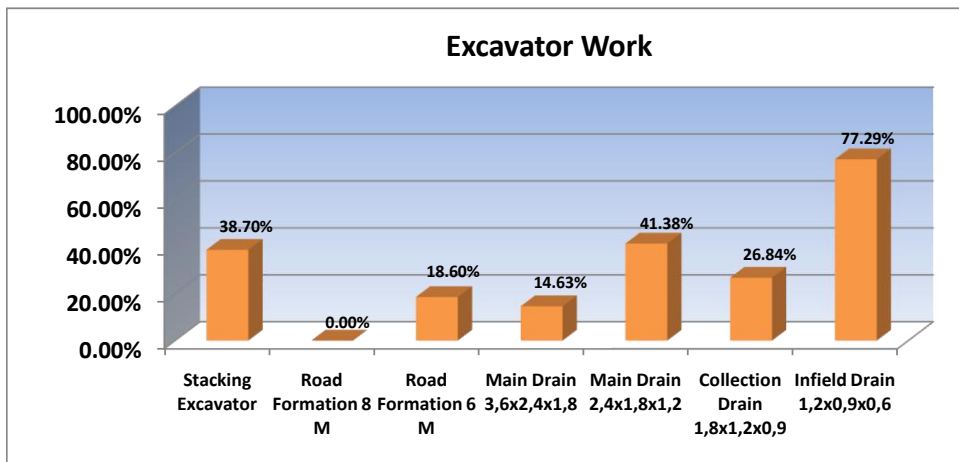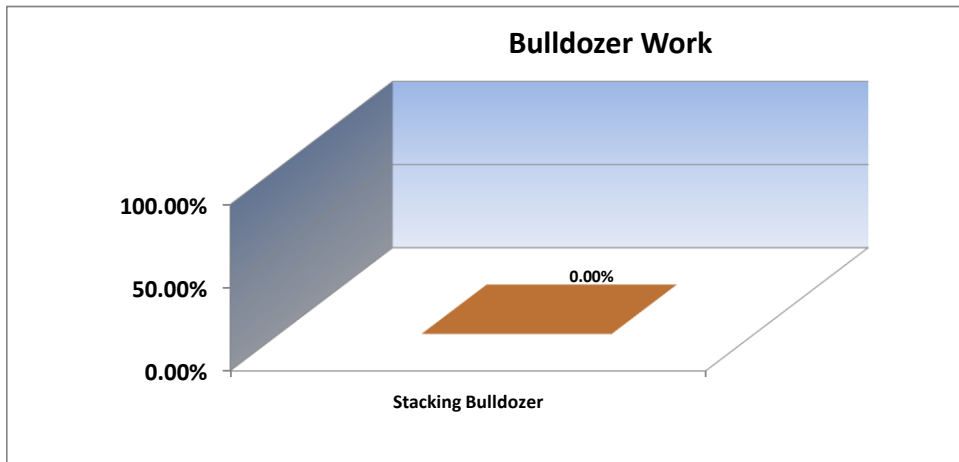




# PT. RIMBA HARAPAN SAKTI

## CLAIM SUMMARY

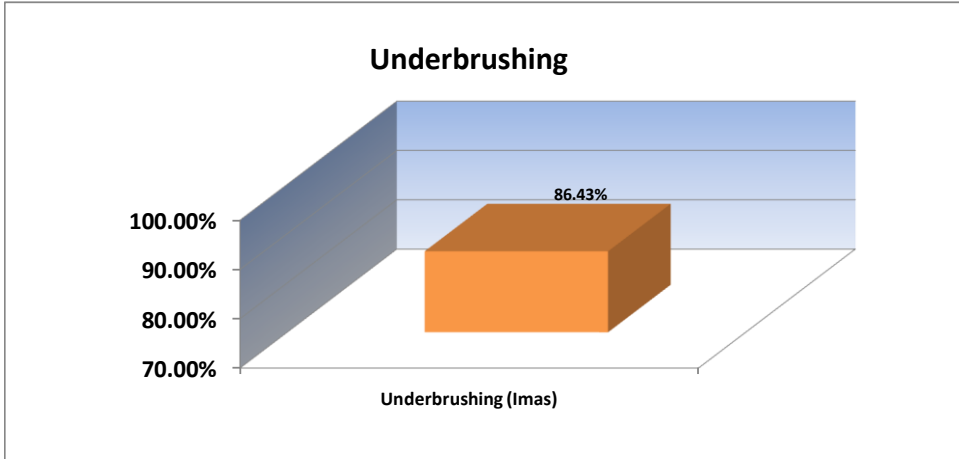


### Chart & Detail Per Month

Type of Work	SPK Vol ( Ha )	Progress	%
Stacking Bulldozer	200.00	-	0.00%

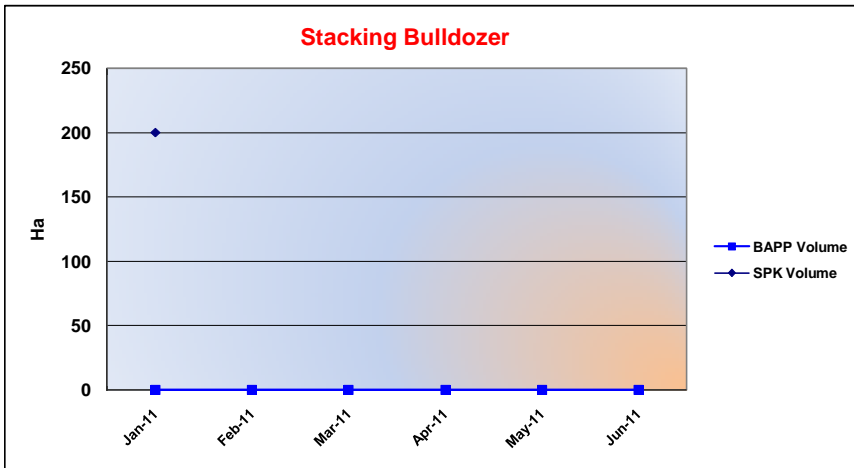

Month	Monthly Progress	Accumulated
Jan-11	-	-
Feb-11	-	-
Mar-11	-	-
Apr-11	-	-
May-11	-	-
Jun-11	-	-
<b>Total</b>	-	-

Type of Work	SPK Vol ( Ha )	Progress	%
Stacking Excavator	500.00	193.49	38.70%

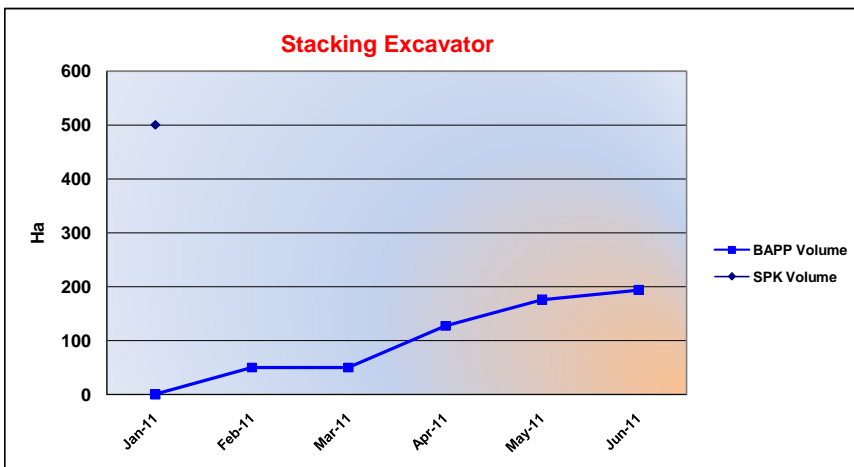


Month	Monthly Progress	Accumulated
Jan-11	-	-
Feb-11	49.90	49.90
Mar-11	-	49.90
Apr-11	76.92	126.82
May-11	49.17	175.99
Jun-11	17.50	193.49
<b>Total</b>	193.49	



# PT. RIMBA HARAPAN SAKTI


## CLAIM SUMMARY

Type of Work	SPK Vol (Meter)	Progress	%
Road Formation 8 M	7,000.00	-	0.00%

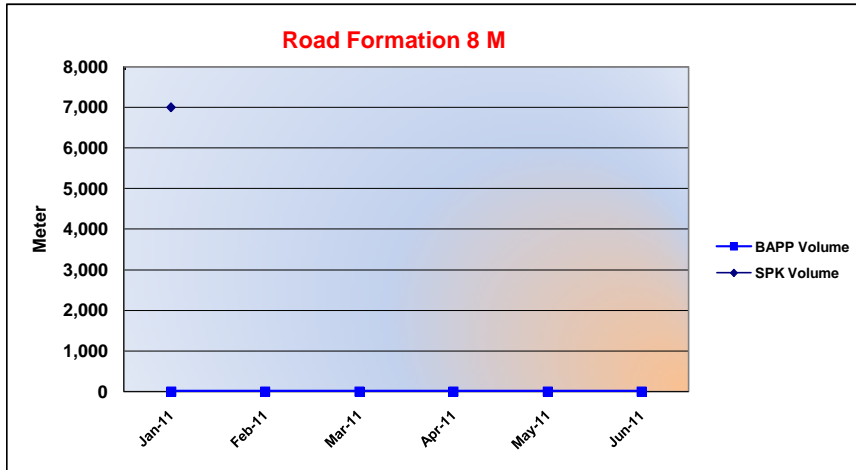


Month	Monthly Progress	Accumulated
Jan-11	-	-
Feb-11	-	-
Mar-11	-	-
Apr-11	-	-
May-11	-	-
Jun-11	-	-
<b>Total</b>	<b>-</b>	<b>-</b>

Type of Work	SPK Vol (Meter)	Progress	%
Road Formation 6 M	35,000.00	6,510.00	18.60%

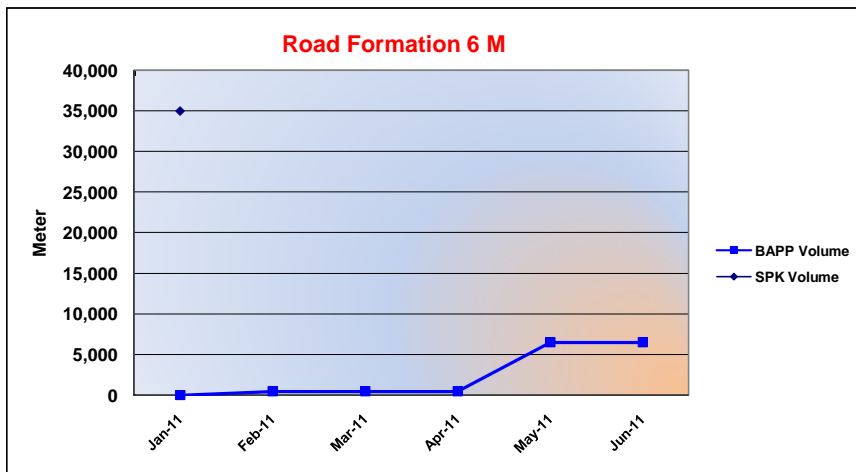

Month	Monthly Progress	Accumulated
Jan-11	-	-
Feb-11	474.00	474.00
Mar-11	-	474.00
Apr-11	-	474.00
May-11	6,036.00	6,510.00
Jun-11	-	6,510.00
<b>Total</b>	<b>6,510.00</b>	<b>-</b>

Type of Work	SPK Vol (Meter)	Progress	%
Main Drain 3.6x2.4x1.8	8,100.00	1,185.00	14.63%

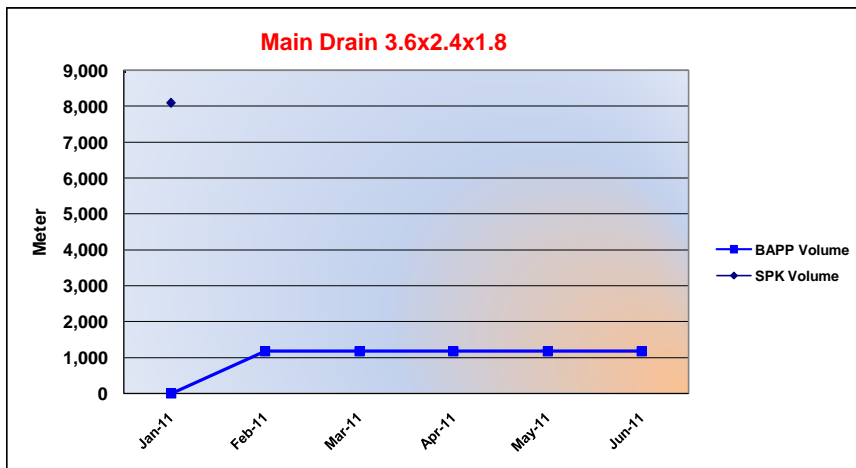


Month	Monthly Progress	Accumulated
Jan-11	-	-
Feb-11	1,185.00	1,185.00
Mar-11	-	1,185.00
Apr-11	-	1,185.00
May-11	-	1,185.00
Jun-11	-	1,185.00
<b>Total</b>	<b>1,185.00</b>	<b>-</b>



# PT. RIMBA HARAPAN SAKTI


## CLAIM SUMMARY

Type of Work	SPK Vol (Meter)	Progress	%
Main Drain 2,4x1,8x1,2	27,000.00	11,173.00	41.38%

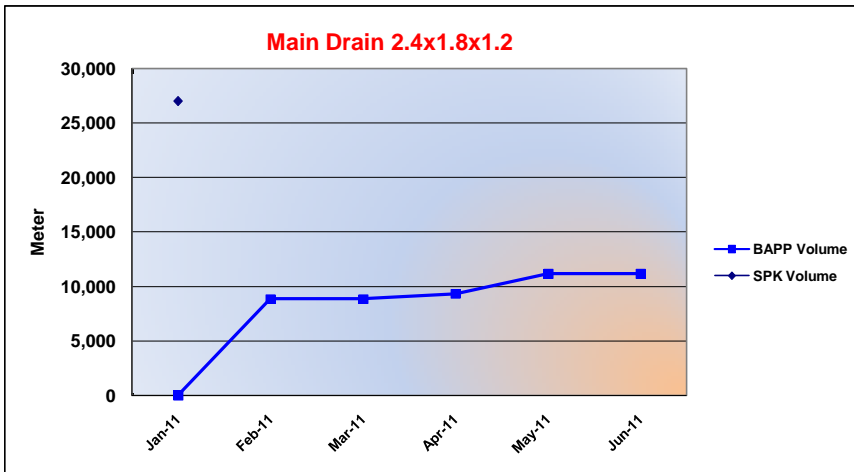


Month	Monthly Progress	Accumulated
Jan-11	-	-
Feb-11	8,847.00	8,847.00
Mar-11	-	8,847.00
Apr-11	482.00	9,329.00
May-11	1,844.00	11,173.00
Jun-11	-	11,173.00
<b>Total</b>	<b>11,173.00</b>	

Type of Work	SPK Vol (Meter)	Progress	%
Collection Drain 1,8x1,2x0,9	130,000.00	34,897.00	26.84%

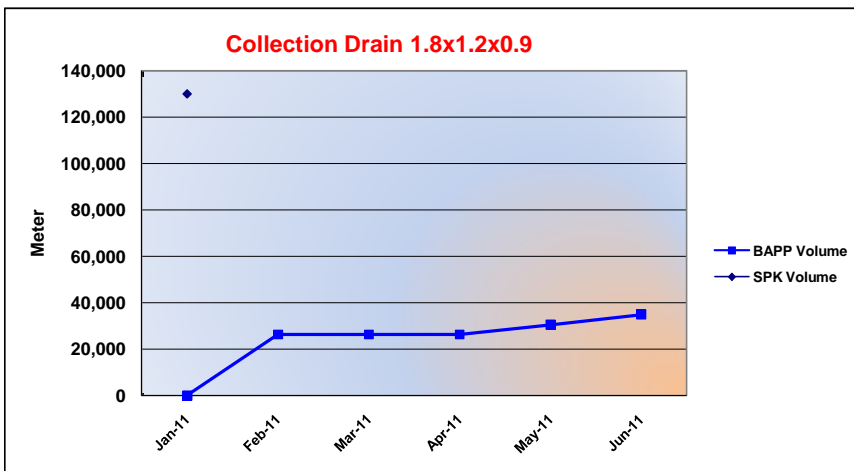

Month	Monthly Progress	Accumulated
Jan-11	-	-
Feb-11	26,298.00	26,298.00
Mar-11	-	26,298.00
Apr-11	-	26,298.00
May-11	4,148.00	30,446.00
Jun-11	4,451.00	34,897.00
<b>Total</b>	<b>34,897.00</b>	

Type of Work	SPK Vol (Meter)	Progress	%
Infield Drain 1,2x0,9x0,6	1,782,000.00	1,377,295.00	77.29%

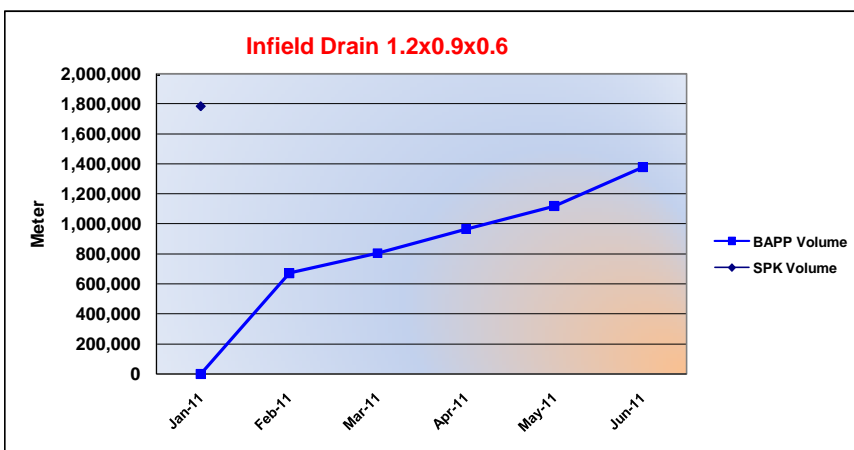


Month	Monthly Progress	Accumulated
Jan-11	-	-
Feb-11	671,001.00	671,001.00
Mar-11	132,594.00	803,595.00
Apr-11	161,915.00	965,510.00
May-11	151,404.00	1,116,914.00
Jun-11	260,381.00	1,377,295.00
<b>Total</b>	<b>1,377,295.00</b>	



# PT. RIMBA HARAPAN SAKTI

## CLAIM SUMMARY

Type of Work	SPK Vol ( Ha )	Progress	%
Underbrushing (Imas)	700.00	605.01	86.43%

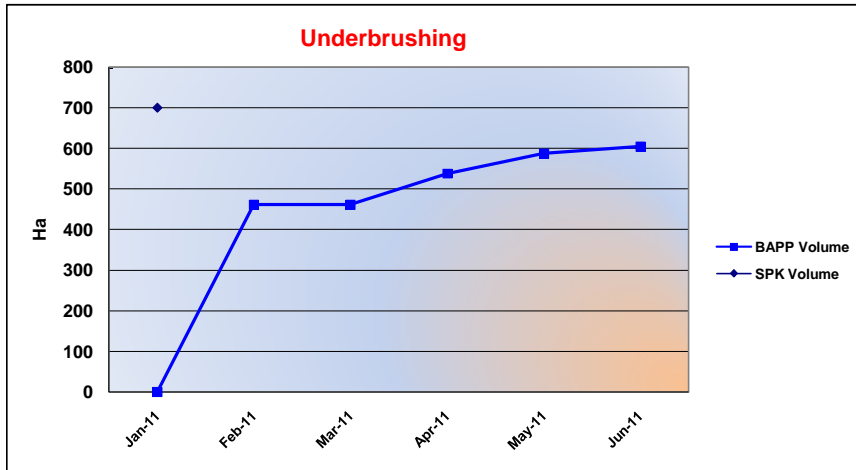

Month	Monthly Progress	Accumulated
Jan-11	-	-
Feb-11	461.42	461.42
Mar-11	-	461.42
Apr-11	76.92	538.34
May-11	49.17	587.51
Jun-11	17.50	605.01
<b>Total</b>	<b>605.01</b>	
