




CLAIM SUMMARY


Contract No. :
1. V/IJM P-P (Int)/51/10

Type of Work	Unit	SPK Vol	Jul - Aug 2010 Claim	September Claim	Total Claimed (Jul - Sep 2010)	%
Preliminary & General						
Site Supervision and Admin Staff	%	100.00	25.00	12.50	37.50	37.50%
Site Office and Temporary Buildings	%	100.00	100.00	-	100.00	100.00%
Preservation of Earth Slopes	%	100.00	-	-	-	0.00%
Site Clearing / Earthworks						
Site Clearing	%	100.00	95.00	-	95.00	95.00%
Bulk Earthworks for Mill Site	%	100.00	35.00	13.00	48.00	48.00%
Bulk Excavation	%	100.00	22.00	10.60	32.60	32.60%
Drains	%	100.00	-	-	-	0.00%
Temporary Earth Drain	%	100.00	-	-	-	0.00%
Turfing	%	100.00	-	-	-	0.00%

Preliminary & General

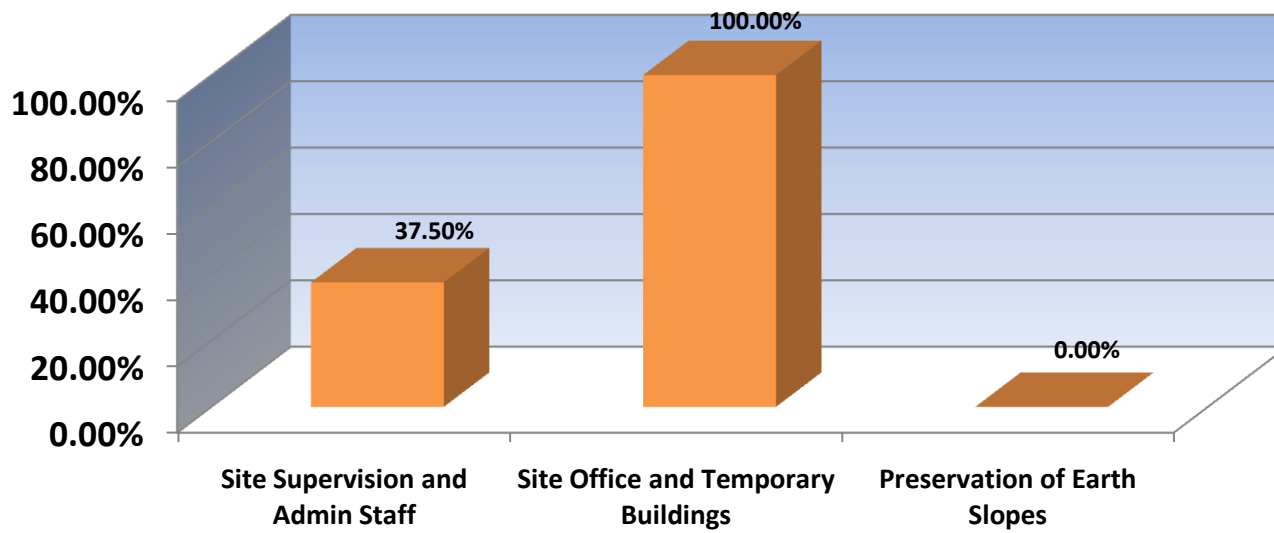

Site Clearing / Earthworks

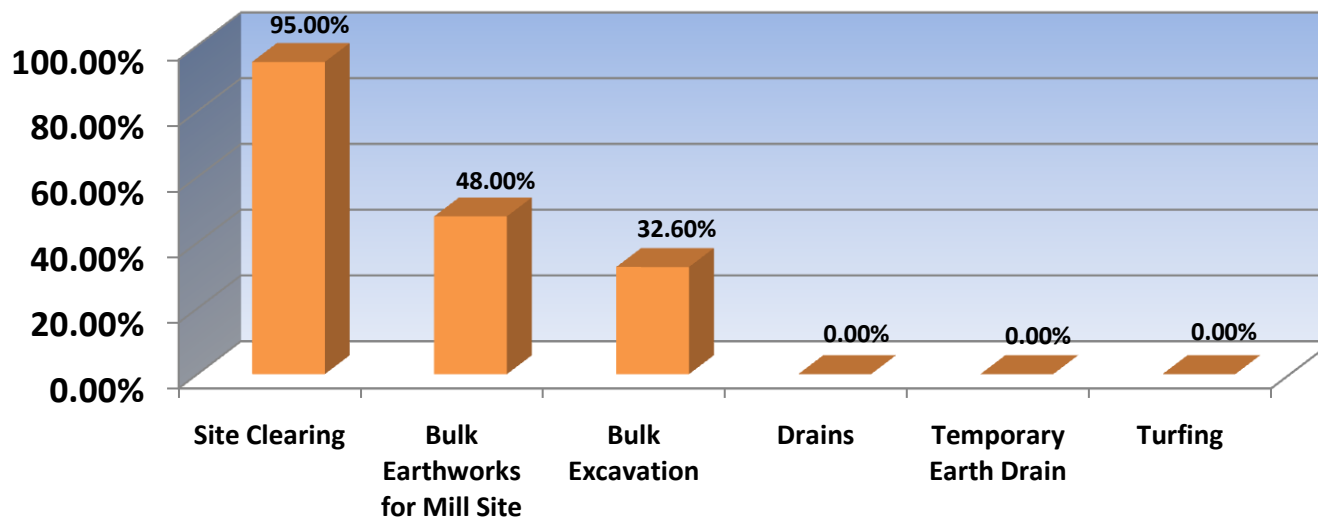




CLAIM SUMMARY


Chart & Detail Per Month

Type of Work	SPK Vol (%)	Progress	%
Site Supervision and Admin Staff	100.00	37.50	37.50%

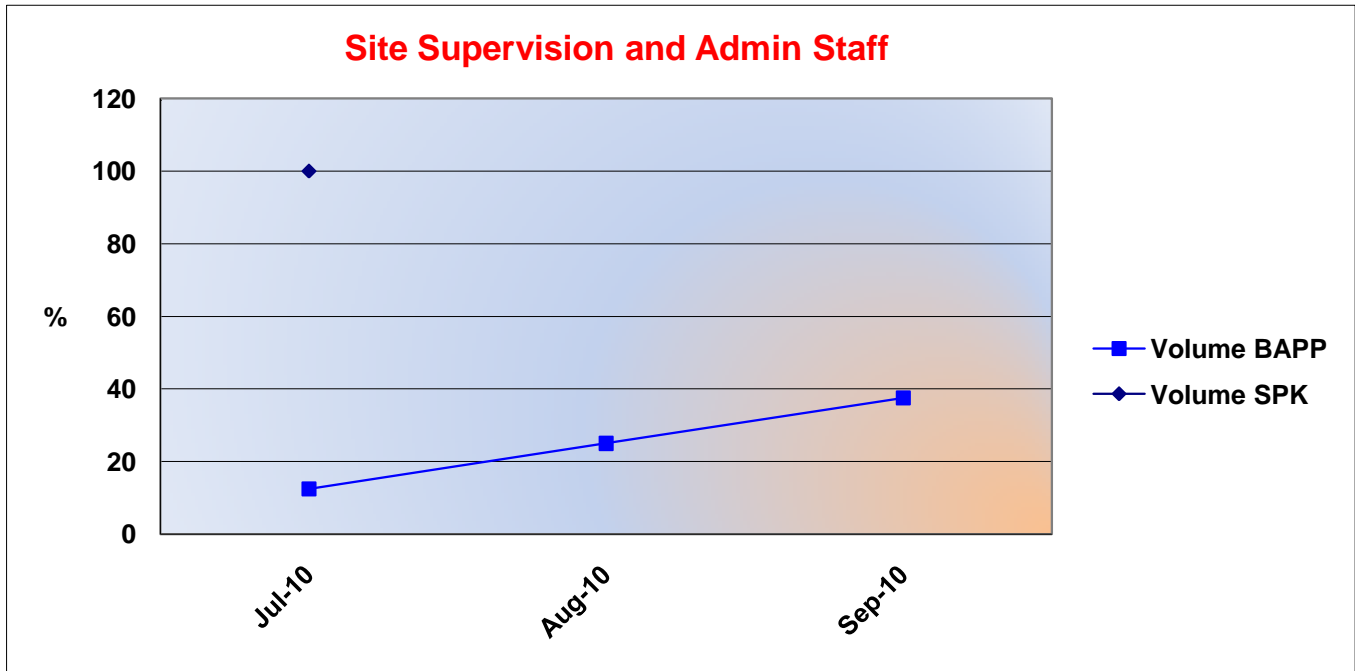


Month	Monthly Progress	Accumulated
Jul-10	12.50	12.50
Aug-10	12.50	25.00
Sep-10	12.50	37.50
	37.50	

Type of Work	SPK Vol (%)	Progress	%
Site Office and Temporary Buildings	100.00	100.00	100.00%

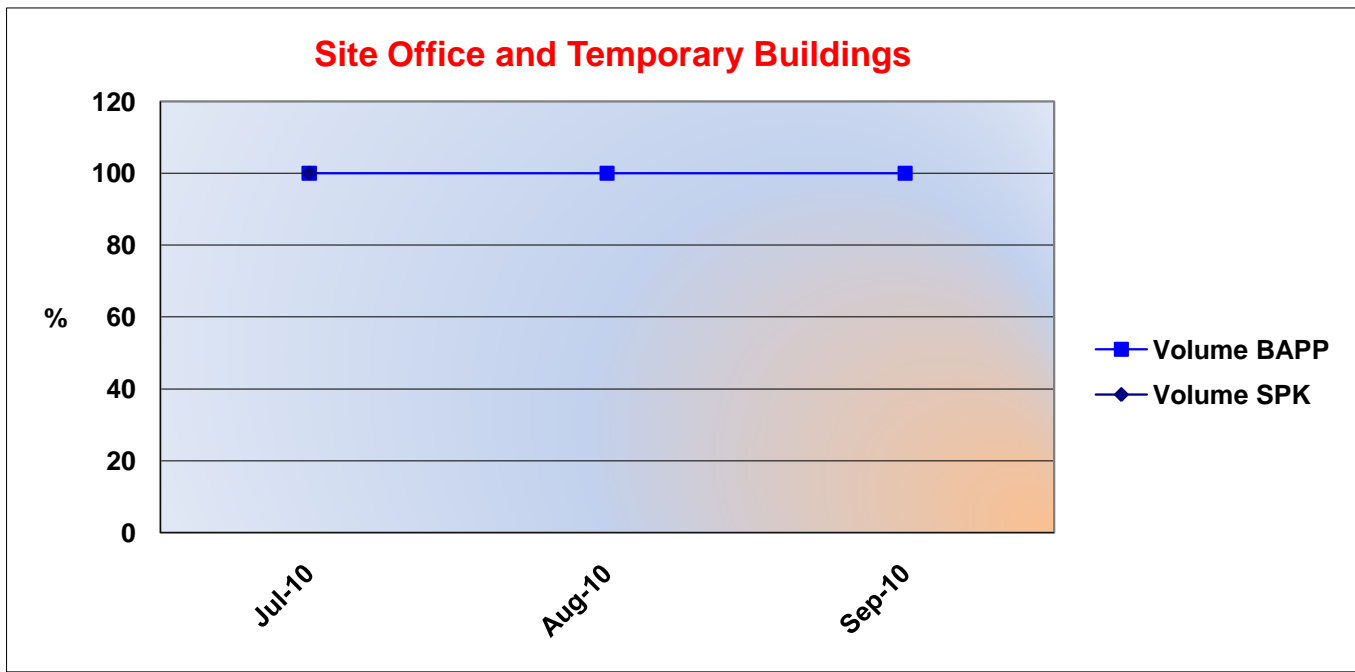

Month	Monthly Progress	Accumulated
Jul-10	100.00	100.00
Aug-10	-	100.00
Sep-10	-	100.00
	100.00	

Type of Work	SPK Vol (%)	Progress	%
Preservation of Earth Slopes	100.00	-	0.00%

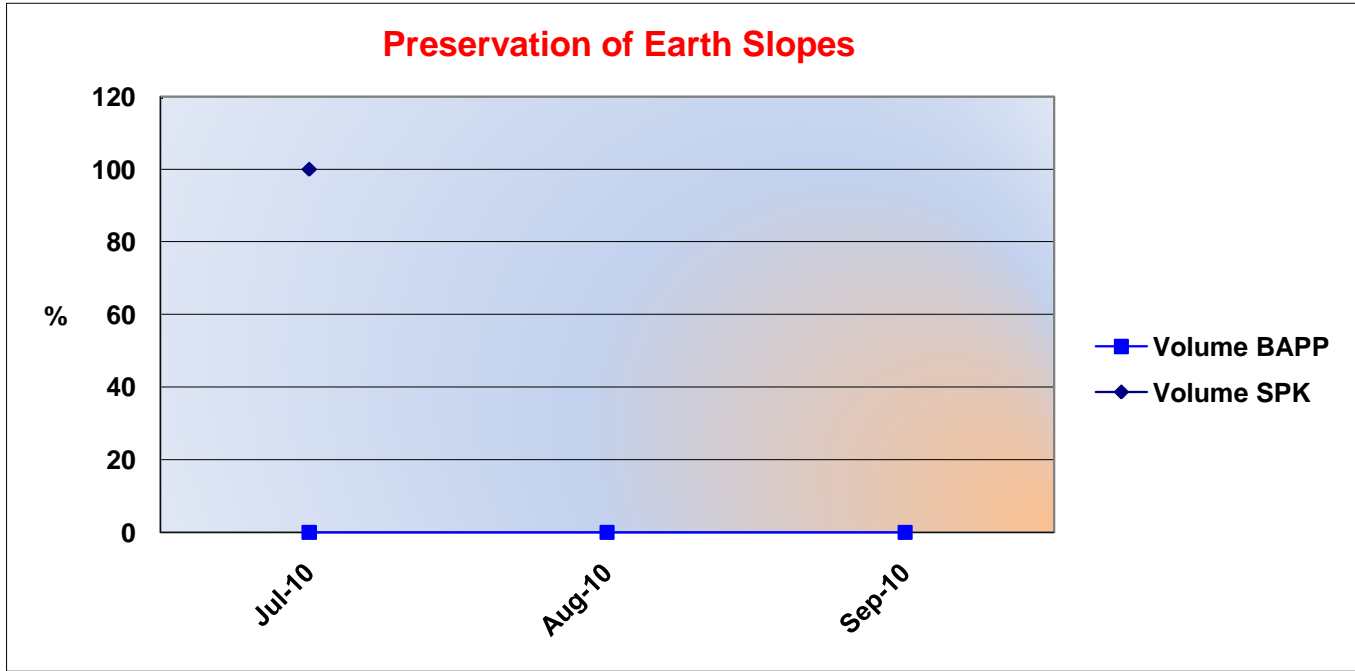


Month	Monthly Progress	Accumulated
Jul-10	-	-
Aug-10	-	-
Sep-10	-	-
	-	




CLAIM SUMMARY

Type of Work	SPK Vol (%)	Progress	%
Site Clearing	100.00	95.00	95.00%

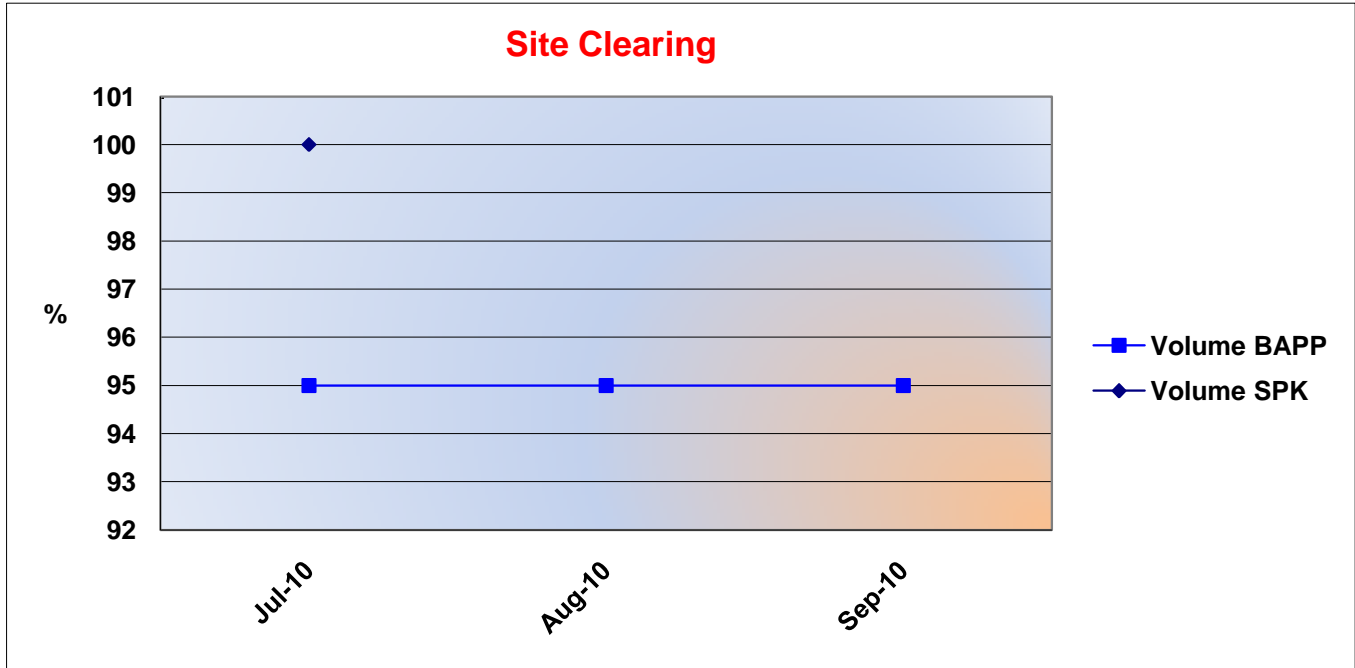


Month	Monthly Progress	Accumulated
Jul-10	95.00	95.00
Aug-10	-	95.00
Sep-10	-	95.00
	95.00	

Type of Work	SPK Vol (%)	Progress	%
Bulk Earthworks for Mill Site	100.00	48.00	48.00%

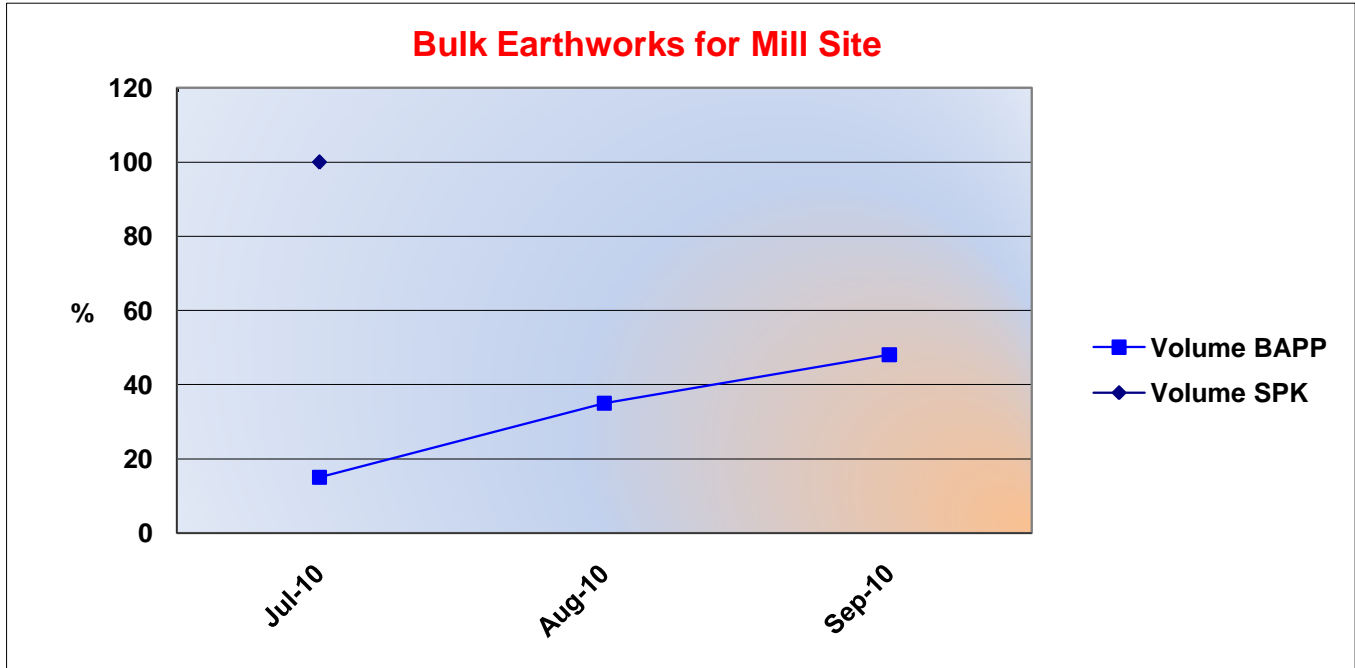

Month	Monthly Progress	Accumulated
Jul-10	15.00	15.00
Aug-10	20.00	35.00
Sep-10	13.00	48.00
	48.00	

Type of Work	SPK Vol (%)	Progress	%
Bulk Excavation	100.00	32.60	32.60%

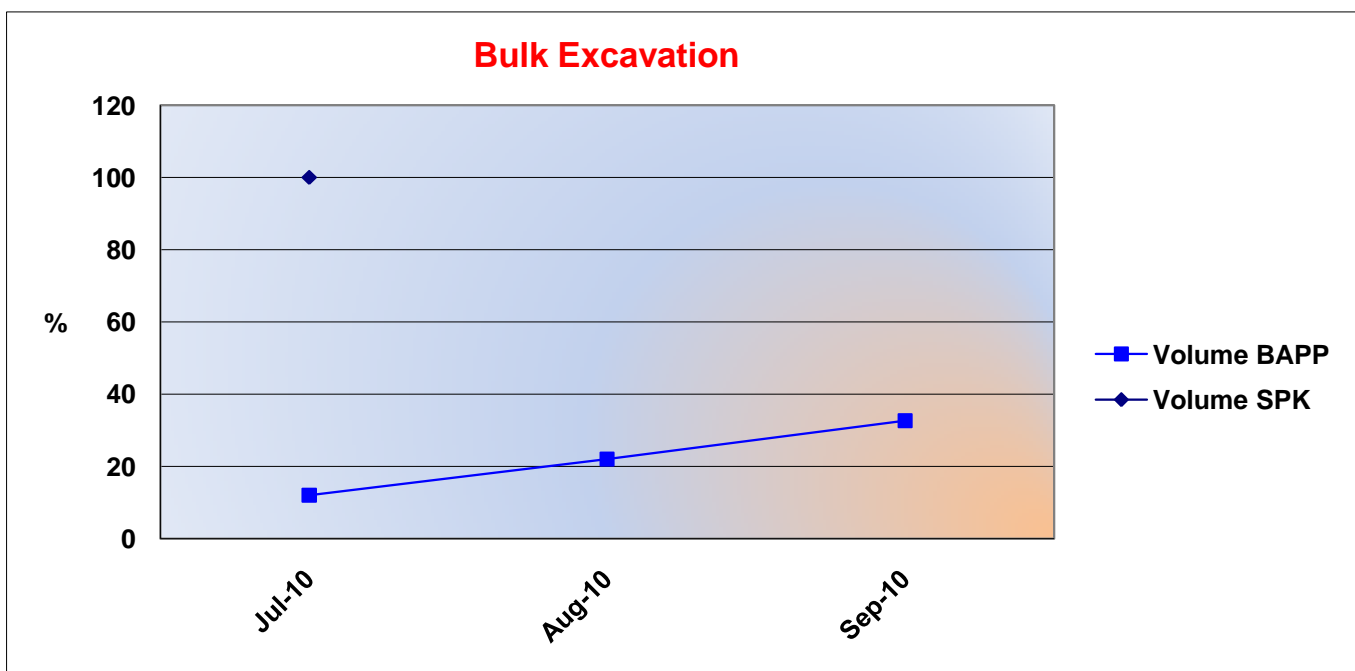


Month	Monthly Progress	Accumulated
Jul-10	12.00	12.00
Aug-10	10.00	22.00
Sep-10	10.60	32.60
	32.60	




CLAIM SUMMARY

Type of Work	SPK Vol (%)	Progress	%
Drains	100.00	-	0.00%

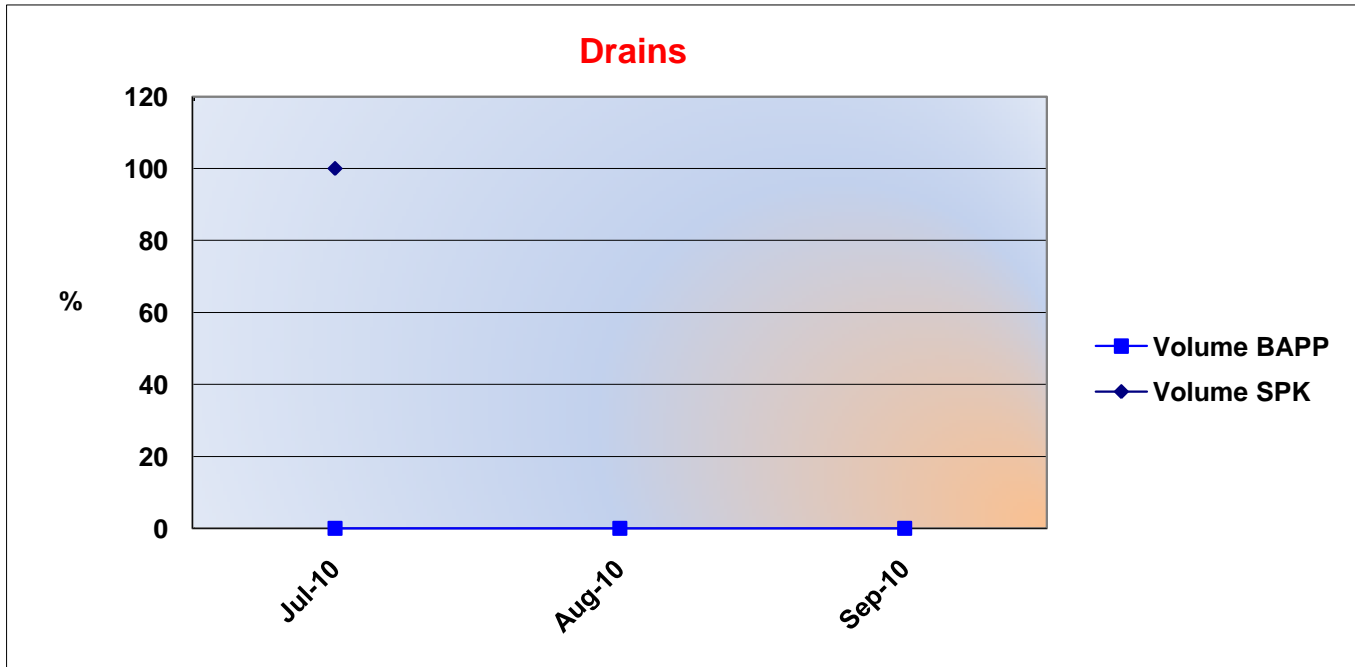


Month	Monthly Progress	Accumulated
Jul-10	-	-
Aug-10	-	-
Sep-10	-	-
	-	-

Type of Work	SPK Vol (%)	Progress	%
Temporary Earth Drain	100.00	-	0.00%

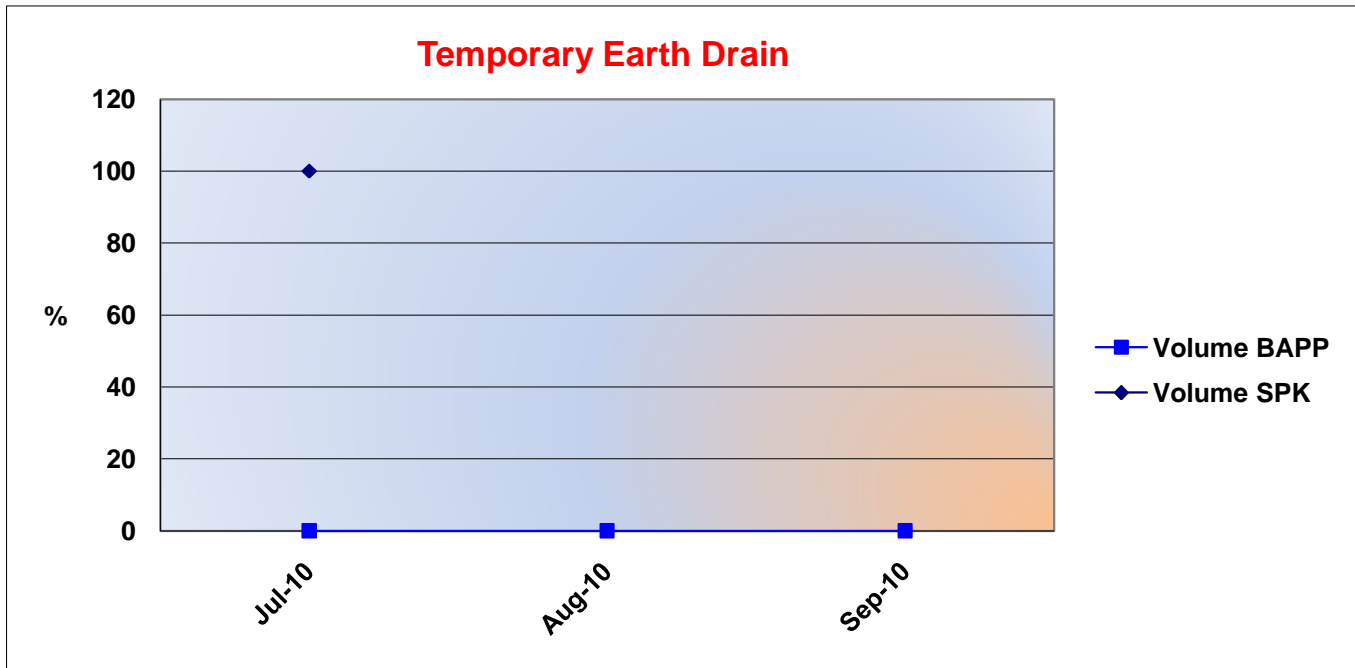

Month	Monthly Progress	Accumulated
Jul-10	-	-
Aug-10	-	-
Sep-10	-	-
	-	-

Type of Work	SPK Vol (%)	Progress	%
Turfing	100.00	-	0.00%

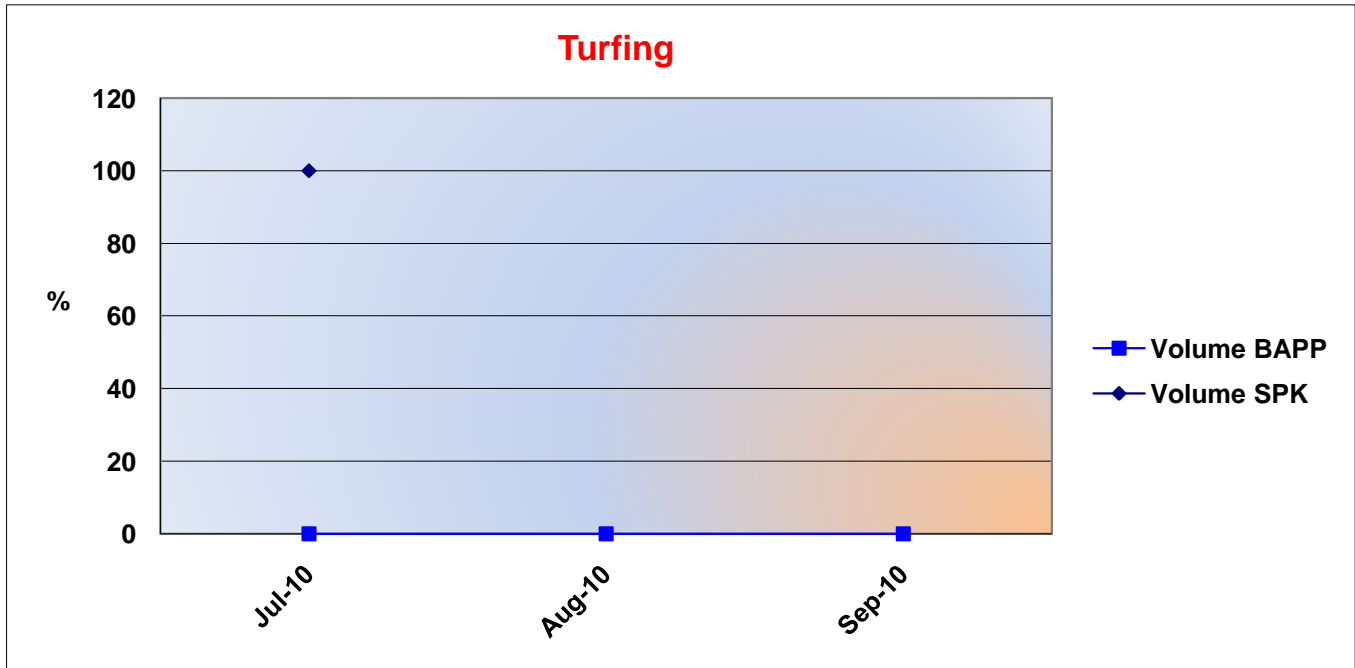

Month	Monthly Progress	Accumulated
Jul-10	-	-
Aug-10	-	-
Sep-10	-	-
	-	-




CLAIM SUMMARY

Contract No. :


1. V/IJM P-P (Int)/52/10

Type of Work	Unit	SPK Vol	Jul - Aug 2010 Claim	September Claim	Total Claimed (Jul - Sep 2010)	%
Preliminary & General						
Access to and within site	%	100.00	100.00	-	100.00	100.00%
Progress Report	%	100.00	25.00	12.50	37.50	37.50%
Progress Photographs	%	100.00	25.00	12.50	37.50	37.50%
Site Supervision and Admin Staff	%	100.00	25.00	12.50	37.50	37.50%
Workmen's Compensation or Insurance	%	100.00	100.00	-	100.00	100.00%
Site Office and Temporary Buildings	%	100.00	100.00	-	100.00	100.00%
Watching and Lighting	%	100.00	100.00	-	100.00	100.00%
Preservation of Earth Slopes	%	100.00	-	-	-	0.00%
As Built Drawings	%	100.00	-	-	-	0.00%
Generator Set 30 KVA	%	100.00	100.00	-	100.00	100.00%
Water Pump (6" Capacity)	%	100.00	-	-	-	0.00%
Site Clearing / Earthworks						
Site Clearing	%	100.00	100.00	-	100.00	100.00%
Bulk Earthworks for Reservoir Bund	%	100.00	0.30	-	0.30	0.30%
Bulk Earthworks for 20 M wide Main Access Road	%	100.00	23.30	10.50	33.80	33.80%
Bulk Excavation for Spillway	%	100.00	-	-	-	0.00%
Bulk Excavation for Base of Reservoir	%	100.00	100.00	-	100.00	100.00%
Excavate, Transport and Fill Clay Material to base of Reservoir	%	100.00	-	-	-	0.00%
Turfing	%	100.00	-	-	-	0.00%

Preliminary & General

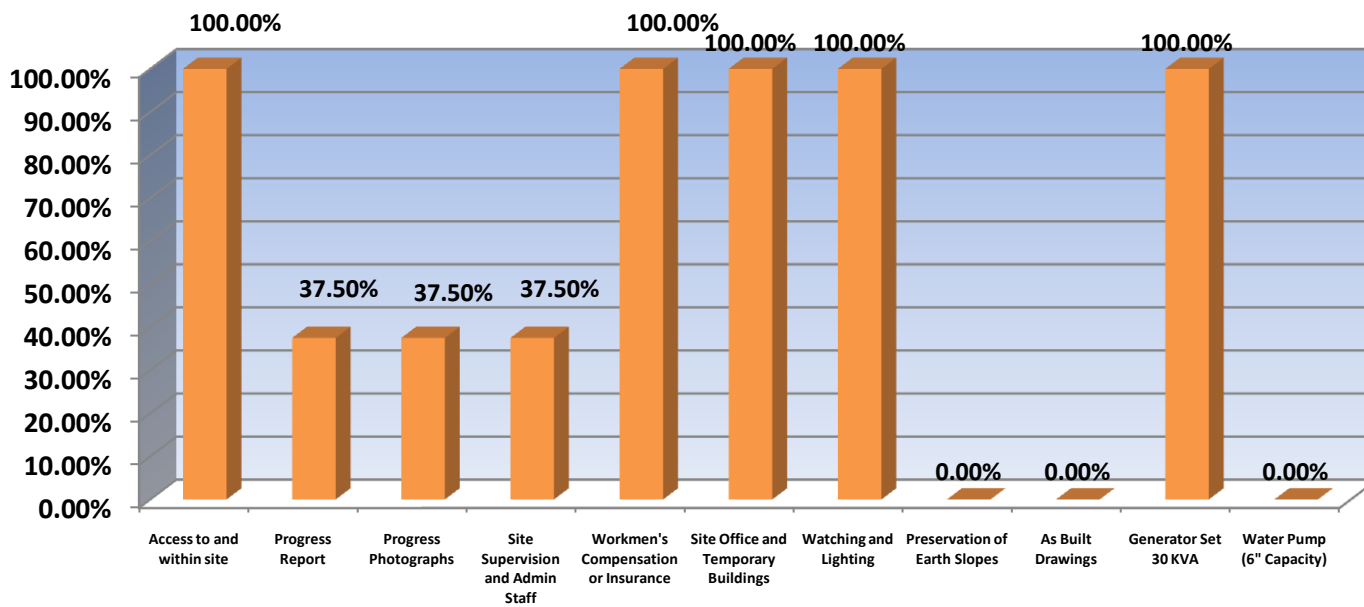

Site Clearing / Earthworks

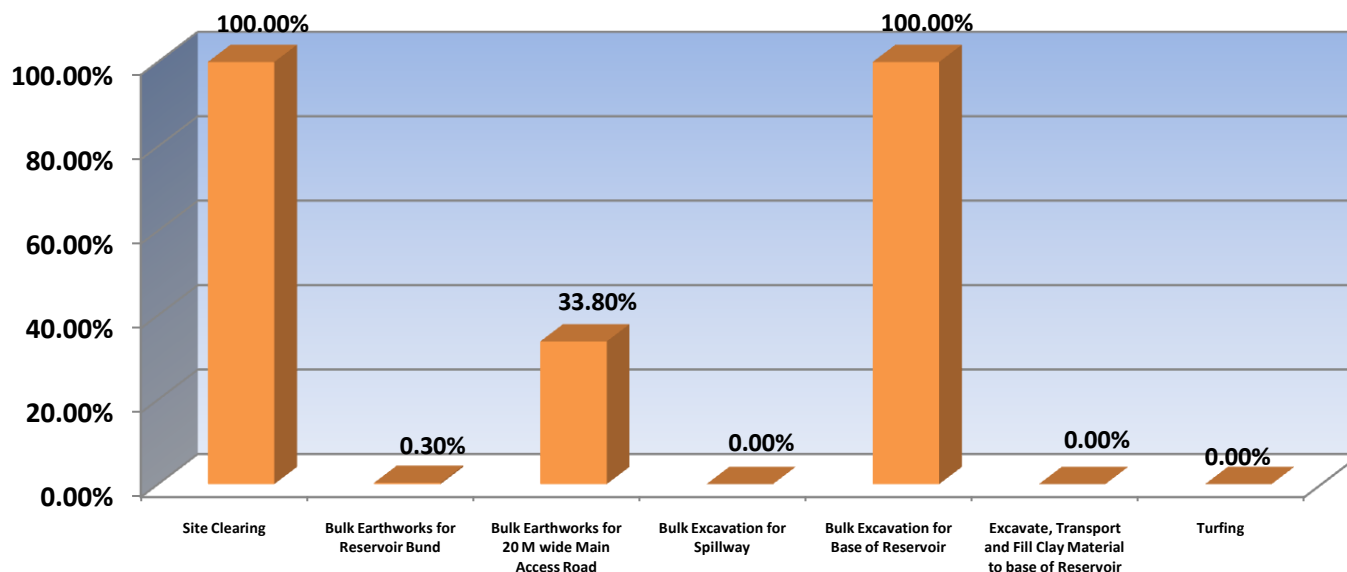




CLAIM SUMMARY


Chart & Detail Per Month

Type of Work	SPK Vol (%)	Progress	%
Access to and within site	100.00	100.00	100.00%

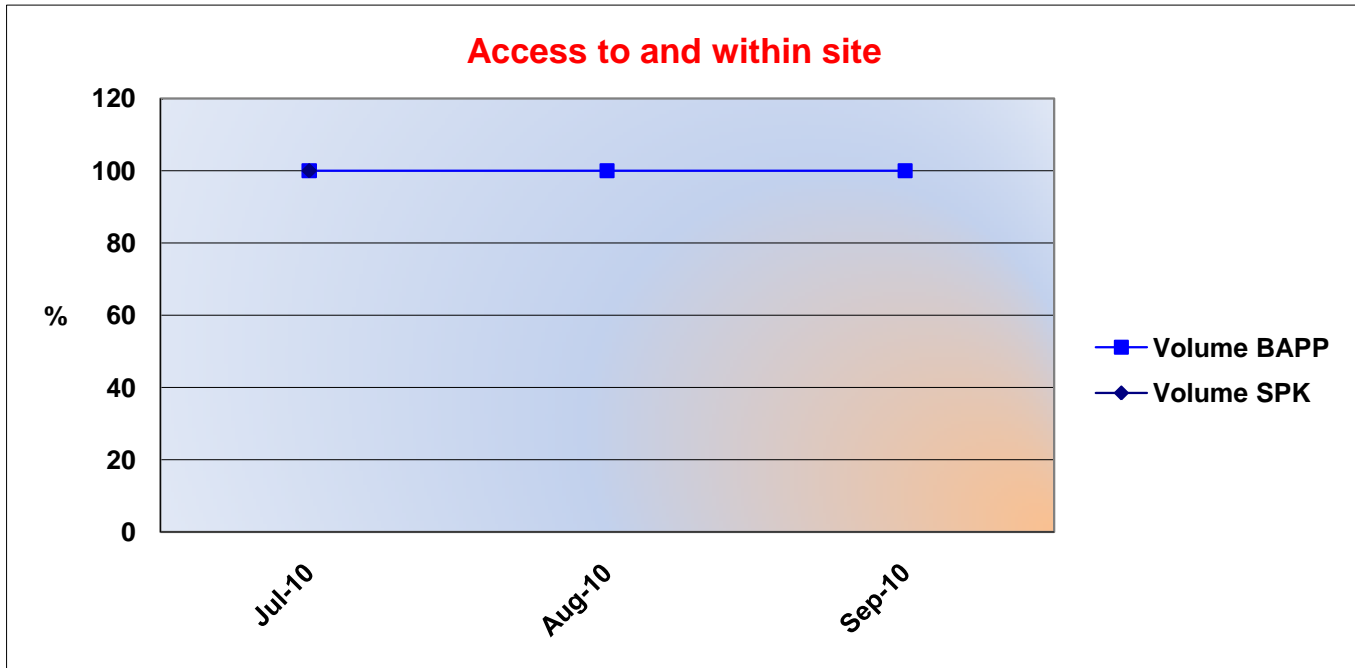


Month	Monthly Progress	Accumulated
Jul-10	100.00	100.00
Aug-10	-	100.00
Sep-10	-	100.00
	100.00	

Type of Work	SPK Vol (%)	Progress	%
Progress Report	100.00	37.50	37.50%

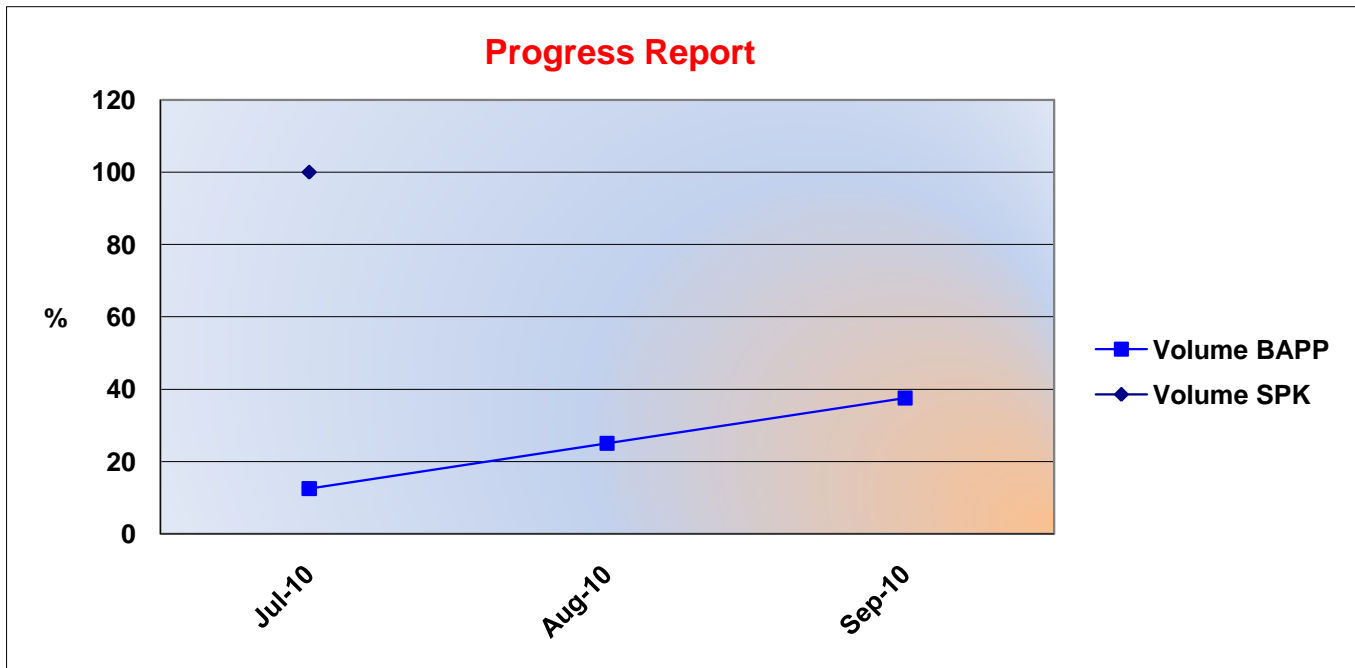

Month	Monthly Progress	Accumulated
Jul-10	12.50	12.50
Aug-10	12.50	25.00
Sep-10	12.50	37.50
	37.50	

Type of Work	SPK Vol (%)	Progress	%
Progress Photographs	100.00	37.50	37.50%

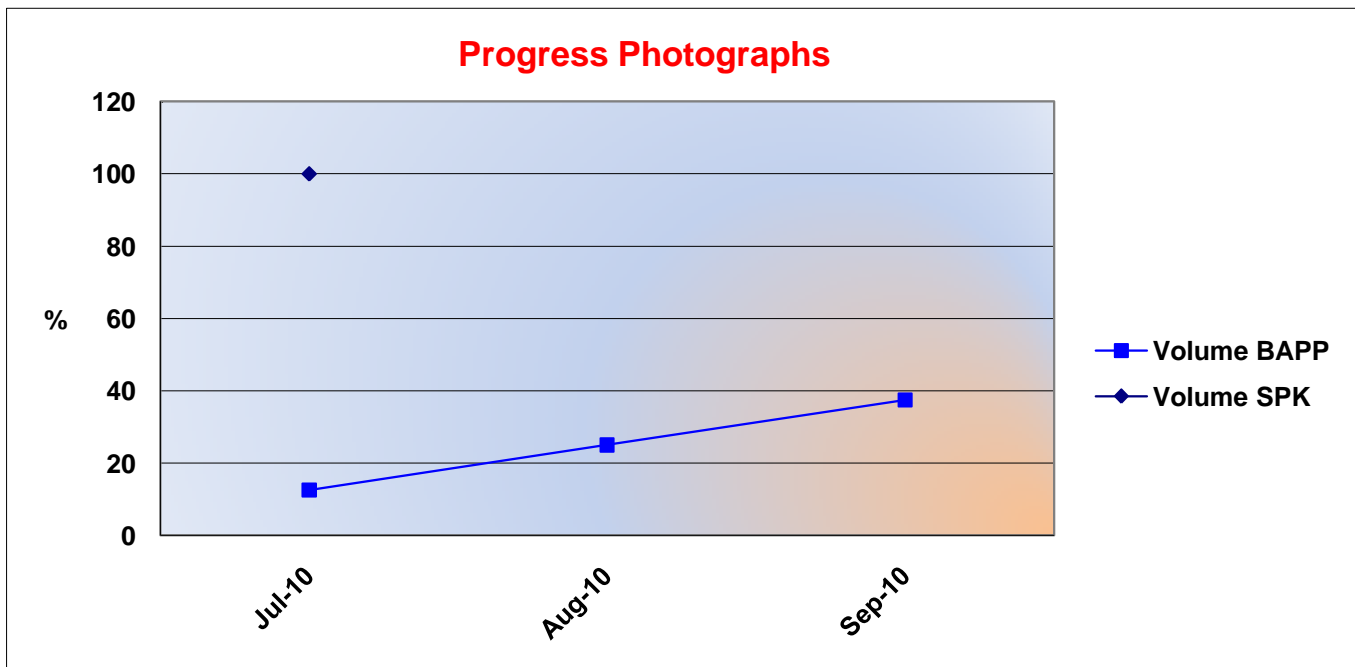


Month	Monthly Progress	Accumulated
Jul-10	12.50	12.50
Aug-10	12.50	25.00
Sep-10	12.50	37.50
	37.50	




CLAIM SUMMARY

Type of Work	SPK Vol (%)	Progress	%
Site Supervision and Admin Staff	100.00	37.50	37.50%

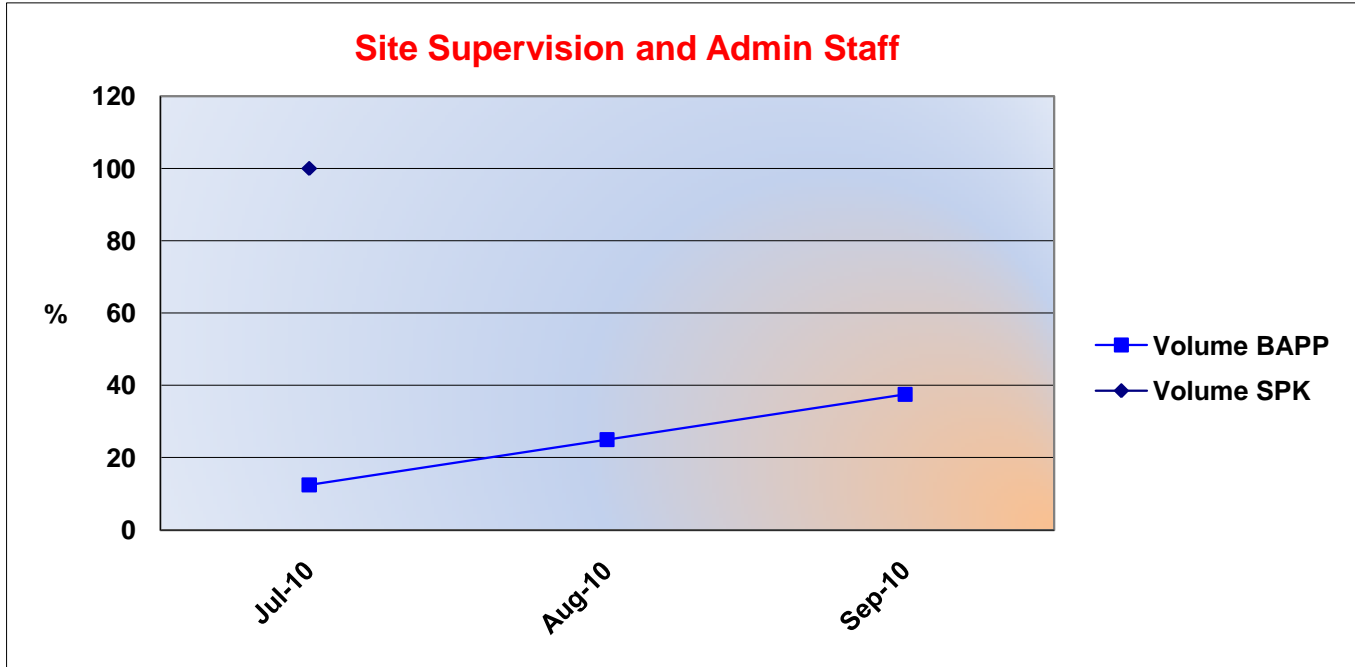


Month	Monthly Progress	Accumulated
Jul-10	12.50	12.50
Aug-10	12.50	25.00
Sep-10	12.50	37.50
	37.50	

Type of Work	SPK Vol (%)	Progress	%
Workmen's Compensation or Insurance	100.00	100.00	100.00%

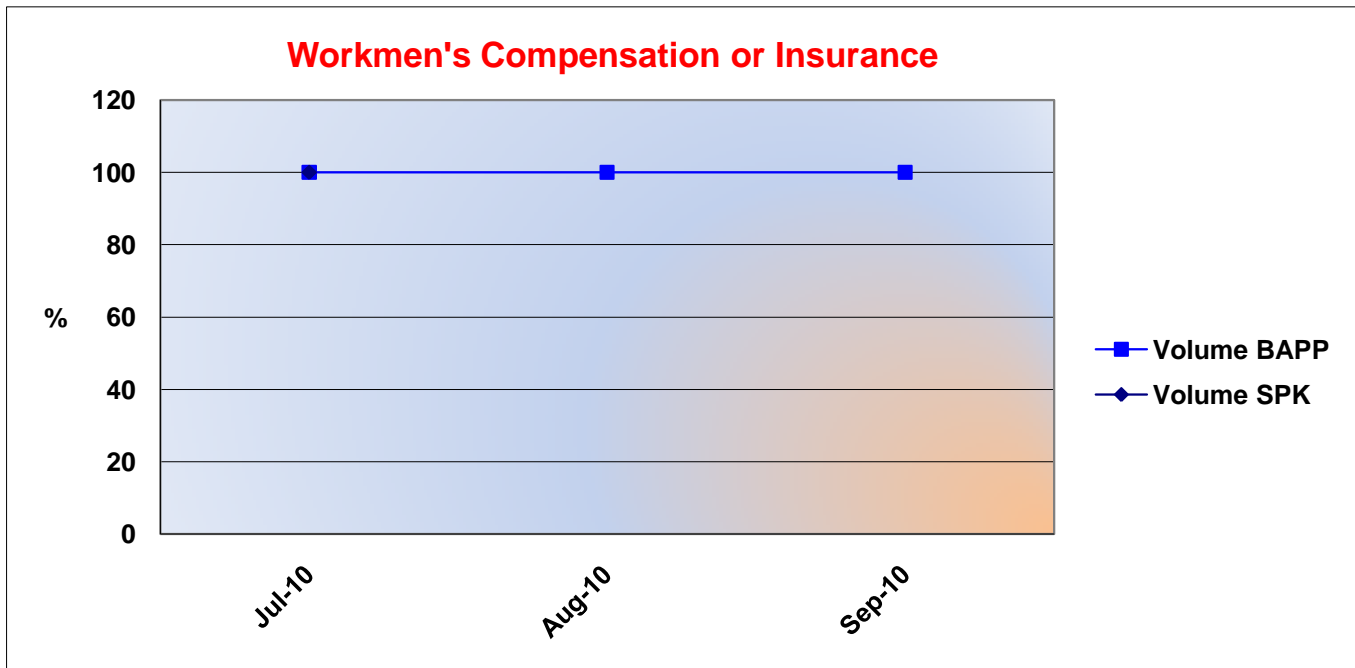

Month	Monthly Progress	Accumulated
Jul-10	100.00	100.00
Aug-10	-	100.00
Sep-10	-	100.00
	100.00	

Type of Work	SPK Vol (%)	Progress	%
Site Office and Temporary Buildings	100.00	100.00	100.00%

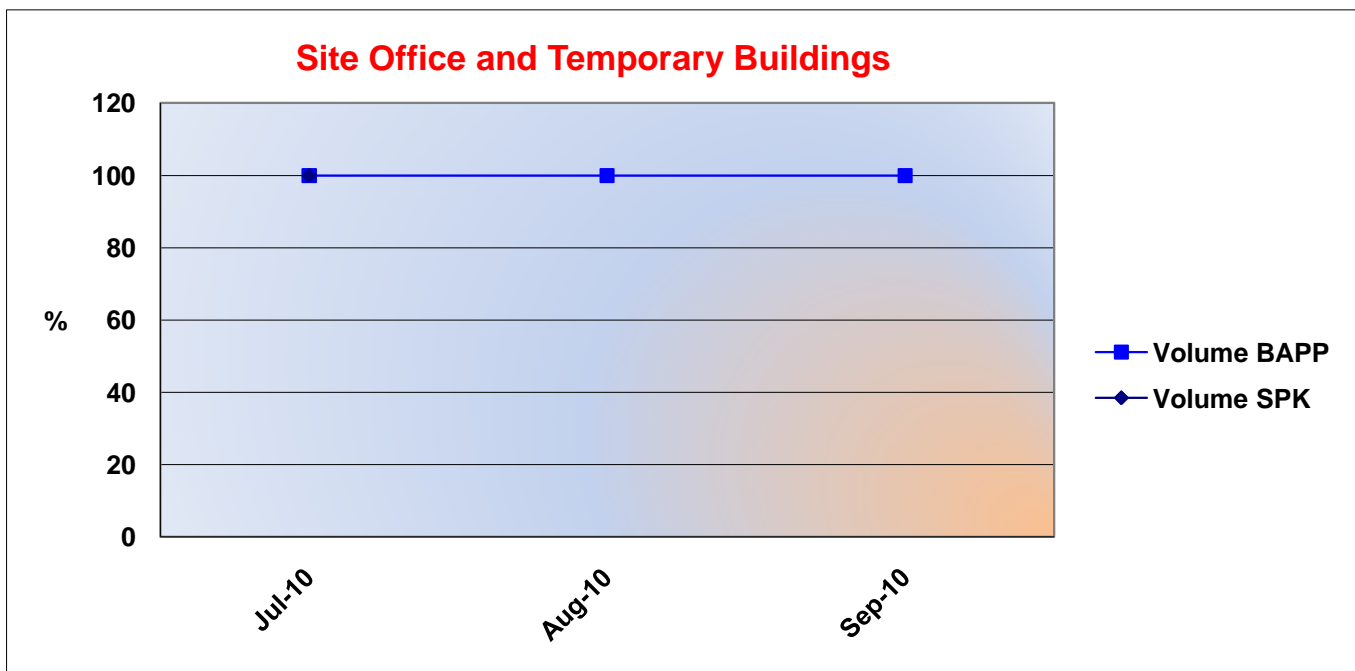


Month	Monthly Progress	Accumulated
Jul-10	100.00	100.00
Aug-10	-	100.00
Sep-10	-	100.00
	100.00	




CLAIM SUMMARY

Type of Work	SPK Vol (%)	Progress	%
Watching and Lighting	100.00	100.00	100.00%

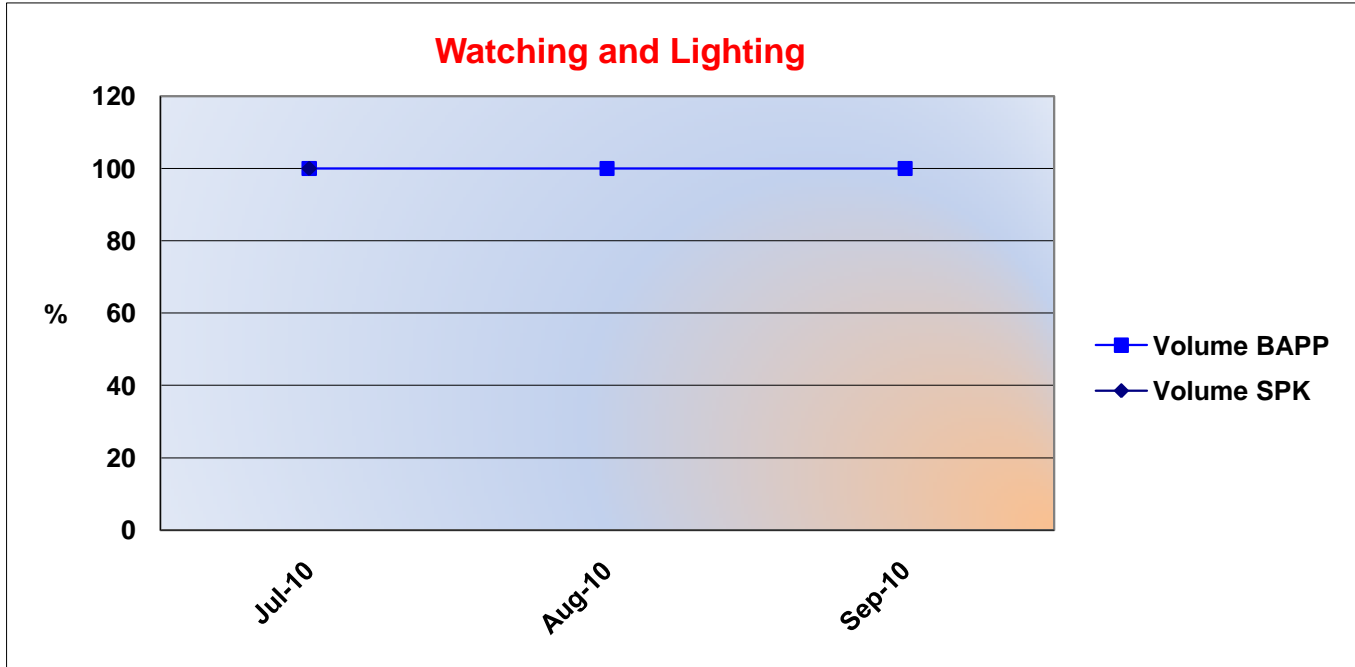


Month	Monthly Progress	Accumulated
Jul-10	100.00	100.00
Aug-10	-	100.00
Sep-10	-	100.00
	100.00	

Type of Work	SPK Vol (%)	Progress	%
Preservation of Earth Slopes	100.00	-	0.00%

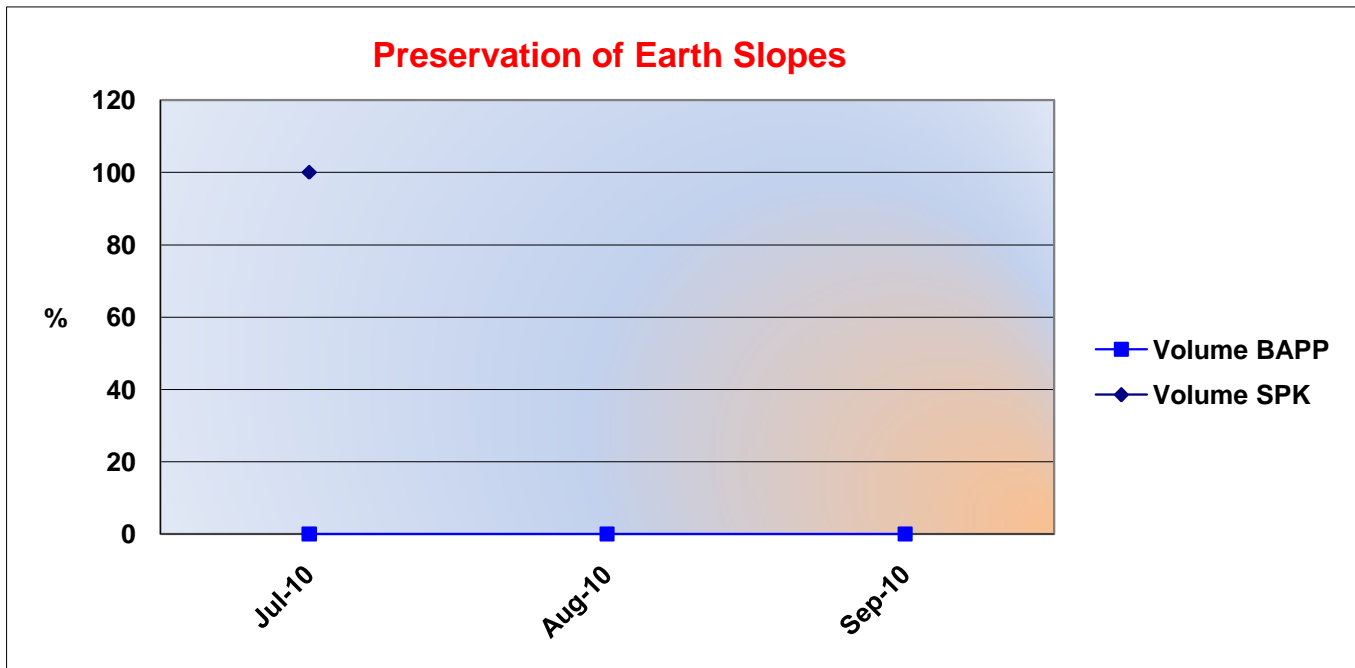

Month	Monthly Progress	Accumulated
Jul-10	-	-
Aug-10	-	-
Sep-10	-	-
	-	

Type of Work	SPK Vol (%)	Progress	%
As Built Drawings	100.00	-	0.00%

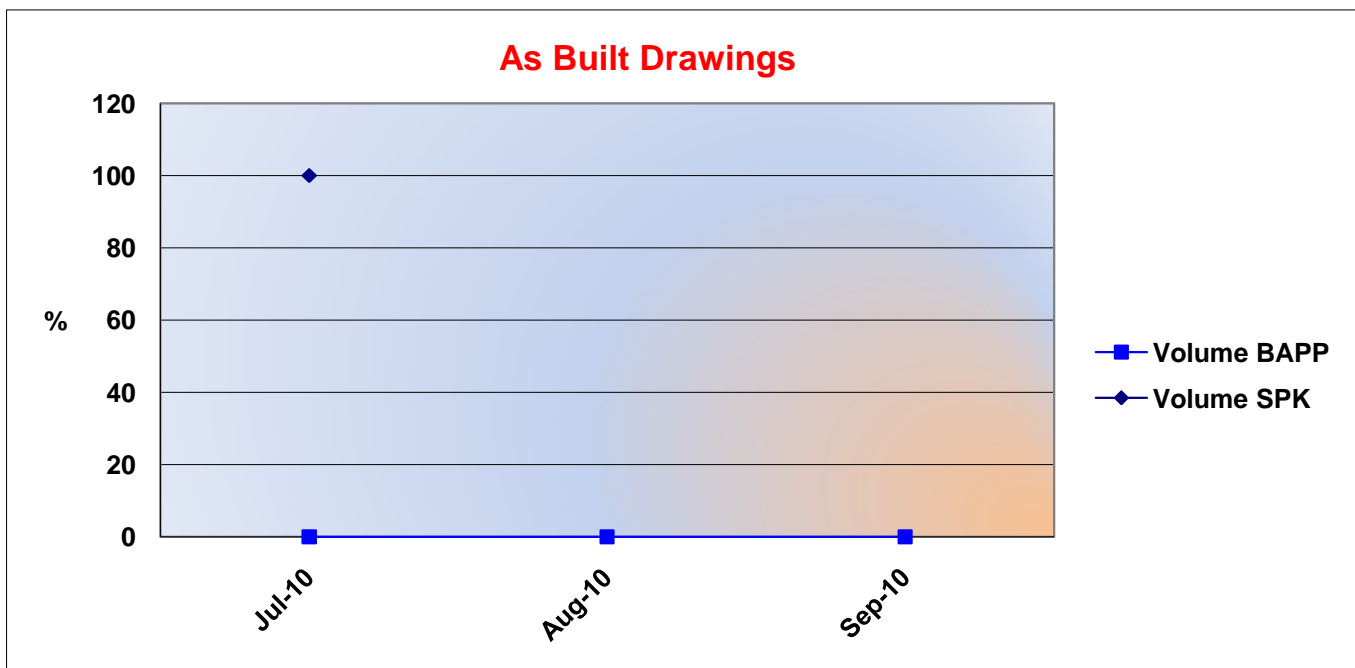


Month	Monthly Progress	Accumulated
Jul-10	-	-
Aug-10	-	-
Sep-10	-	-
	-	




CLAIM SUMMARY

Type of Work	SPK Vol (%)	Progress	%
Generator Set 30 KVA	100.00	100.00	100.00%

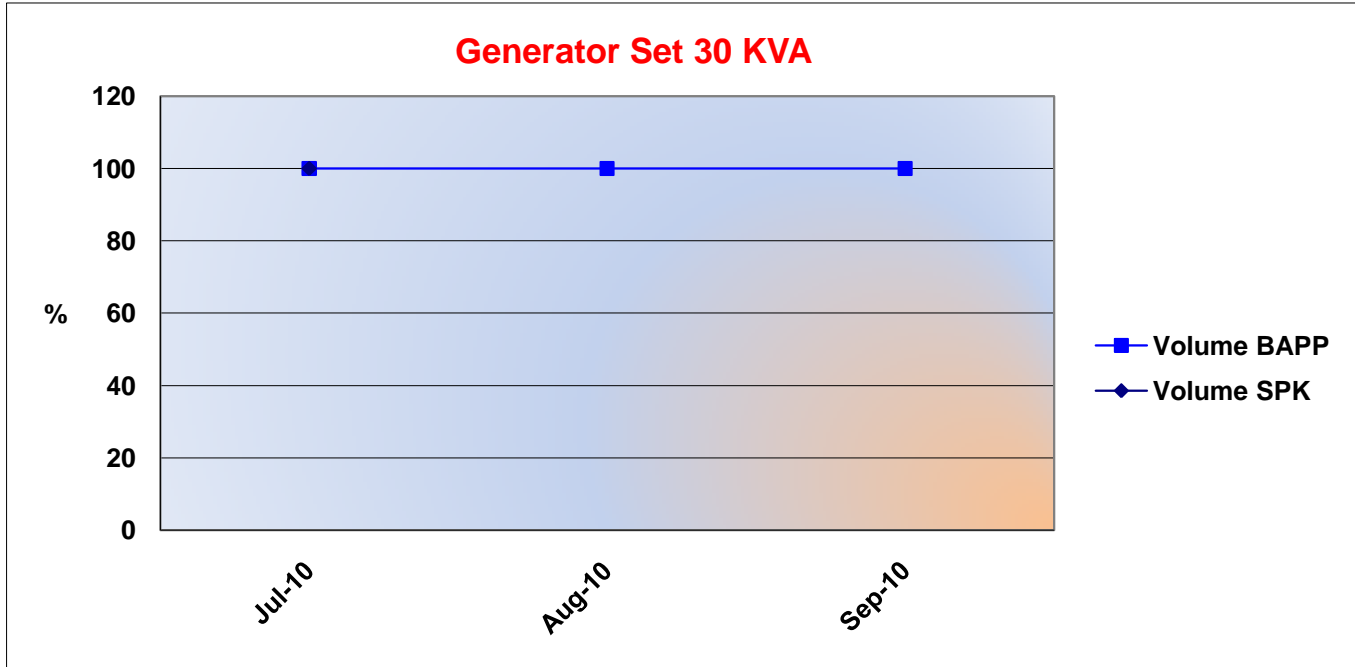


Month	Monthly Progress	Accumulated
Jul-10	100.00	100.00
Aug-10	-	100.00
Sep-10	-	100.00
	100.00	

Type of Work	SPK Vol (%)	Progress	%
Water Pump (6" Capacity)	100.00	100.00	0.00%

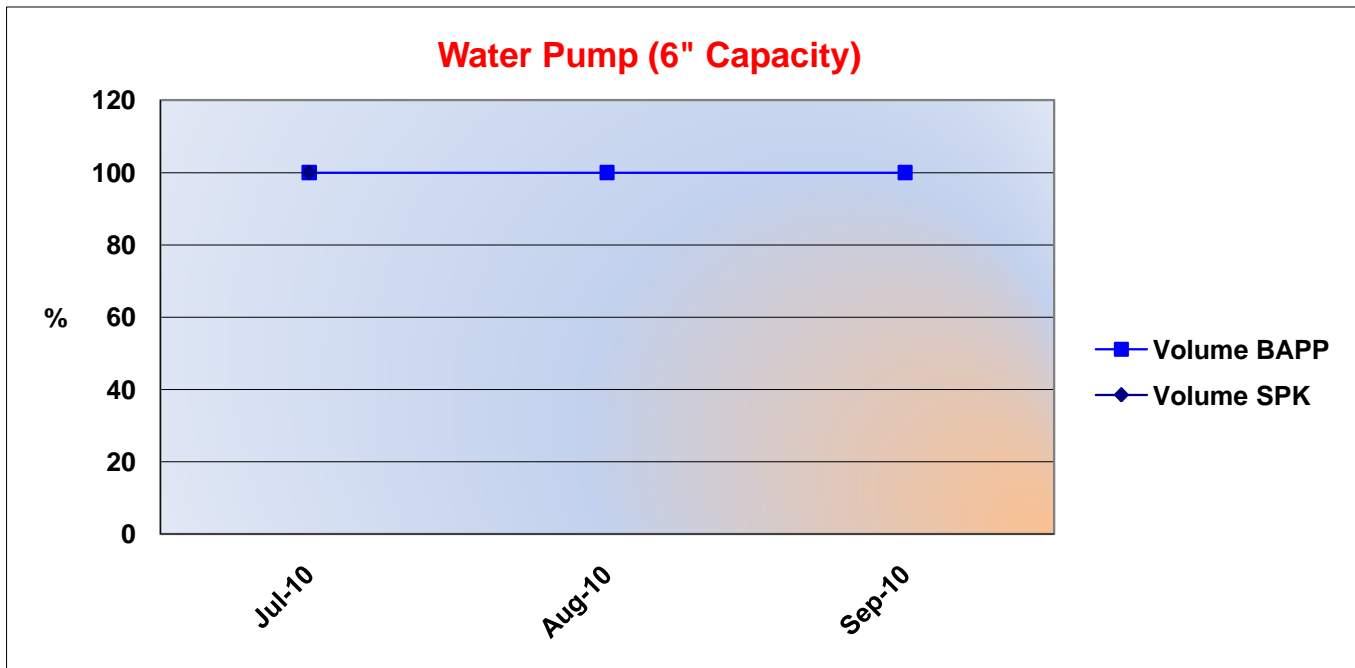

Month	Monthly Progress	Accumulated
Jul-10	100.00	100.00
Aug-10	-	100.00
Sep-10	-	100.00
	100.00	

Type of Work	SPK Vol (%)	Progress	%
Site Clearing	100.00	100.00	100.00%

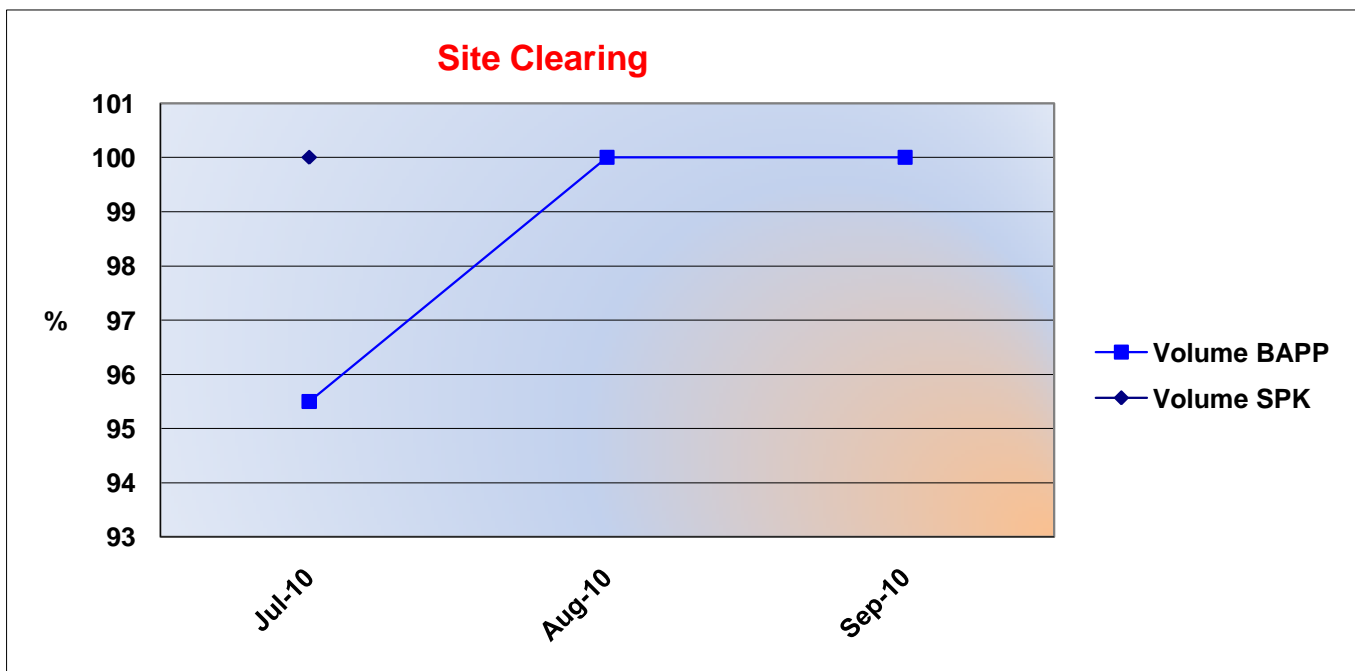


Month	Monthly Progress	Accumulated
Jul-10	95.50	95.50
Aug-10	4.50	100.00
Sep-10	-	100.00
	100.00	




CLAIM SUMMARY

Type of Work	SPK Vol (%)	Progress	%
Bulk Earthworks for Reservoir Bund	100.00	0.30	0.30%

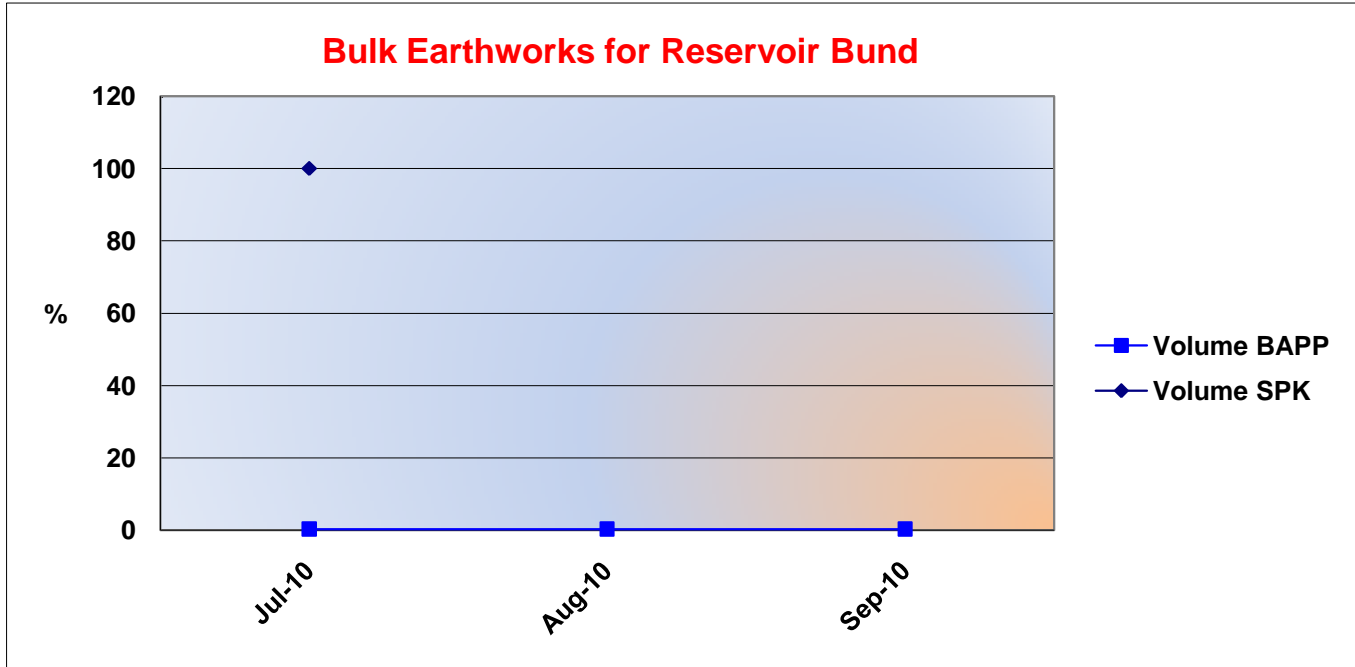


Month	Monthly Progress	Accumulated
Jul-10	0.30	0.30
Aug-10	-	0.30
Sep-10	-	0.30
	0.30	

Type of Work	SPK Vol (%)	Progress	%
Bulk Earthworks for 20 M wide Main Access Road	100.00	33.80	33.80%

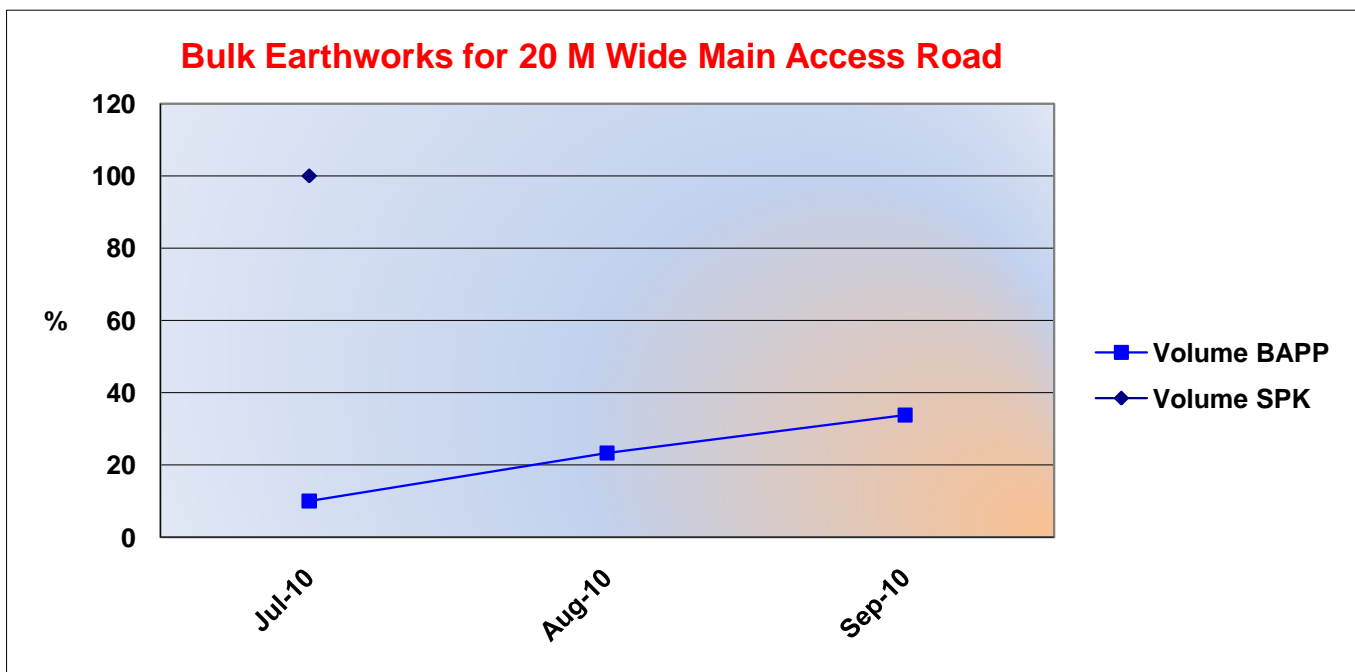

Month	Monthly Progress	Accumulated
Jul-10	10.00	10.00
Aug-10	13.30	23.30
Sep-10	10.50	33.80
	33.80	

Type of Work	SPK Vol (%)	Progress	%
Bulk Excavation for Spillway	100.00	-	0.00%

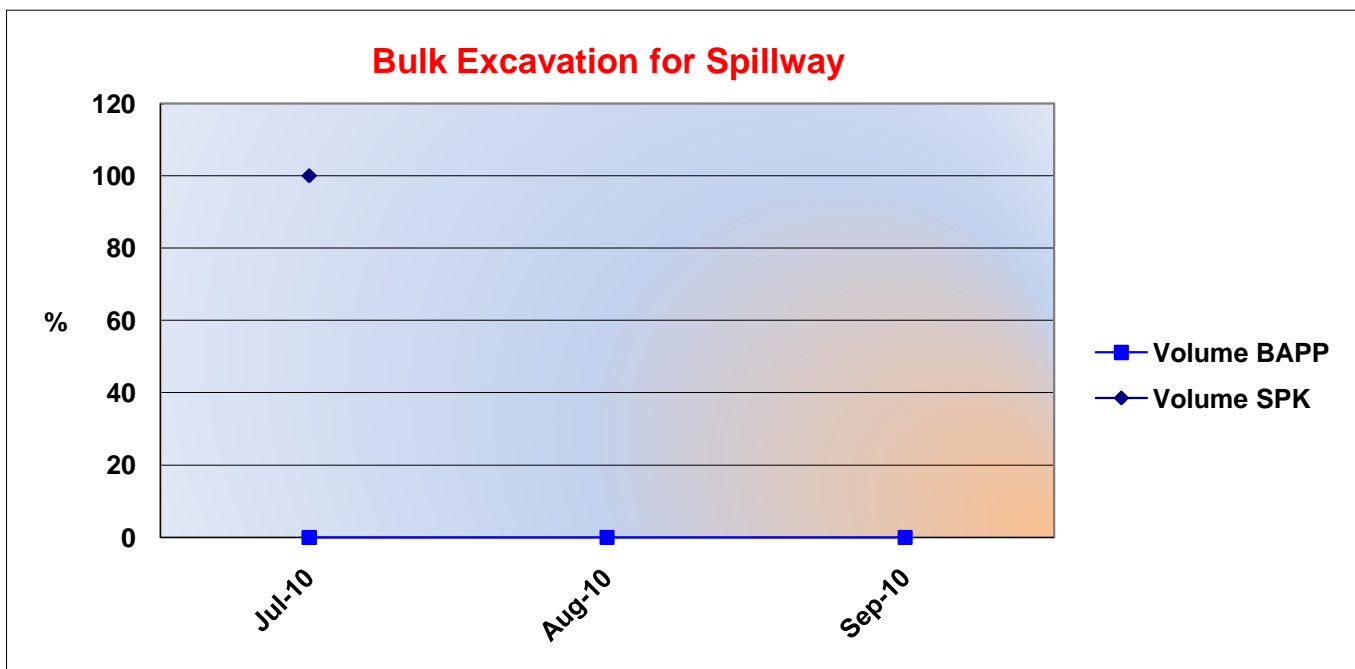


Month	Monthly Progress	Accumulated
Jul-10	-	-
Aug-10	-	-
Sep-10	-	-
	-	




CLAIM SUMMARY

Type of Work	SPK Vol (%)	Progress	%
Bulk Excavation for Base of Reservoir	100.00	100.00	100.00%

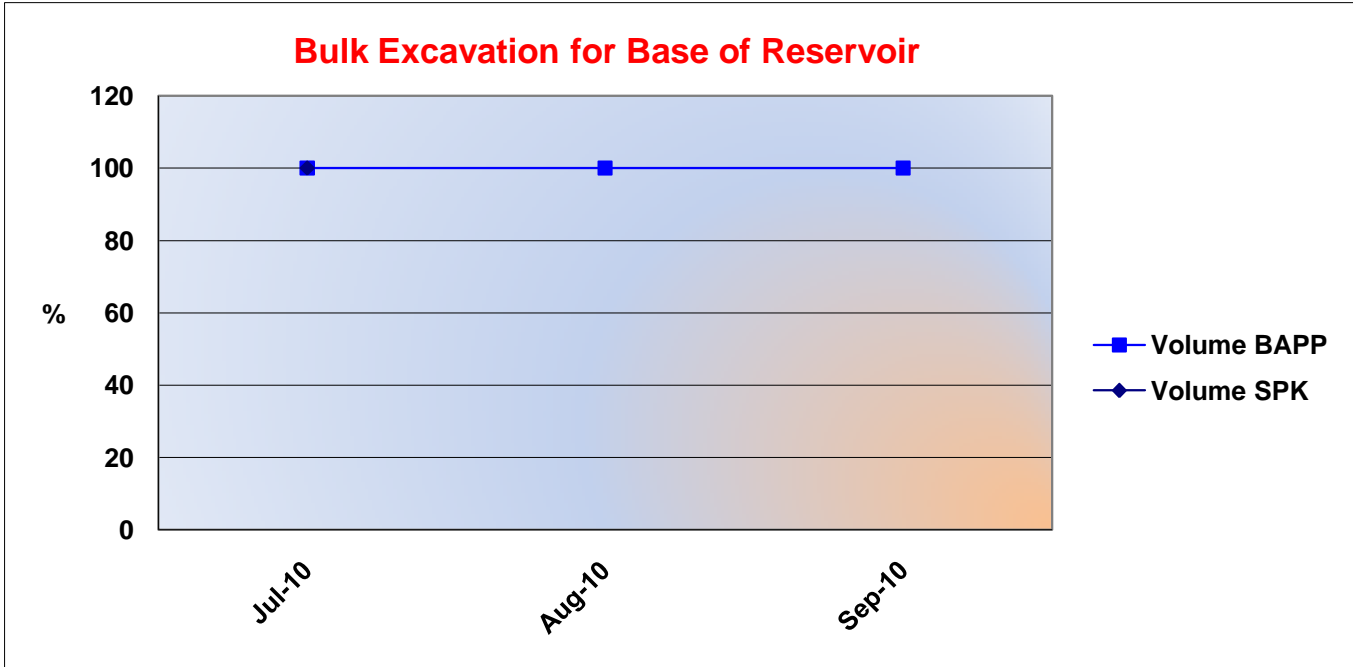


Month	Monthly Progress	Accumulated
Jul-10	100.00	100.00
Aug-10	-	100.00
Sep-10	-	100.00
	100.00	

Type of Work	SPK Vol (%)	Progress	%
Excavate, Transport and Fill Clay Material to base of Reservoir	100.00	-	0.00%

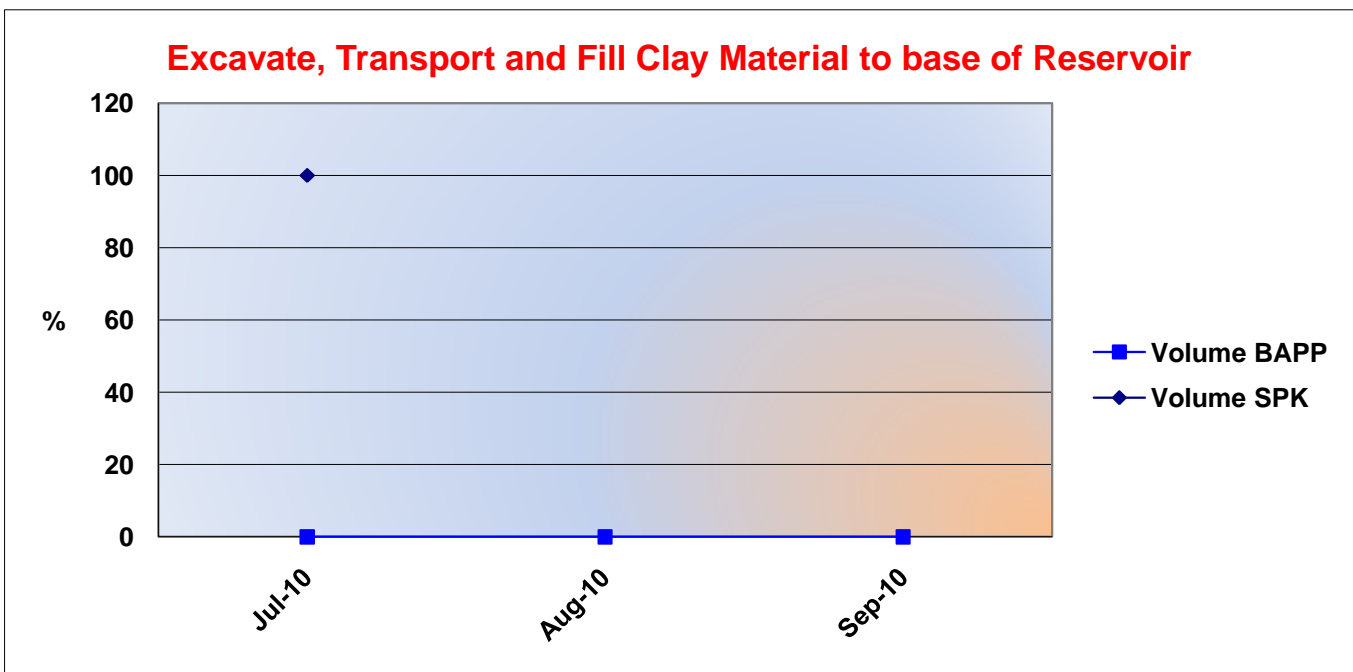

Month	Monthly Progress	Accumulated
Jul-10	-	-
Aug-10	-	-
Sep-10	-	-
	-	

Type of Work	SPK Vol (%)	Progress	%
Turfing	100.00	-	0.00%

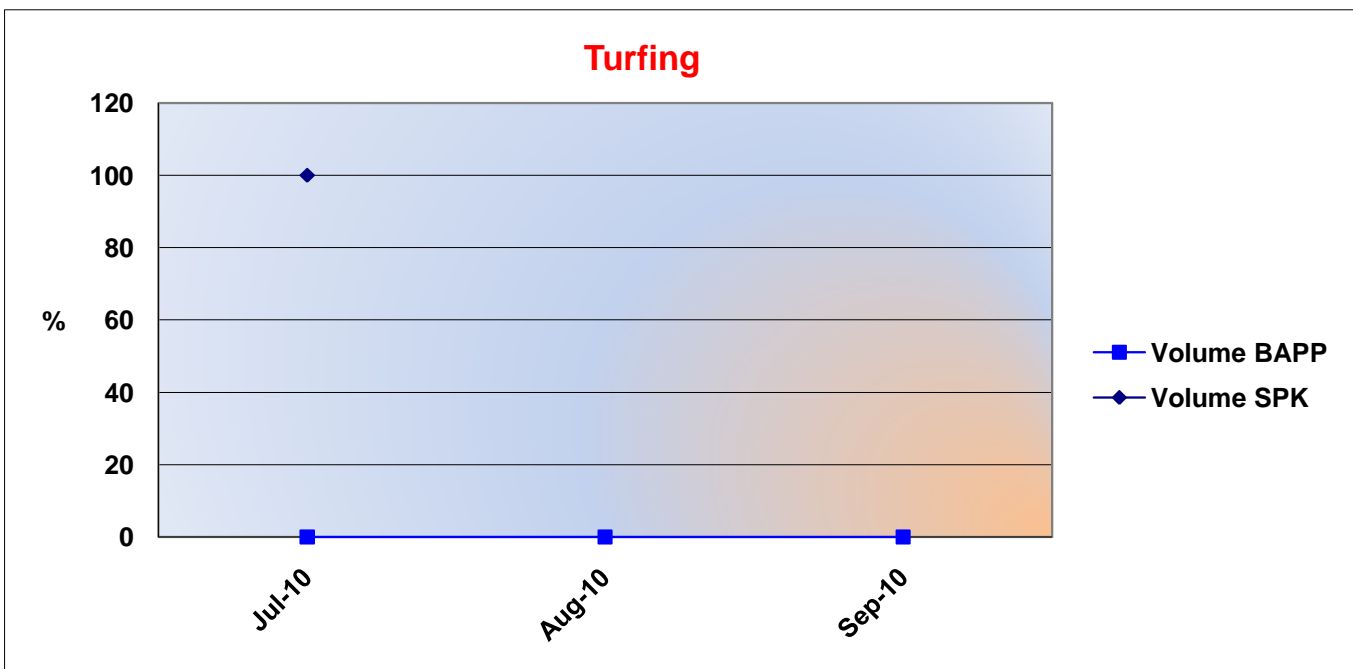

Month	Monthly Progress	Accumulated
Jul-10	-	-
Aug-10	-	-
Sep-10	-	-
	-	
