



PROGRESS REPORT - Kebun Khatulistiwa


KONTRAK NO :

1.KHTE/JKTO/04/09/013 - Jalur Tanam,BPRT & PJLN

2.KHTE/JKTO/04/09/012 - SWAB

Jenis Pekerjaan	Unit	Vol SPK 01 Apr '09 s.d 31 Des '12	Realisasi			%
			AKUMULASI S.D BULAN LALU	BAPP Desember 2012	S.D BAPP Desember 2012	
Bulldozer						
Jalur Tanam Darat	Ha	2.142,00	1.737,46	1,85	1.739,31	81,20%
Main Road Darat	Meter	16.565,00	11.026,06	-	11.026,06	66,56%
Collection Road Darat	Meter	54.566,00	37.161,06	-	37.161,06	68,10%
Jalan Contour	Meter	247.911,00	279.440,25	529,99	279.970,24	112,93%
Teras Contour	Meter	1.741.020,00	1.522.490,25	1.772,90	1.524.263,15	87,55%
Sewa Bulldozer	HM	-	13.126,10	43,00	13.169,10	
Excavator						
Jalur Tanam Rawa	Ha	1.237,00	1.597,70	8,22	1.605,92	129,82%
Parit 1 x 1 x 0,75	Meter	363.615,00	270.931,94	3.020,39	273.952,33	75,34%
Parit 2 x 2 x 1,5	Meter	71.183,00	94.182,06	374,96	94.557,02	132,84%
Parit 4 x 4 x 3	Meter	19.309,00	10.438,04	-	10.438,04	54,06%
Main Road Rawa	Meter	11.189,00	6.987,68	-	6.987,68	62,45%
Collection Road Rawa	Meter	36.859,00	19.729,96	-	19.729,96	53,53%
Gorong-gorong	Unit	-	120,00	-	120,00	
Jembatan 2 M	Unit	-	664,00	2,00	666,00	
Jembatan 4 M	Unit	-	47,00	-	47,00	
Jembatan 5-10 M	Unit	-	4,00	-	4,00	
Jembatan > 10 M	Unit	-	-	-	-	
Sewa Excavator	HM	-	13.010,10	196,00	13.206,10	

Pekerjaan Bulldozer

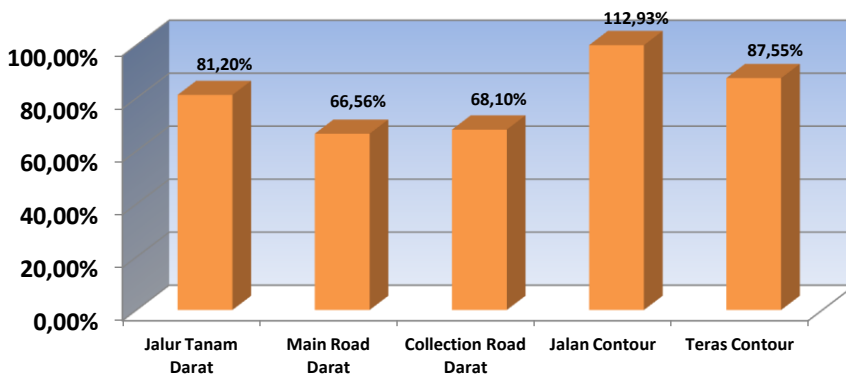

Pekerjaan Excavator

