



KOPBUN RAYA BATADUH


PROGRESS REPORT - Kenari Plasma

KONTRAK NO :

1. 069/KNRA/LOA/12/2013
2. 069/KNRA/JKTO/12/2013-PEMBUKAAN LAHAN
3. 069/KNRA/JKTO/12/2013-SWAB LP
4. 069/KNRA/JKTO/12/2013-IMAS TUMBANG

Jenis Pekerjaan	Unit	Vol SPK 1 Jan '13 s.d. 31 Des '14	Realisasi			%
			AKUMULASI S.D BULAN LALU	BAPP Feb 2014	S.D BAPP Feb 2014	
Bulldozer						
Jalur Tanam Darat	Ha	196,00	-	7,73	7,73	3,94%
Main Road Darat	Meter	8.358,00	-	1.652,62	1.652,62	19,77%
Collection Road Darat	Meter	3.847,00	-	642,58	642,58	16,70%
Jalan Contour	Meter	13.570,00	-	-	-	0,00%
Teras Contour	Meter	131.570,00	-	-	-	0,00%
Sewa Bulldozer	HM		-	143,00	143,00	
Excavator						
Jalur Tanam Rawa	Ha	42,00	-	4,01	4,01	9,55%
Parit 1 x 1 x 0,75	Meter	17.129,52	-	1.661,15	1.661,15	9,70%
Parit 2 x 2 x 1,5	Meter	9.611,46	-	1.311,67	1.311,67	13,65%
Parit 4 x 4 x 3	Meter	431,00	-	-	-	0,00%
Main Road Rawa	Meter	70,00	-	-	-	0,00%
Collection Road Rawa	Meter	223,24	-	-	-	0,00%
Gorong-gorong	Unit		-	-	-	
Jembatan 2 M	Unit		-	2,00	2,00	
Jembatan 4 M	Unit		-	1,00	1,00	
Jembatan 5-10 M	Unit		-	-	-	
Jembatan > 10 M	Unit		-	-	-	
Sewa Excavator	HM		-	118,00	118,00	
Imas Tumbang	Ha	200,00	-	-	-	0,00%

Pekerjaan Bulldozer

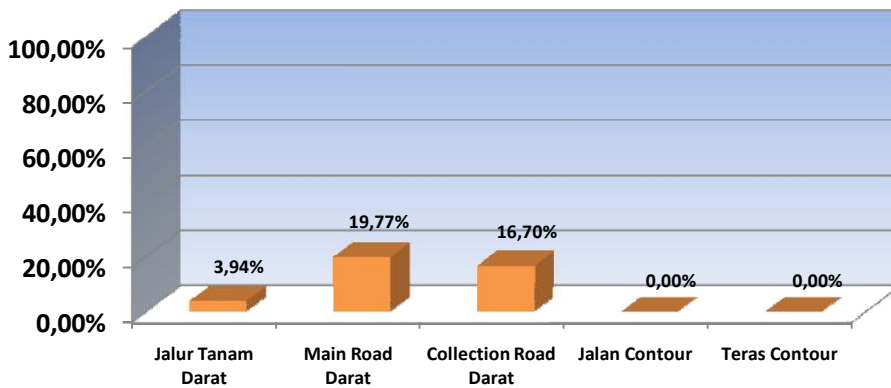

Pekerjaan Excavator

