




PROGRESS REPORT - Kebun Sungai Besar

KONTRAK NO :

1. 180/SBSE/LOA/12/2013
2. 180/SBSE/JKTO/12/2013-PEMBUKAAN LAHAN, SWAB LP
3. 030/SBSE/JKTO/01/2014-PUNCHER & COMPACTION
4. 005/SBSE/JKTO/01/2014-GAMBANGAN

Jenis Pekerjaan	Unit	Vol SPK 1 Jan '14 s.d. 31 Des '14	Realisasi			%
			AKUMULASI S.D BULAN LALU	BAPP Feb 2014	S.D BAPP Feb 2014	
Bulldozer						
Jalur Tanam Darat	Ha	345,00	-	-	-	0,00%
Main Road Darat	Meter	1.326,00	-	-	-	0,00%
Collection Road Darat	Meter	4.368,00	-	-	-	0,00%
Jalan Contour	Meter	24.725,00	-	-	-	0,00%
Teras Contour	Meter	239.725,00	-	-	-	0,00%
Sewa Buldozer	HM		-	30,00	30,00	
Excavator						
Jalur Tanam Rawa	Ha	155,00	22,91	64,58	87,49	56,45%
Parit 1 x 1 x 0,75	Meter	56.675,00	3.427,63	1.371,73	4.799,36	8,47%
Parit 2 x 2 x 1,5	Meter	8.658,00	-	568,00	568,00	6,56%
Parit 4 x 4 x 3	Meter	2.231,00	-	-	-	0,00%
Main Road Rawa	Meter	1.581,00	304,48	462,96	767,44	48,54%
Collection Road Rawa	Meter	5.208,00	302,19	182,99	485,18	9,32%
Gorong-gorong	Unit		-	2,00	2,00	
Jembatan 2 M	Unit		2,00	2,00	4,00	
Jembatan 4 M	Unit		-	-	-	
Jembatan 5-10 M	Unit		-	-	-	
Jembatan > 10 M	Unit		-	-	-	
Sewa Excavator	HM		421,70	376,00	797,70	
Imas Tumbang	Ha	500,00	-	-	-	0,00%
Puncher	Meter	225,00	-	-	-	0,00%
Compaction	Meter	225,00	-	-	-	0,00%
Gambangan	Meter	9.855,00	-	351,62	351,62	3,57%

Pekerjaan Bulldozer

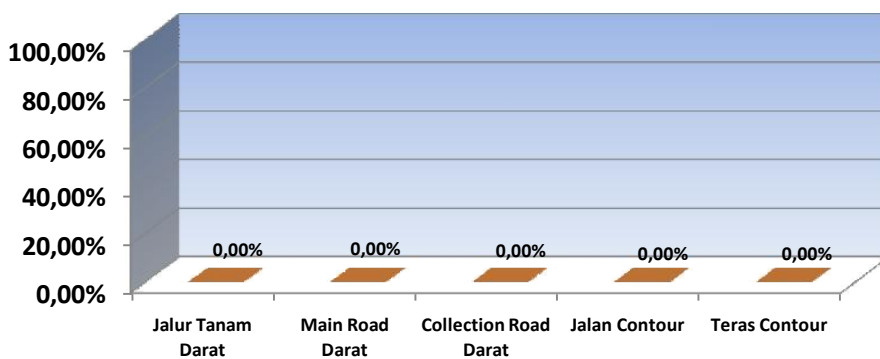

Pekerjaan Excavator

