





PROGRESS REPORT - Kebun Kudung

KONTRAK NO :

1. 30/SPJJ/SRS.-FF/III/2015

Jenis Pekerjaan	Unit	Vol SPK 01 Jan '15 s.d 31 Des '15	Realisasi			%
			AKUMULASI S.D BULAN LALU	BAPP Feb 2015	S.D BAPP Feb 2015	
Bulldozer						
Imas Tumbang	Ha	-	-	-	-	
Stacking Darat	Ha	910,00	33,17	69,25	102,42	11,25%
Acess Road 12 M	Meter	2.002,00	-	-	-	0,00%
Main Road 9 M	Meter	5.400,00	-	-	-	0,00%
Collection Road 7 M	Meter	27.000,00	1.182,00	4.000,00	5.182,00	19,19%
Jalan Contour	Meter	96.300,00	4.103,00	15.037,00	19.140,00	19,88%
Teras Contour	Meter	775.320,00	43.269,00	88.002,00	131.271,00	16,93%
Excavator						
Stacking Rawa	Ha	610,10	21,29	31,20	52,49	8,60%
Gorong-gorong 6 x 3	Unit	910,00	10,00	13,00	23,00	2,53%
Jembatan	Unit	272,00				
Jembatan 4 x 6			13,00	24,00	37,00	13,60%
Jembatan 6 x 6			-	-	-	0,00%

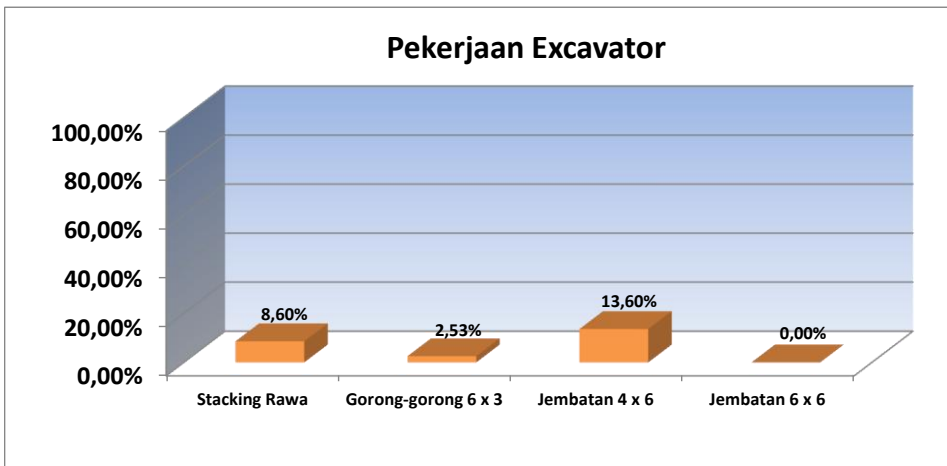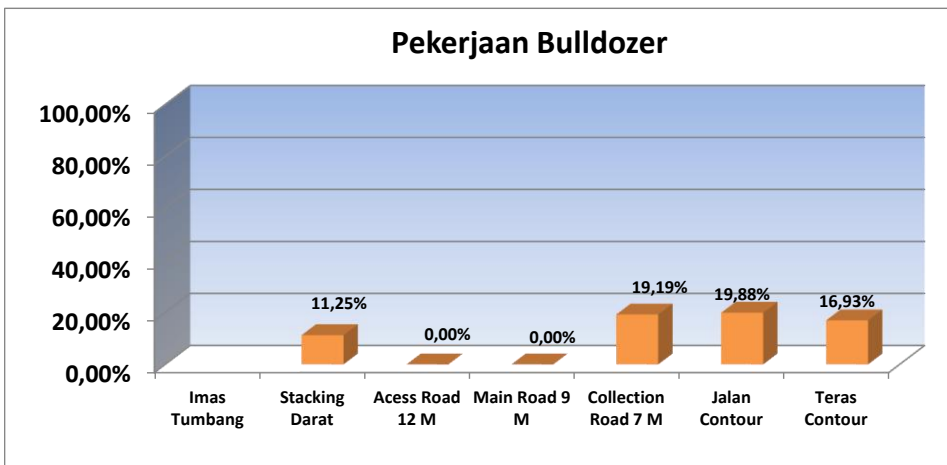




PROGRESS REPORT - Kebun Kudung


Chart & Detail Per Month

Jenis Pekerjaan	Unit	Vol SPK	Realisasi	%
Imas Tumbang	Ha	-	-	0,00%

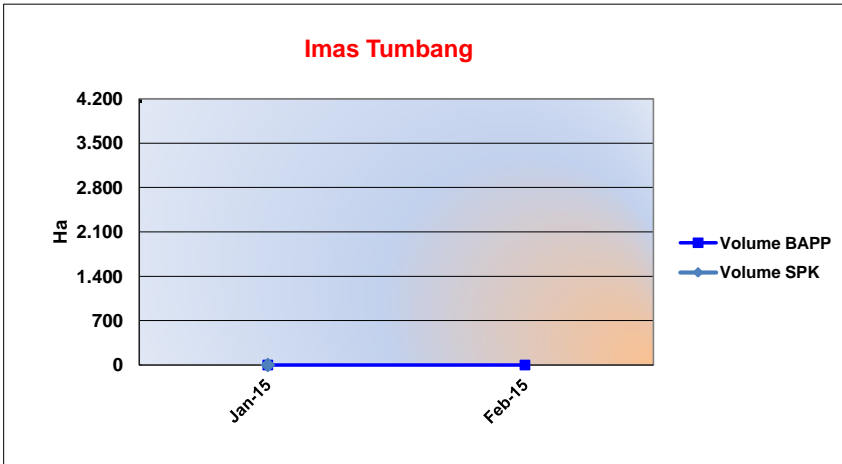


Bulan	Hasil per Bulan	Kumulatif
Jan-15	-	-
Feb-15	-	-
	-	

Jenis Pekerjaan	Unit	Vol SPK	Realisasi	%
Stacking Darat	Ha	910,00	102,42	11,25%

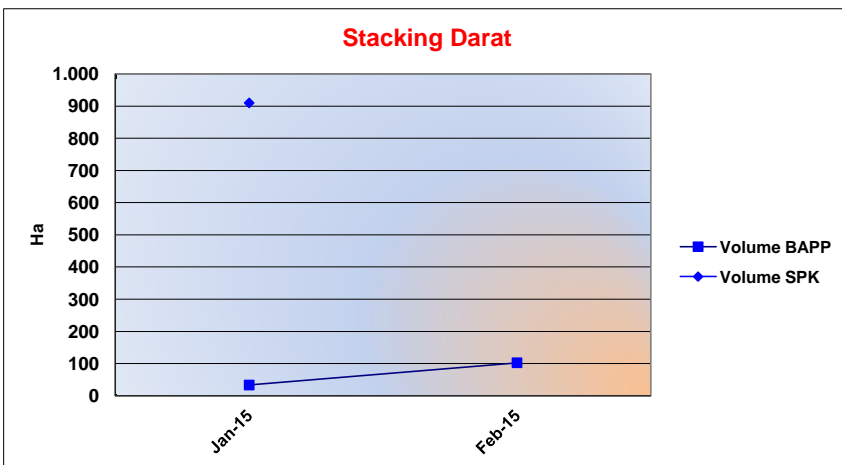

Bulan	Hasil per Bulan	Kumulatif
Jan-15	33,17	33,17
Feb-15	69,25	102,42
	102,42	

Jenis Pekerjaan	Unit	Vol SPK	Realisasi	%
Acess Road 12 M	Meter	2.002,00	-	-

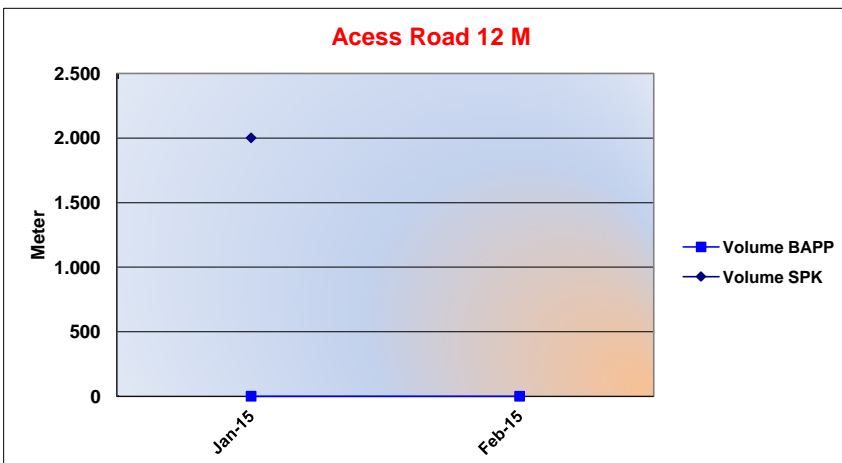


Bulan	Hasil per Bulan	Kumulatif
Jan-15	-	-
Feb-15	-	-
	-	



PROGRESS REPORT - Kebun Kudung


Jenis Pekerjaan	Unit	Vol SPK	Realisasi	%
Main Road 9 M	Meter	5.400,00	-	0,00%

Bulan	Hasil per Bulan	Kumulatif
Jan-15	-	-
Feb-15	-	-
	-	

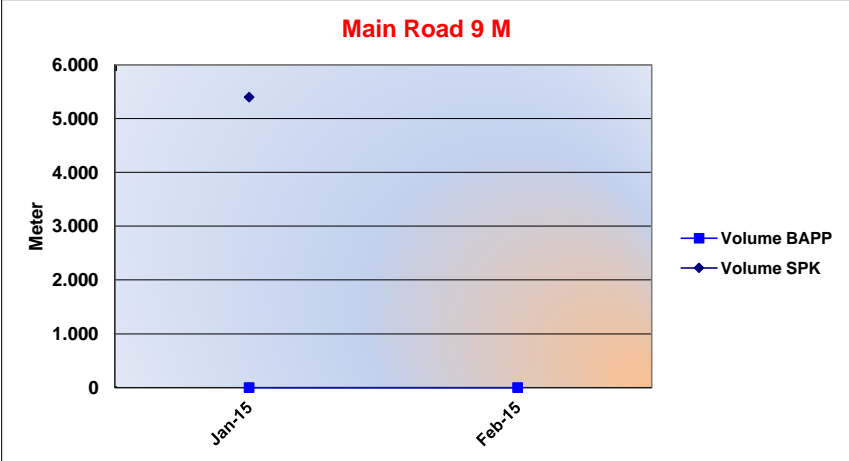


Jenis Pekerjaan	Unit	Vol SPK	Realisasi	%
Collection Road 7 M	Meter	27.000,00	5.182,00	19,19%

Bulan	Hasil per Bulan	Kumulatif
Jan-15	1.182,00	1.182,00
Feb-15	4.000,00	5.182,00
	5.182,00	

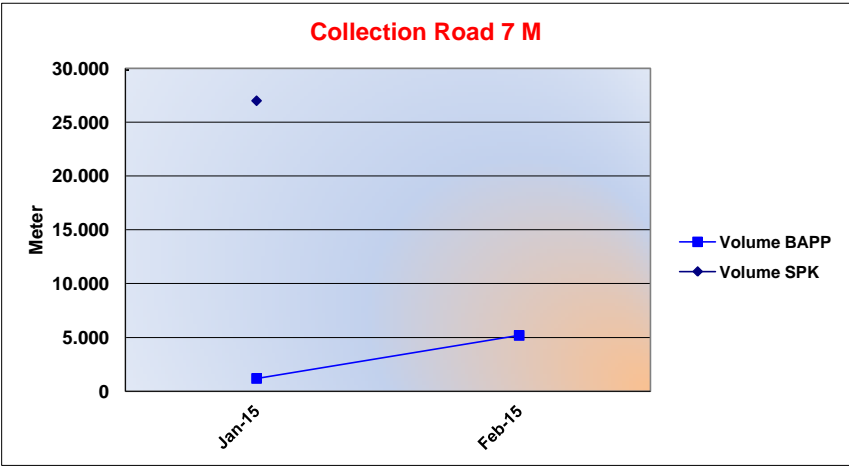

Jenis Pekerjaan	Unit	Vol SPK	Realisasi	%
Jalan Contour	Meter	96.300,00	19.140,00	19,88%

Bulan	Hasil per Bulan	Kumulatif
Jan-15	4.103,00	4.103,00
Feb-15	15.037,00	19.140,00
	19.140,00	

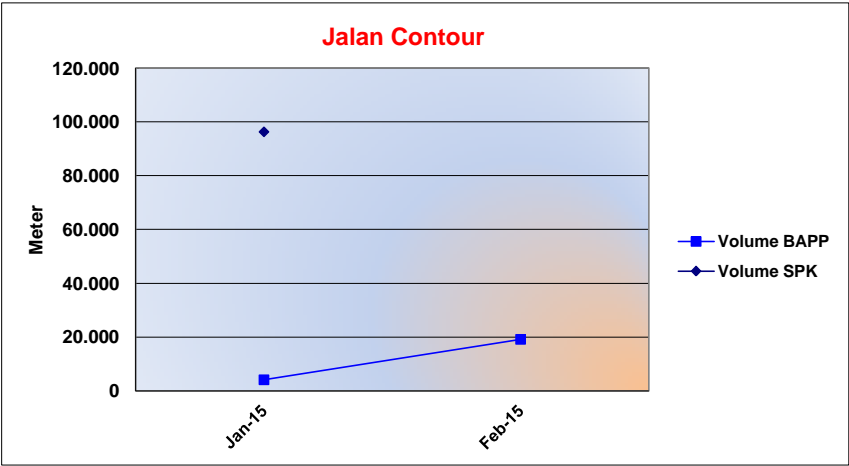




PT. SABHANTARA RAWI SENTOSA

PROGRESS REPORT - Kebun Kudung


Jenis Pekerjaan	Unit	Vol SPK	Realisasi	%
Teras Contour	Meter	775.320,00	131.271,00	16,93%

Bulan	Hasil per Bulan	Kumulatif
Jan-15	43.269,00	43.269,00
Feb-15	88.002,00	131.271,00
	131.271,00	

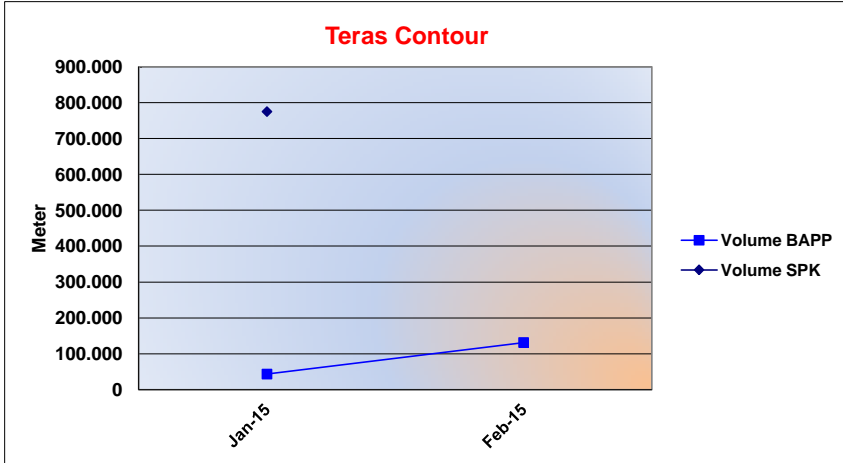


Jenis Pekerjaan	Unit	Vol SPK	Realisasi	%
Sewa Bulldozer	HM	-	-	0,00%

Bulan	Hasil per Bulan	Kumulatif
Jan-15	-	-
Feb-15	-	-
	-	

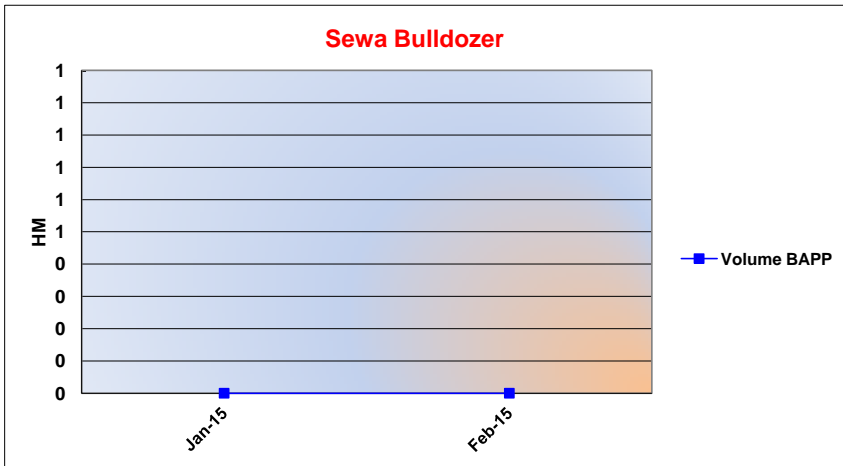

Jenis Pekerjaan	Unit	Vol SPK	Realisasi	%
Stacking Rawa	Ha	610,10	52,49	8,60%

Bulan	Hasil per Bulan	Kumulatif
Jan-15	21,29	21,29
Feb-15	31,20	52,49
	52,49	

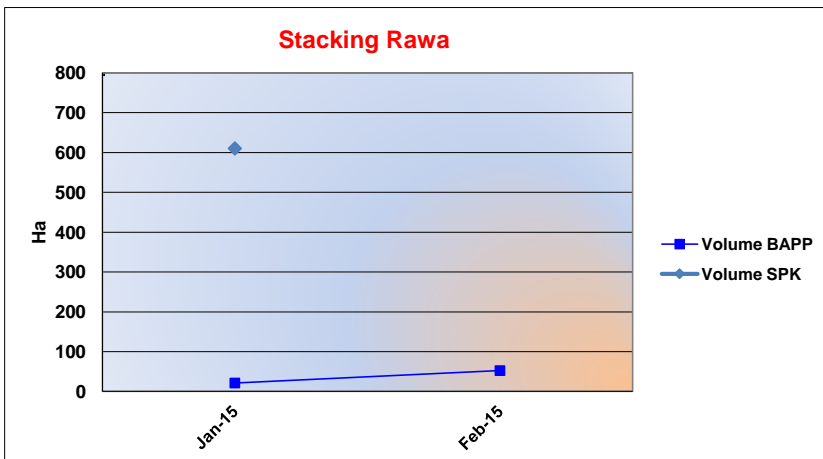




PROGRESS REPORT - Kebun Kudung


Jenis Pekerjaan	Unit	Vol SPK	Realisasi	%
Gorong-gorong 6 x 3	Unit	910,00	23,00	2,53%

Bulan	Hasil per Bulan	Kumulatif
Jan-15	10,00	10,00
Feb-15	13,00	23,00
	23,00	

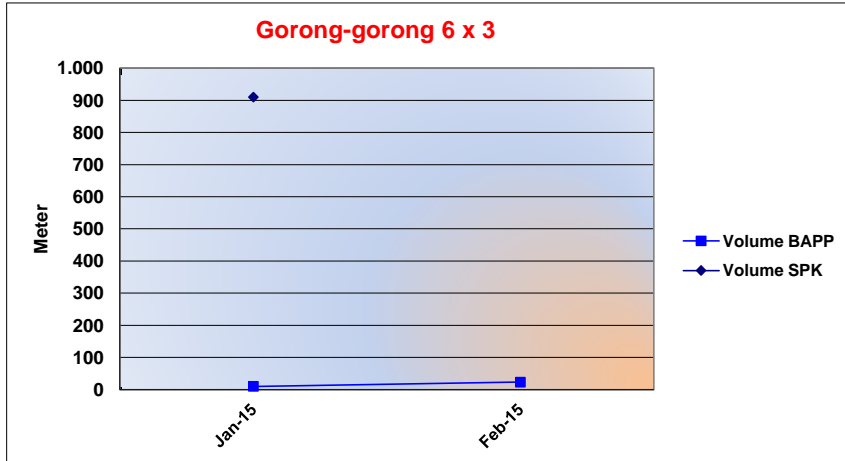

Jenis Pekerjaan	Unit	Vol SPK	Realisasi	%
Jembatan 4 x 6	Unit	272,00	37,00	13,60%

Bulan	Hasil per Bulan	Kumulatif
Jan-15	13,00	13,00
Feb-15	24,00	37,00
	37,00	

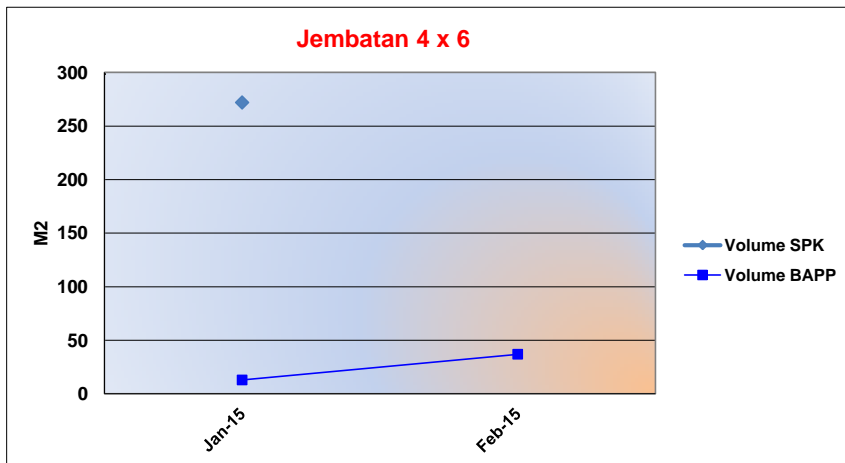

Jenis Pekerjaan	Unit	Vol SPK	Realisasi	%
Jembatan 6 x 6	Unit	272,00	-	0,00%

Bulan	Hasil per Bulan	Kumulatif
Jan-15	-	-
Feb-15	-	-
	-	

