




PROGRESS REPORT - Kebun Sungai Besar

KONTRAK NO :

1. 175/SBSE/JKTO/12/2012-Jalur Tanam, BPRT, & PJLN
2. 175/SBSE/JKTO/12/2012-SWAB

Jenis Pekerjaan	Unit	Vol SPK 1 Jan '13 s.d. 31 Des '13	Realisasi			%
			AKUMULASI S.D BULAN LALU	BAPP Juni 2013	S.D BAPP Juni 2013	
Bulldozer						
Jalur Tanam Darat	Ha	231,00	99,20	51,47	150,67	65,23%
Main Road Darat	Meter	1.408,00	586,20	972,07	1.558,27	110,67%
Collection Road Darat	Meter	4.637,00	2.307,77	178,02	2.485,79	53,61%
Jalan Contour	Meter	10.695,00	-	-	-	0,00%
Teras Contour	Meter	103.695,00	-	-	-	0,00%
Sewa Buldozer	HM		119,80	76,00	195,80	
Excavator						
Jalur Tanam Rawa	Ha	69,00	57,49	25,62	83,11	120,45%
Parit 1 x 1 x 0,75	Meter	26.805,00	505,79	8.418,65	8.924,44	33,29%
Parit 2 x 2 x 1,5	Meter	4.628,00	1.102,68	880,04	1.982,72	42,84%
Parit 4 x 4 x 3	Meter	1.394,00	-	-	-	0,00%
Main Road Rawa	Meter	704,00	1.187,11	195,87	1.382,98	196,45%
Collection Road Rawa	Meter	2.318,00	1.751,17	1.490,56	3.241,73	139,85%
Gorong-gorong	Unit		10,00	7,00	17,00	
Jembatan 2 M	Unit		-	2,00	2,00	
Jembatan 4 M	Unit		-	-	-	
Jembatan 5-10 M	Unit		-	-	-	
Jembatan > 10 M	Unit		-	-	-	
Sewa Excavator	HM		278,80	254,10	532,90	
Imas Tumbang	Ha	300,00	-	-	-	0,00%

Pekerjaan Bulldozer

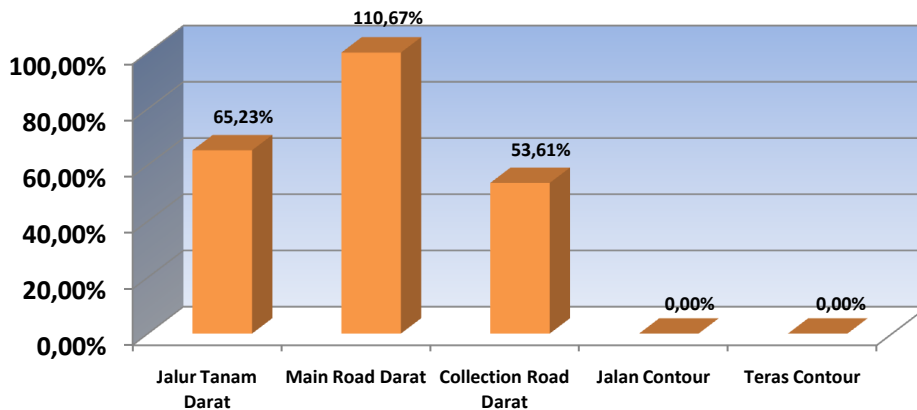

Pekerjaan Excavator

