



PT. NUSANTARA SAWIT PERSADA


PROGRESS REPORT - Rasau Tumbuh

KONTRAK NO :

1. NSP/JKTO/038/10/2013-PL Add I
2. NSP/JKTO/043/10/2013-SWAB

Jenis Pekerjaan	Unit	Vol SPK 01 Nov 2013 s.d 31 Des 2014	Realisasi			%
			AKUMULASI S.D BULAN LALU	BAPP NoV 2014	S.D BAPP Nov 2014	
Bulldozer						
Perun Mekanis Darat	Ha	50,00	-	-	-	0,00%
Main Road Darat	Meter	600,00	-	-	-	0,00%
Collection Road Darat	Meter	2.000,00	-	-	-	0,00%
Sewa Bulldozer PC D 85	HM	-	-	-	-	-
Sewa Bulldozer D 31	HM	-	623,00	-	-	-
Excavator						
Perun Mekanis Rawa	Ha	450,00	91,67	-	91,67	20,37%
Parit 1 x 1 x 0,75	Meter	91.000,00	63.136,00	5.309,00	68.445,00	75,21%
Parit 2 x 2 x 1,5	Meter	16.500,00	4.550,00	122,00	4.672,00	28,32%
Parit 4 x 4 x 3	Meter	5.250,00	4.536,00	-	4.536,00	86,40%
Main Road Rawa	Meter	5.000,00	859,00	-	859,00	17,18%
Collection Road Rawa	Meter	16.000,00	1.749,00	42,00	1.791,00	11,19%
Sewa Excavator PC 200	HM	-	826,00	39,00	865,00	-
Sewa Excavator PC 100	HM	-	-	-	-	-
Sewa Excavator PC 50	HM	-	-	-	-	-
Sewa Grader GD 511	HM	-	-	-	-	-
Sewa Vibro SV 512	HM	-	-	-	-	-
Gorong-gorong 1 M	Unit	-	-	-	-	-
Jembatan Kayu 2 M	Unit	-	-	-	-	-
Jembatan Kayu 4 M	Unit	-	-	-	-	-
Jembatan Kayu 5-10 M	Unit	-	-	-	-	-
Jembatan > 10 M	Unit	-	-	-	-	-

Pekerjaan Bulldozer

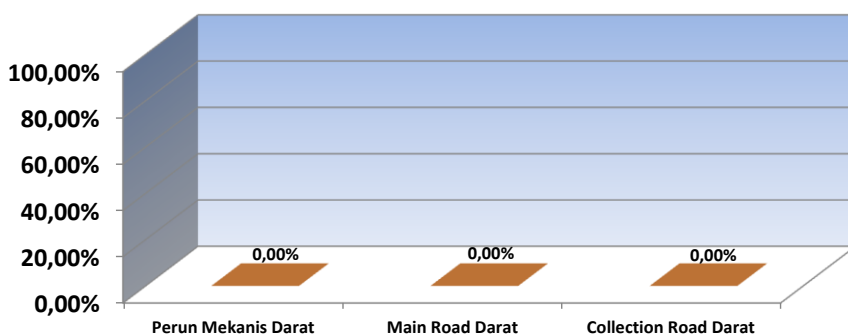

Pekerjaan Excavator

